

Carver Police Station Carver, MA

MONTHLY PROGRESS REPORT
June 2020



Architect:



Jacunski Humes Architects, LLC

General Contractor:



Tower Construction Corp.

Owner's Project Manager:



prepared by:
Daedalus Projects, Inc.

PROJECT
Carver Police Station**PROJECT MANAGER**
Joe Sullivan**CONTRACTOR**
Tower Construction**ON SITE REPRESENTATIVE**
Alyssa Chatani

MONTHLY PROGRESS REPORT - JUNE 2020**GENERAL COMMENTARY OF MONTHLY PROGRESS**

During the month of June, sitework continued with Dig-It laying out the pre-cast concrete curbing by the library and installing it before the library reopened. They also removed two trees by the library. After curbing was completed, they began loam at the curbing and compacting that area. The fence was moved to allow the library employees access to their building for reopening. American Electrical was working on temporary power to the building and installing conduit within the masonry block wall. They tied in their electrical to all door frames at the Sally Port and cell blocks for access control. LaPan checked measurements and laid out plumbing piping at Sally Port. G&H was on site briefly to install control wiring within the masonry block walls as well. John Oliveira & Sons completed sidewalk preparation and pour and removed wood column boxes after the slab on grade pour. Commercial Masonry began their work in the Sally Port and cells, with Briggs inspecting their mortar and grout periodically. Structural Steel was delivered during the first week of June and erection began and was completed the following week with no issues. Empire began erecting their roof trusses using a Lull operator and Barber began exterior cold metal framing. Szewczak Associates visited the site to inspect the steel work and found no issues. Briggs also performed a steel inspection and seismic testing which passed. Fitzmeyer and Tocci also visited the site to do a preliminary walk-through, a kick-off meeting will be planned for August for MEP trades. The Town's Building Inspector visited the site to review progress on site and found no issues.

SCHEDULE COMMENTARY

Tower Construction provided a master schedule with a substantial completion date of March 8, 2021.

DIVISION 03 – CONCRETE**Section 03 30 00 Cast-In Place Concrete**

Week of June 1

- Sidewalk prep took place and began removing wood column boxes from the slab.
- Poured concrete sidewalk by the library and finished it.

Week of June 8

- Installing expansion joints at columns to prepare for concrete infill. Poured 8CY concrete.

Week of June 15

- Removing forms from the sidewalk.

Week of June 22, 29

- Not on site.

DIVISION 04 – MASONRY**Section 04 20 00 Unit Masonry**

Week of June 1

- Not on site.

Week of June 8

- Began layout and installation of CMU block at Sally Port.

Week of June 15

- Continued installation of CMU block at Sally Port.
- Began forming cell blocks.

Week of June 22

- Continued installation of CMU block at Sally Port and continued forming cell blocks.
- Continued installation of CMU block at intermediate block wall Sally Port.

Week of June 29

- Continued installation of CMU block at intermediate block wall Sally Port.

DIVISION 05 – METALS

Section 05 12 00 Structural Steel

Week of June 1

- Began steel erection. Set all 44 columns.
- Continued erecting steel beams. Completed steel erection.
- Began welding and straightening ensuring steel is plumb.

Week of June 8

- Continued welding and straightening ensuring steel is plumb.
- Finalized bolts and welds.

Week of June 15, 22, 29

- Not on site.

DIVISION 07 – ROOFING

Section 074000 Roofing and Siding

Week of June 1

- Began wood blocking on steel beams.

Week of June 8

- Continued wood blocking on steel beams.

Week of June 15

- Completed wood blocking on steel beams.
- Began installing joists at roofing across Sally Port.

Week of June 22

- Began installing trusses on the roof.

Week of June 29

- Continued installing roof trusses.

DIVISION 09 – FINISHES

Section 09 12 00 Gypsum Board Assemblies

Week of June 1, 8

- Not on site.

Week of June 15

- Began exterior cold metal framing.
- Continued cold metal framing and laying down membrane flashing.

Week of June 22

- Continued cold metal framing and laying down membrane flashing.
- Continued laying down membrane flashing at Training Room.

Week of June 29

- Continued cold metal framing and wood bracing.

DIVISION 21 – FIRE SUPPRESSION

Section 21 00 00 Fire Protection

Week of June 1, 8, 15, 22, 29

- Not on site.

DIVISION 22 – PLUMBING

Section 22 00 00 Plumbing

Week of June 1, 8

- Not on site.

Week of June 15

- Reviewed status of work at cells and Sally Port.

Week of June 22

- Checking measurements and laying out piping at Sally Port.

Week of June 29

- Not on site.

DIVISION 26 – ELECTRICAL

Section 26 00 00 Electrical

Week of June 1

- Not on site.

Week of June 8

- Began working on temporary power to the building.

Week of June 15

- Worked on tying in electrical conduit to door frames.
- Continuing conduit installation in the masonry wall.

Week of June 22

- Continued installing conduit in the CMU in Sally Port.

Week of June 29

- Continued installing conduit in the CMU in Sally Port.

DIVISION 31 – EARTHWORK

Section 31 20 00 Earth Moving

Week of June 1

- Laying out concrete curbing.
- Setting curbing on Center Street to about the start of the library.
- Removed 2 trees from the library.

Week of June 8

- Continuing setting curbing at the library.

Week of June 15

- Began filling loam at curbing and compacting.

Week of June 22, 29

- Not on site.

OPM ACTIVITIES

CHA's on-site representative oversaw photo-documenting the daily activities and materials delivered to the site. Daily construction activity reports were uploaded weekly to a share file site. Town of Carver officials were contacted as the need arises and the client was made aware of any project challenges. We are continuing to track and verify the accuracy of certified payroll reports for Carver weekly. Construction Meetings are held weekly via Microsoft Teams conference calls. Notes are kept and distributed by CHA. CHA is tracking the construction progress versus the project schedule and coordinating and integrating the Owner's outside vendors into the contractor's construction schedule.

DESIGNER ACTIVITIES

JHA visited the site to confer, clarify and verify with the contractor and OPM. They provided documentation for agreed-upon changes. They are reviewing submittals and RFIs in a timely manner as they are being sent. CHA and JHA review the contractor's application for payment and adjust with JHA as the installed work dictates. The Team then recommends the adjusted payment sum to the Town's Procurement Officer.

QUALITY CONTROL


CHA and Tower's superintendent inspected the site daily and JHA inspects bi-weekly.

SAFETY COMPLIANCE

Ongoing safety walks are performed. No outstanding issues. Extra precautions are being taken due to COVID-19; a handwashing sink has been installed on site and all meetings are virtual. Tower Construction had a discussion with subcontractors on site on following safety protocol. They are each filling out a daily COVID-19 safety sheet. CHA is filling out daily health certifications as well.






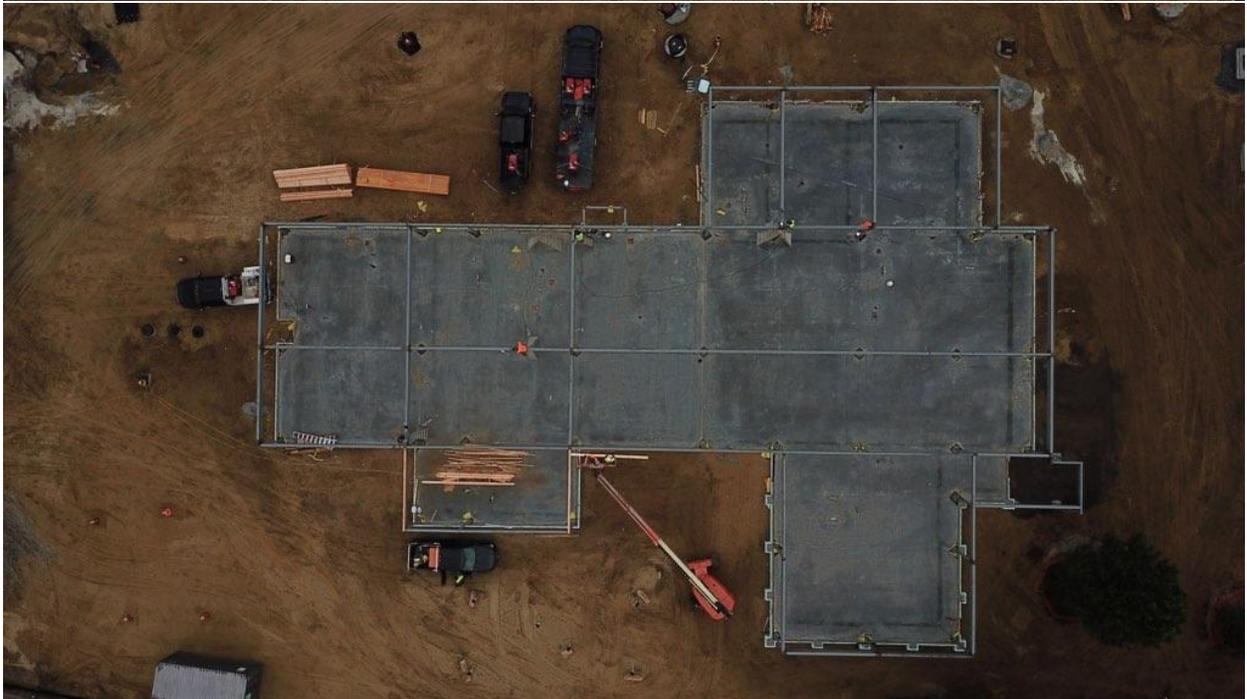





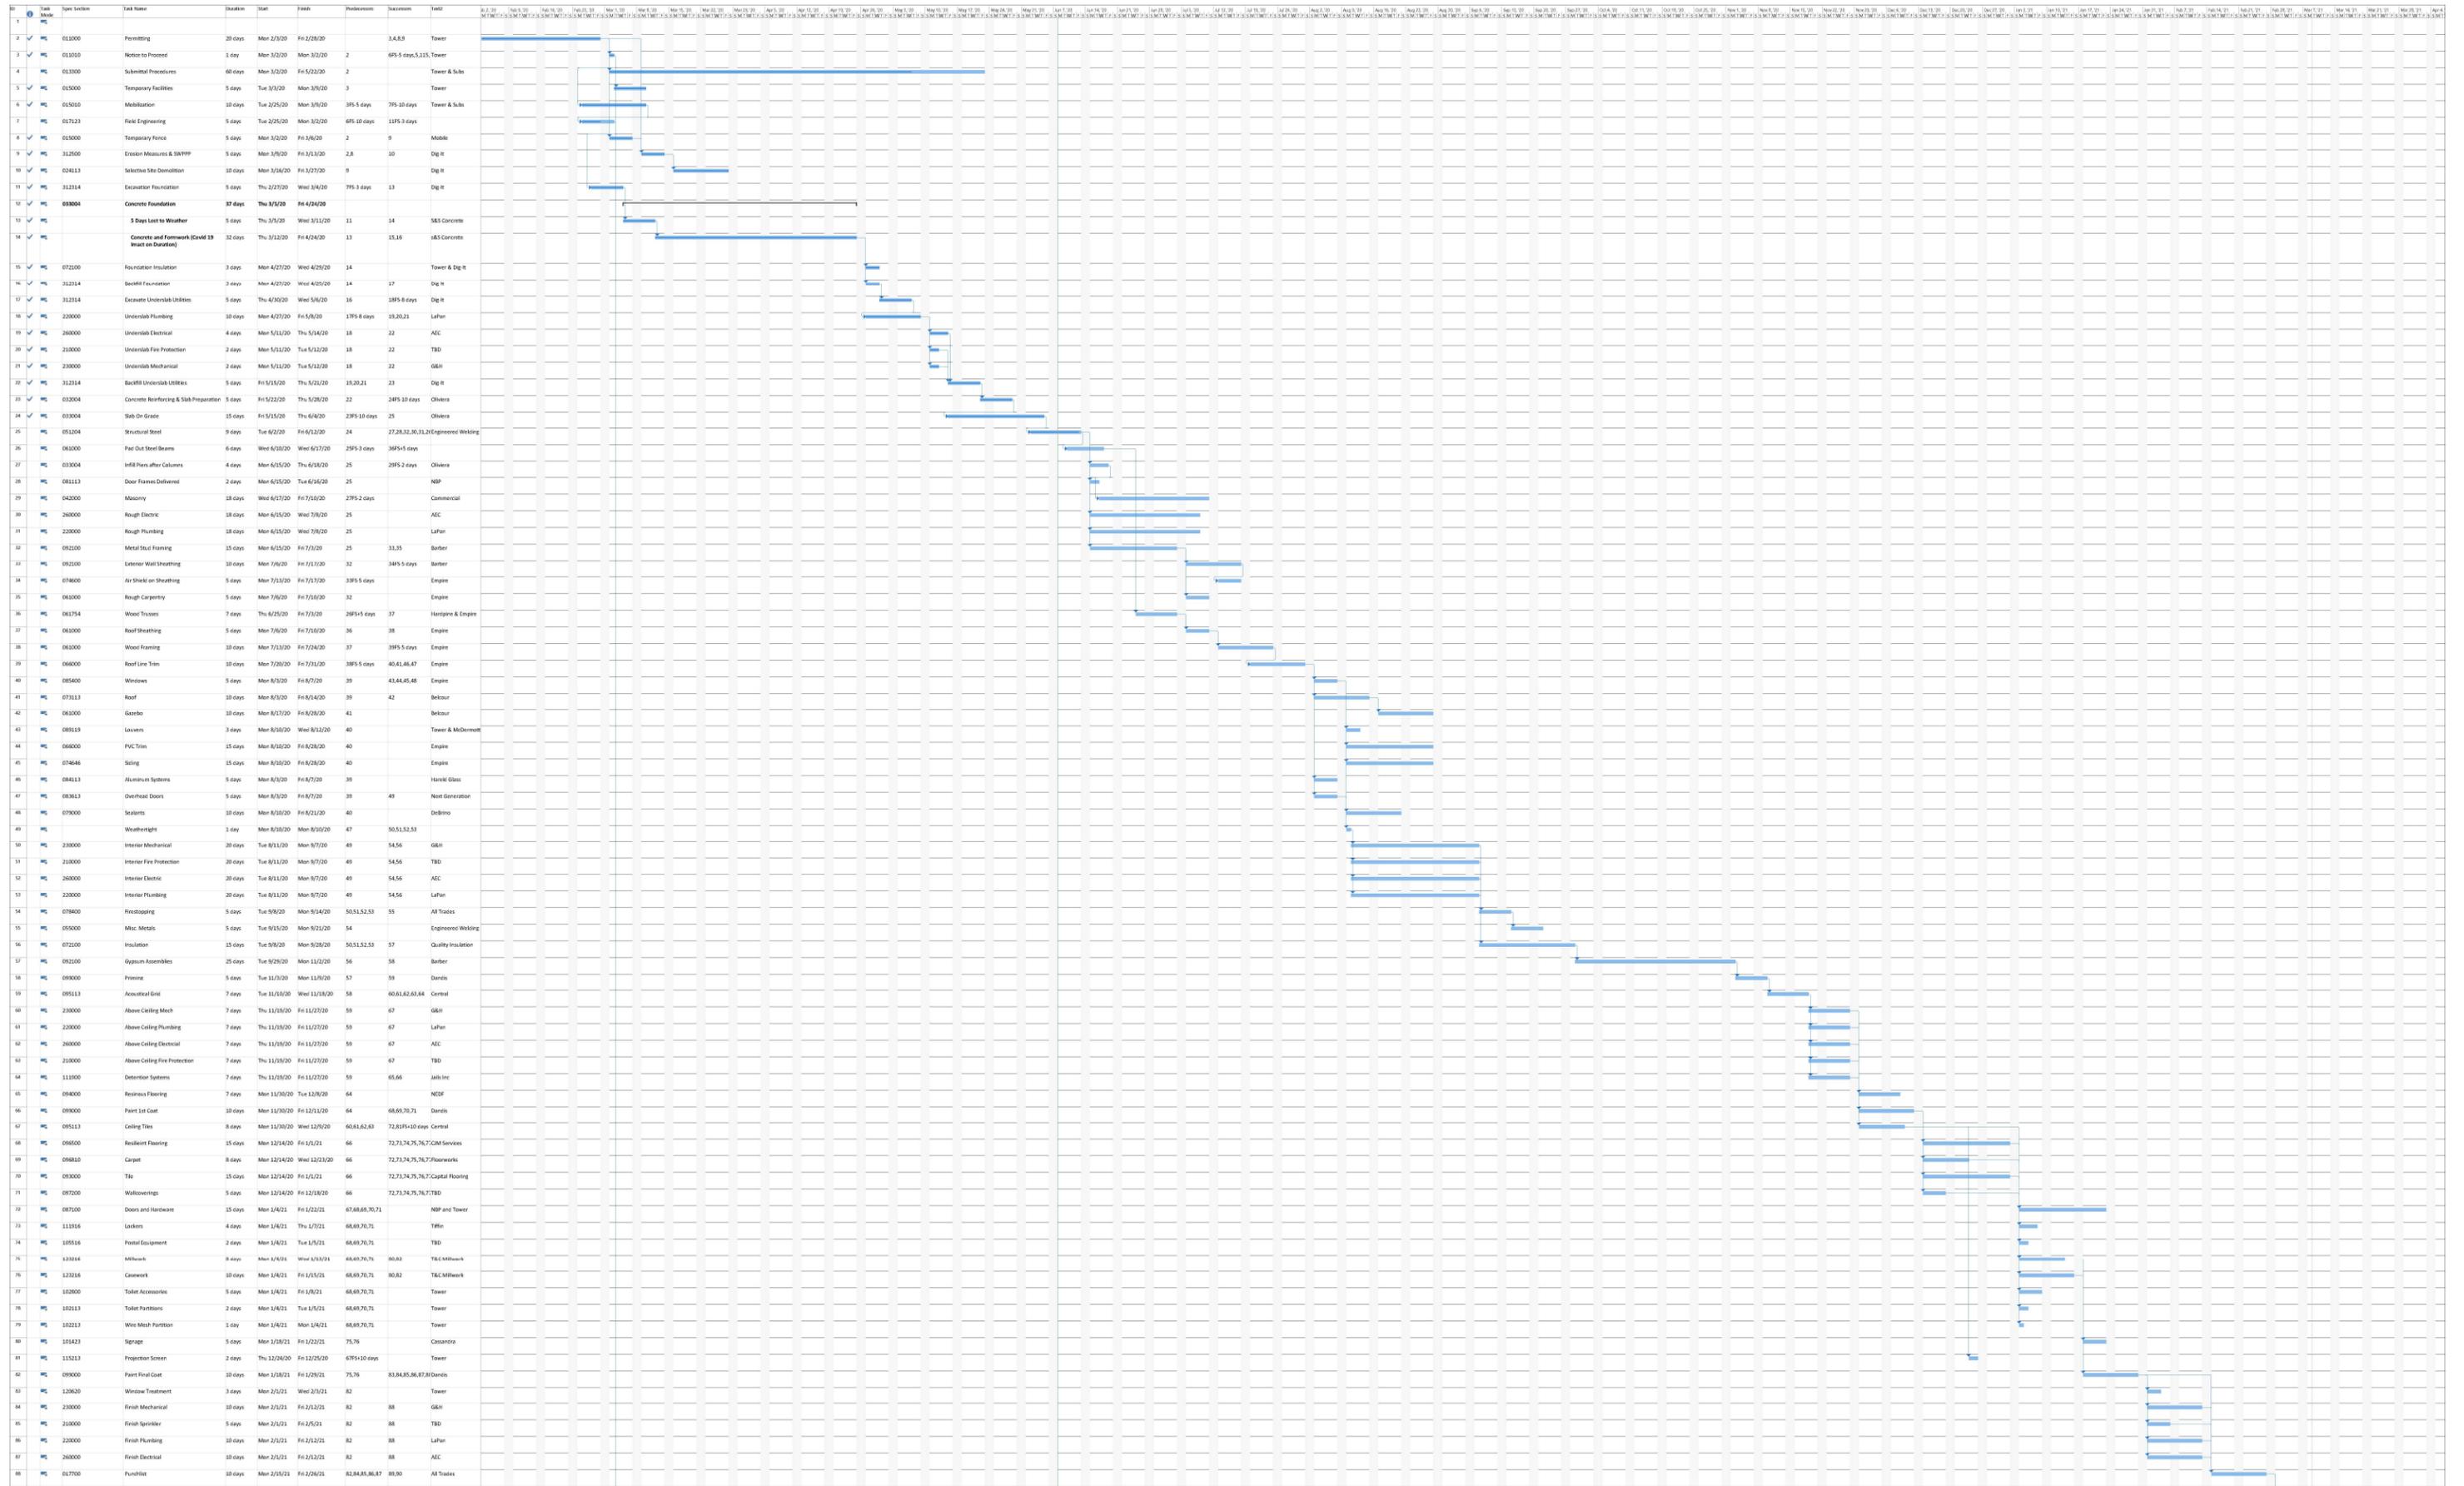

ID	Task Name	Start	End	Duration	Predecessors	Resources	Notes
88	020113 Floor Cleaning	Mon 3/2/21	Fri 3/5/21	3 days		88	
89	010000 Inspections	Mon 3/7/21	Fri 3/5/21	5 days		88, 91	All Trades
91	010000 Occupancy	Mon 3/8/21	Mon 3/8/21	1 day		90	Carver
92	Outbuilding Schedule to be finalized with Execution of ASI Change No. 001 and Approval on alternate 1						
93	230000 Release Tank from Approved Submittal	Wed 5/27/20	Wed 5/27/20	1 day		94	Delta
94	230000 Delivery of Underground Fire Protection Tanks	Thu 5/28/20	Wed 7/15/20	45 days		93, 96, 97, 5 days	Delta
95	330000 Shoring	Thu 7/9/20	Wed 7/15/20	5 days	94, 95	94, 95	Dig - it
96	230000 Installation of Tanks	Thu 7/16/20	Wed 7/22/20	5 days	94	97	Delta
97	230000 Installation of Piping	Thu 7/30/20	Wed 8/5/20	5 days	96	98	Delta
98	330000 Backfilling & Removing Shoring	Thu 8/6/20	Wed 8/12/20	5 days	97	99	Dig - it
99	330000 Drainage	Thu 8/13/20	Wed 8/19/20	5 days	98	100	Dig - it
100	030000 Foundation	Thu 8/20/20	Wed 9/2/20	10 days	99	101	S&S Concrete
101	230000 Underlab Utilities	Thu 8/27/20	Wed 9/6/20	5 days	100	102	LaPar and American
102	030004 Slab On Grade	Thu 9/14/20	Wed 9/23/20	5 days	101	103	Olivera
103	040000 Framing	Thu 9/24/20	Wed 10/21/20	20 days	102	104	Empire
104	040000 Trusses & Sheathing	Thu 10/22/20	Wed 11/4/20	10 days	103	105	Empire
105	070113 Roof	Thu 11/5/20	Thu 11/12/20	5 days	104	106	Rebour
106	070044 Siding & Trim	Fri 11/13/20	Thu 11/26/20	10 days	105	108, 107	Empire
107	230000 Fire Protection & Pump	Fri 11/27/20	Thu 1/14/21	35 days	106	109	Delta
108	230000 - 270000 Rough Trades	Fri 11/27/20	Thu 12/10/20	10 days	106	109	LaPar, G&H, AEC
109	080200 Gypsum Assemblies	Fri 12/11/20	Thu 12/24/20	10 days	108	110	Barber
110	102213 Wire Mesh Partition	Fri 12/25/20	Thu 12/31/20	5 days	109	111	Bode
111	090500 Flooring	Fri 1/7/21	Thu 1/7/21	1 day	110	112	Capital Flooring
112	090000 Painting	Fri 1/8/21	Thu 1/25/21	10 days	111		Dandis
113							
114	312000 Cuts & Fills	Tue 3/2/20	Mon 4/6/20	5 days			Dig - it
115	330000 Site Drainage	Tue 3/3/20	Mon 4/13/20	10 days		116	Dig - it
116	330000 Site Sewer	Tue 4/14/20	Wed 4/15/20	1 day	115	117	Dig - it
117	330000 Site Water	Thu 4/16/20	Wed 4/23/20	5 days	116	118	Dig - it
118	330000 Site Electrical	Thu 4/23/20	Wed 5/20/20	20 days	117	119	Dig - it and AEC
119	312324 Gravel	Thu 5/21/20	Wed 6/3/20	10 days	118	120	Dig - it
120	312116 Binder	Thu 6/4/20	Wed 6/10/20	5 days	119	121, 122, 123, 124, 125, 126, 127, 128, 129, 130	Dig - it
121	312113 Curbing	Thu 8/20/20	Wed 8/26/20	5 days	120, 121, 122, 123, 124, 125, 126, 127, 128, 129, 130	122	Dig - it
122	312113 Ballards	Thu 8/27/20	Wed 9/2/20	5 days	121	123	Dig - it
123	312113 Sidewalks	Thu 9/3/20	Wed 9/23/20	15 days	122	124	Dig - it
124	312113 Fencing	Thu 9/24/20	Wed 10/7/20	10 days	123	125	Dig - it
125	312000 Fine Grading	Thu 10/8/20	Wed 10/28/20	15 days	124	126	Dig - it
126	312113 Loam	Thu 10/29/20	Wed 11/4/20	5 days	125	127	Dig - it
127	312116 Top Course Asphalt	Thu 11/5/20	Wed 11/11/20	5 days	126	128	Dig - it
128	312113 Signage	Thu 11/12/20	Fri 11/13/20	1 day	127	129	Dig - it
129	312113 Striping	Mon 11/16/20	Tue 11/17/20	1 day	128		Dig - it

**Tower Construction
Change Proposal Log**

TOWER CONSTRUCTION CORP.		Open Change Proposals			05.26.20				
		Rejected Change Proposals							
		Approved Change Proposals							
CP#	CO#	Date	Description	CP Amount	Amount Approved	Amount Pending	Amount Not Approved	Subcontractor	Sub Amount
1		03.12.20	Fire Protection File Sub Award	\$ 91,092.02			\$ 91,092.02		
1 Rev 1	1	03.16.20	Fire Protection File Sub Award	\$ 49,369.00	\$ 49,369.00			Delta Mechanical	\$49,369.00
2		04.07.20	ASI No. 001 - Fire Pump Modifications	\$ 284,304.41			\$ 284,304.41		
2 Rev 1	2	04.12.20	ASI No. 001 - Fire Pump Modifications	\$ 273,320.55	\$273,320.55			EWF	\$4,500.00
								Debito Caulking	\$150.00
								Barber Drywall	\$7,500.00
								Bode Material	-\$1,295.00
								Delta Mechanical	\$51,176.47
								American	\$27,072.72
								LaPan	\$3,281.00
								Dig It	\$120,890.40
								Outback Engineering	\$1,950.00
3	2	03.12.20	ASI No. 002 BDA Review	\$ (31,286.05)	\$(31,268.05)			American Electrical	-\$30,657.95
4		03.12.20	ASI No. 003 - Main Circuit Breaker	\$ 3,067.04			\$ 3,067.04	American Electrical	\$2,733.55
4 Rev 1	2	04.07.20	ASI No. 003 - Main Circuit Breaker	\$ -	\$ -			American Electrical	\$0.00
5		04.07.20	Alternate No. 001 - Out Building Construction	\$ 344,000.00			\$ 344,000.00	All trades	
5 Rev 1	3	04.12.20	Alternate No. 001 - Out Building Construction	\$ 344,000.00	\$344,000.00			All Trades	
6		03.18.20	Septic System	\$ 44,269.79			\$ 44,269.79	Dig-It Construction	\$39,935.00
7		04.07.20	Unforeseen Old Foundation Removal	\$ 5,397.34			\$ 5,397.34	Dig-It Construction	\$4,810.46
7 Rev 1	2	04.12.20	Unforeseen Old Foundation Removal	\$ 5,285.68	\$ 5,285.68			Dig-It Construction	\$4,935.28
8		04.07.20	ASI No. 006 - Genset AP	\$ 451.61			\$ 451.61	American Electrical	\$402.50
8 Rev 1	2	04.12.20	ASI No. 006 - Genset AP	\$ 431.08	\$ 431.08			American Electrical	\$402.50
9		04.08.20	Unsuitable Materials	\$ 36,581.71			\$ 36,581.71	Dig-It Construction	\$32,604.02
9 Rev 1		04.12.20	Unsuitable Materials	\$ 36,254.87			\$ 36,254.87	Dig-It Construction	\$33,851.42
9 Rev 2	2	04.14.20	Unsuitable Materials	\$ 19,995.75	\$ 19,995.75			Dig-It Construction	\$18,670.17
10		04.22.20	ASI No. 008 DS-C Fixture	\$ 1,473.34		\$ 1,473.34		American Electrical	\$905.00
								LaPan	\$470.67
11		04.22.20	ASI No. 009 Security Revisions	\$ 1,510.74			\$ 1,510.74	American Electrical	\$1,410.59
11 Rev 1		05.13.20	ASI No. 009 Security Revisions	\$ -		\$ -		American Electrical	\$0.00
12		05.13.20	ASI No. 004 Mechanical Equipment Relocation	\$ -		\$ -		American Electrical	
								G&H Mechanical	
								Dig-It	
13		05.13.20	ASI No. 007 Locker Electrical	\$ 677.88		\$ 677.88		American	\$632.94
14			ASI No. 010 Wall Type Revision					Barber	
15		05.13.20	ASI No. 011 Fire Alarm Revisions	\$ -		\$ -		American Electrical	\$0.00
16		05.13.20	ASI No. 012 Door Leaf Type DL-A	\$ -		\$ -		Hareld Glass	\$0.00
17		05.13.20	Delete UPS From Project Scope	\$ (30,207.60)		\$ (30,207.60)		American Electrical	-\$29,834.67
18		06.16.20	ASI No. 13 Fire Alarm Scope of Work Revisions	\$4,173.60		\$4,173.60		American Electrical	\$3,896.77
			Totals		\$661,134.01	\$ (23,882.78)			
					\$ 6,957,500.00				
	1		CP 1 R1	\$ 49,369.00	\$ 7,006,869.00				
	2		CP 2R1, 3, 4R1, 7R1, 8R1, 9R2	\$ 267,765.01	\$ 7,274,634.01				
	3		CP 5R1	\$ 344,000.00	\$ 7,618,634.01				

Architectural Supplemental Instructions (ASI) Log

New Facility for the Carver Police Department
 3 Center Street, Carver, Massachusetts
 JHA Project #: 1830

		Release Date:	Related CP(s):
ASI #001	Fire Protection and Related Revisions Fire Pump and Cistern relocation to the outbuilding.	January 28, 2020	1, 2, 5
ASI #002	BDA System Deletion of the BDA System from the scope of work.	February 3, 2020	3
ASI #003	Main Circuit Breaker Revisions to the main circuit breaker requirements.	February 24, 2020	4
ASI #004	Mechanical Location Revisions to the locations of the exterior mechanical units ACCU-1, ACCU-2, SCU-1, and SCU-2 and associated landscaping revisions.	March 20, 2020	12
ASI #005	Footing Subbase Deletion of the sub-base requirements below footings due to geotech on-site review.	March 13, 2020	
ASI #006	Genset AP Notational scope clarification to the Genset AP riser.	March 16, 2020	8
ASI #007	Locker Electrical Revision to incorporate GFCI into the locker circuit after submittal indicated it not inherent to the pre-manufactured locker devices.	March 18, 2020	13
ASI #008	Plumbing Fixture DS-C Revisions to the DS-C fixture type and requirements.	April 15, 2020	10
ASI #009	Security Revisions Revisions to the security scope of drawing E-4.0.	April 15, 2020	11
ASI #010	Wall Type Revision Revisions to select wall types of drawing A-11.1.	April 15, 2020	14
ASI #011	Fire Alarm Revisions Owner request to swap FACP & FAA locations and remove key box at outbuilding storage.	April 23, 2020	15
ASI #012	Door Leaf Type DL-A Revision to the height of the bottom rail of door leaf type "DL-A"	April 28, 2020	16
ASI #013	Fire Alarm Relocation of FACP and addition of one (1) FAA per owner's request.	May 11, 2020	18
ASI #013-R1	Fire Alarm Supersedes ASI #013 for relocation of FACP per owner's request.	June 22, 2020	
ASI #014	Aluminum Storefront Colors Clarification of storefront colors.	June 15, 2020	
ASI #015	Electrical Additions Owner request to add a phone jack to the day room and television box to lobby.	July 1, 2020	
ASI #016	Library Curbing Replacements Owner request to replace existing bit. conc. berm curbing at library with precast conc.	July 1, 2020	

SHOP DRAWING LOG

PROJECT: New Facility for the Carver Police Department, 3 Center Street, Carver, Massachusetts							STATE PROJECT No.:				
G.C.: Tower Construction Corporation							JHA PROJECT No.: 1830				
TEAM: JH Architects (JHA); Garcia-Galuska-DeSousa (GGD); Linden Landscape Architects (LLA); Szewczak Associates (SA); Paul Hawley Associates (PHA); CAMA (CAMA); Building Engineering Resources (BER)							G.C. PROJECT No.: 2252				
JHA SHOP DRAWING NUMBER	G.C. SHOP DRAWING NUMBER	DESCRIPTION <div style="font-size: small; margin-top: 5px;"> = Reviewed & Returned = Under JHA Review = Under Consultant Review = Under Owner Review = Awaiting G.C. Response </div>	DATE REC'D	DATE SENT	DATE REC'D	DATE SENT	DATE REC'D	DATE RTN'D	REVIEWER	ACTION / REMARK	COMMENTS
			- From - G.C.	- To - Owner	- From - Owner	- To - Consult	- From - Consult	- To - G.C.			
DIVISION 0 - OWNER SUBMISSIONS											
DIVISION 1 - GENERAL REQUIREMENTS											
010000-001-1	-	Underslab Coordination Drawings	04/01/20	-	-	04/01/20	04/15/20	04/15/20	BER	AN	
011000-001-1	011000-01s	Carver Site Access Plan	01/29/20	01/29/20	02/20/20	01/29/20	01/29/20	02/20/20	ToC/LLA	AN	
011000-002-1	011000-02	Carver Police Schedule	02/19/20	-	-	-	-	02/27/20	JHA	A	
011000-003-1	011000-03	Above Slab Coordination Drawings	05/06/20	-	-	05/06/20	05/28/20	05/28/20	BER	A	
DIVISION 2 - EXISTING CONDITIONS											
DIVISION 3 - CONCRETE											
032004-001-1	032004-01	Rebar Shop Drawing	01/15/20	-	-	01/15/20	-	-	SA/LLA	-	<i>Incorporated into 032004-001-2</i>
032004-001-2	032004-02	Rebar Shop Drawing	01/22/20	-	-	01/28/20	02/05/20	02/05/20	SA/LLA	AC/RR	
032004-001-2	032004-02	Rebar Shop Drawing	-	-	-	-	-	04/03/20	SA/LLA	AC	<i>Updated marks dated 2020-04-03</i>
032004-001-3	032004-01 Rev2	Rebar Shop Drawing	03/03/20	-	-	04/03/20	04/03/20	04/03/20	SA	R	<i>Re-design voided via negotiations</i>
033004-001-1	033004-02s	Concrete Slab on Grade	02/19/20	-	-	02/19/20	02/24/20	02/24/20	SA	AC	
033004-002-1	033004-4s	Footings + Foundation Walls	02/19/20	-	-	02/19/20	02/24/20	02/24/20	SA	AC	
033004-002-2	033004-4s Rev 1	Footings + Foundation Walls	03/06/20	-	-	03/06/20	-	-	SA	-	<i>Received For Record Only</i>
033004-002-3	033004-4s Rev 2	Footings + Foundation Walls	03/10/20	-	-	03/10/20	03/19/20	03/19/20	SA	AC	
033004-003-1	033004-06s	Expansion Joint	03/05/20	-	-	03/06/20	03/13/20	03/13/20	SA	A	
033004-004-1	033004-07s	Non-Shrink Grout	03/05/20	-	-	03/06/20	03/13/20	03/13/20	SA	A	
033004-005-1	033004-08s	Stego Wrap Vapor Barrier 15 Mil	03/05/20	-	-	03/06/20	03/13/20	03/13/20	SA	A	
033004-006-1	033004-09s	Concrete Slab on Grade Layout	05/06/20	-	-	05/06/20	05/14/20	05/14/20	SA/JHA	AC	

SHOP DRAWING LOG

PROJECT: New Facility for the Carver Police Department, 3 Center Street, Carver, Massachusetts								STATE PROJECT No.:			
G.C.: Tower Construction Corporation								JHA PROJECT No.: 1830			
TEAM: JH Architects (JHA); Garcia-Galuska-DeSousa (GGD); Linden Landscape Architects (LLA); Szewczak Associates (SA); Paul Hawley Associates (PHA); CAMA (CAMA); Building Engineering Resources (BER)								G.C. PROJECT No.: 2252			
JHA SHOP DRAWING NUMBER	G.C. SHOP DRAWING NUMBER	DESCRIPTION <div style="font-size: small; margin-top: 5px;"> = Reviewed & Returned = Under JHA Review = Under Consultant Review = Under Owner Review = Awaiting G.C. Response </div>	DATE REC'D	DATE SENT	DATE REC'D	DATE SENT	DATE REC'D	DATE RTN'D	REVIEWER	ACTION / REMARK	COMMENTS
			- From - G.C.	- To - Owner	- From - Owner	- To - Consult	- From - Consult	- To - G.C.			
DIVISION 4 - MASONRY											
042000-001-1	042000-01s	Unit Masonry	01/22/20	-	-	01/22/20	01/29/20	02/05/20	JHA	A	
042000-002-1	042000-02s	Masonry Reinforcement Shop Drawings	01/22/20	-	-	01/22/20	01/29/20	01/30/20	SA/JHA	AC	
042000-003-1	042000-03s	Precast Concrete Products	02/14/20	-	-	-	-	02/14/20	JHA	AC	
042000-004-1	042000-04s	Precast Concrete Profile	02/18/20	-	-	-	-	02/19/20	JHA	AC	
042000-005-1	042000-05s	Precast Concrete Color Samples	03/04/20	-	-	-	-	03/16/20	JHA	AC	Samples Received 3/12/20
DIVISION 5 - METALS											
051204-001-1	051204-01	Anchor Bolts Setting Plan & Details	01/15/20	-	-	01/15/20	01/29/20	01/29/20	SA	AC	
051204-002-1	051204-02s	Structural Steel Drawings	02/13/20	-	-	02/13/20	02/27/20	02/27/20	SA	RR	
051204-002-2	051204-02 Rev 1	Structural Steel Drawings	03/21/20	-	-	03/21/20	04/02/20	04/02/20	SA	A/AC	
055133-001-1	051204-03s	Ships Ladder	05/27/20	-	-	-	-	06/10/20	JHA	AC	
DIVISION 6 - WOOD & PLASTICS											
061000-001-1	061000-01s	Lumber	03/26/20	-	-	03/31/20	04/03/20	04/03/20	SA/JHA	AC/RR	
061000-001-2	061000-01s Rev 1	Lumber	04/08/20	-	-	-	-	04/08/20	JHA	-	Not accepted for review
061000-002-1	061000-01s	LVLs	04/10/20	-	-	04/10/20	04/20/20	04/21/20	SA	AC	
061000-003-1	061000-02s	Air Infiltration Barrier and Tape	04/10/20	-	-	-	-	04/15/20	SA/JHA	A	
061000-004-1	061000-03s	Construction Subfloor Adhesive	04/10/20	-	-	04/10/20	-	04/21/20	JHA	AC	
061000-005-1	061000-04s	Exterior Sheathing	04/10/20	-	-	04/10/20	04/20/20	04/21/20	SA	AC	
061000-006-1	061000-05s	Hunter Panels	04/10/20	-	-	-	-	04/15/20	SA/JHA	A	
061000-007-1	061000-06s	Self-Adhered Flashing	04/10/20	-	-	-	-	04/15/20	SA/JHA	R	
061000-007-2	061000-06s Rev 1	Self-Adhered Flashing	04/21/20	-	-	-	-	04/21/20	JHA	A	
061000-008-1	061000-07s	TJI	04/10/20	-	-	04/10/20	04/20/20	04/21/20	SA	AC/R	
061000-009-1	06100-08s	Framing Lumber Materials	04/10/20	-	-	04/10/20	04/20/20	04/21/20	SA	AC	
061754-001-1	061754-01s	Truss Shop Drawing	01/27/20	-	-	01/28/20	02/11/20	02/11/20	SA	RR	
061754-001-2	061754-01s Rev 1	Trusses	03/10/20	-	-	03/10/20	03/24/20	03/24/20	SA	AC	
061754-001-3	061754-01s Rev 2	Truss Seals	05/18/20	-	-	05/18/20	05/28/20	05/28/20	SA	AC	
061754-002-1	061754-02s	Outbuilding Truss SD	04/29/20	-	-	04/29/20	05/08/20	05/12/20	SA	AC	
064000-001-1	06400-01s	Fiberglass Column	06/10/20	-	-	-	-	06/12/20	JHA	A	

SHOP DRAWING LOG

PROJECT: New Facility for the Carver Police Department, 3 Center Street, Carver, Massachusetts							STATE PROJECT No.:				
G.C.: Tower Construction Corporation							JHA PROJECT No.: 1830				
TEAM: JH Architects (JHA); Garcia-Galuska-DeSousa (GGD); Linden Landscape Architects (LLA); Szewczak Associates (SA); Paul Hawley Associates (PHA); CAMA (CAMA); Building Engineering Resources (BER)							G.C. PROJECT No.: 2252				
JHA SHOP DRAWING NUMBER	G.C. SHOP DRAWING NUMBER	DESCRIPTION	DATE REC'D	DATE SENT	DATE REC'D	DATE SENT	DATE REC'D	DATE RTN'D	REVIEWER	ACTION / REMARK	COMMENTS
			- From - G.C.	- To - Owner	- From - Owner	- To - Consult	- From - Consult	- To - G.C.			
064400-001-1	064400-01s	Moldings and Decorative Millwork	05/06/20	-	-	-	-	05/15/20	JHA	AC	
066000-001-1	06600-01s	PVC Trim	05/06/20	-	-	-	-	05/13/20	JHA	A	
DIVISION 7 - THERMAL & MOISTURE PROTECTION											
072100-001-1	033004-05s	Dow Insulation	03/05/20	-	-	-	-	03/15/20	JHA	A	
072100-002-1	033004-09s	Tuff II Coating	03/05/20	-	-	-	-	03/15/20	JHA	A	
073113-001-1	073113s	Asphalt Shingles	02/18/20	-	-	-	-	02/20/20	JHA	AC/RR/R	
073113-002-1	073113-25s	Color Samples & Color Chart	03/04/20	-	-	-	-	03/16/20	JHA	AC	Samples Received 3/12/20
074600-001-1	074600-01s	NuCedar	04/10/20	-	-	-	-	04/16/20	JHA	AC/RR	
074600-002-1	074600-02	Siding Color Samples	05/07/20	05/20/20	05/20/20	-	-	05/27/20	JHA	AC	Samples Received 5/15/20
074646-001-1	074646-01s	Fiber Cement Siding	04/10/20	-	-	-	-	04/16/20	JHA	AC	
075323-001-1	075323-01s	Membrane Roofing	03/04/20	-	-	-	-	03/15/20	JHA	A/R	Only Flat Insulation Not Approved
075323-002-1	075323-02s	Metal Roofing	06/23/20	-	-	-	-	07/01/20	JHA	AC	
079200-001-1	079200-01s	Elastomeric Joint Sealant	01/30/20	-	-	-	-	02/10/20	JHA	R	
079200-002-1	079200-02s	Sealant Color Chart	01/30/20	-	-	-	-	02/10/20	JHA	RR	
079200-003-1	079200-03s	Non-Sag Urethane Sealant	01/30/20	-	-	-	-	02/10/20	JHA	A	
079200-004-1	079200-04s	Acrylic-Emulsion Sealant and Color Chart	01/30/20	-	-	-	-	02/03/20	JHA	AC	
079200-005-1	079200-05s	Security Sealant	01/30/20	-	-	-	-	01/30/20	JHA	R	
079200-005-2	079200-05s Rev1	Security Sealant	02/07/20	-	-	-	-	02/07/20	JHA	A	
079200-006-1	079200-06s	Resilient Silicone Sealant	01/30/20	-	-	-	-	02/03/20	JHA	R	
DIVISION 8 - OPENINGS											
081113-001-1	081113-01	Door and Frame Schedule	04/13/20	-	-	-	-	04/16/20	JHA	AC	
081113-001-2	081113-03s Rev1	Door and Frame Schedule	05/01/20	-	-	-	-	-	JHA		Contingent on Frames Resubmission
081113-002-1	081113-02	Door Frames	04/13/20	-	-	-	-	04/16/20	JHA	RR	
081113-002-2	081113-03s Rev1	Doors Frames	05/01/20	-	-	-	-	05/13/20	JHA	R	
081113-003-1	081113-03	Steel Doors	04/13/20	-	-	-	-	04/16/20	JHA	AC/RR/R	
081113-003-2	081113-03s Rev1	Steel Doors	05/01/20	-	-	-	-	05/13/20	JHA	A/R	
081400-001-1	081400-01	Wood Doors	04/13/20	-	-	-	-	04/16/20	JHA	AC	
083326-001-1	083616-03s	Shop Drawing and Product Data for Door 125C	04/10/20	-	-	-	-	04/16/20	JHA	AC	
083613-001-1	083613-01s	Shop Drawings for Doors 125B & 118B	03/06/20	-	-	-	-	03/16/20	JHA	AC	

SHOP DRAWING LOG

PROJECT: New Facility for the Carver Police Department, 3 Center Street, Carver, Massachusetts								STATE PROJECT No.:			
G.C.: Tower Construction Corporation								JHA PROJECT No.: 1830			
TEAM: JH Architects (JHA); Garcia-Galuska-DeSousa (GGD); Linden Landscape Architects (LLA); Szewczak Associates (SA); Paul Hawley Associates (PHA); CAMA (CAMA); Building Engineering Resources (BER)								G.C. PROJECT No.: 2252			
JHA SHOP DRAWING NUMBER	G.C. SHOP DRAWING NUMBER	DESCRIPTION <div style="font-size: small; margin-top: 5px;"> = Reviewed & Returned = Under JHA Review = Under Consultant Review = Under Owner Review = Awaiting G.C. Response </div>	DATE REC'D	DATE SENT	DATE REC'D	DATE SENT	DATE REC'D	DATE RTN'D	REVIEWER	ACTION / REMARK	COMMENTS
			- From - G.C.	- To - Owner	- From - Owner	- To - Consult	- From - Consult	- To - G.C.			
083613-002-1	083616-02s	Product Data Overhead Doors 112B and 118B	04/10/20	-	-	-	-	04/16/20	JHA	AC	
083613-003-1	083616-04s	Motors	04/10/20	-	-	-	-	04/16/20	JHA	RR	
084113-001-1	088000-01s	Door & Frame Product Data	05/18/20	-	-	-	-	05/27/20	JHA	AC	
084113-002-1	084113-01s	Aluminum Entrances & Storefronts	05/28/20	-	-	-	-	06/12/20	JHA	AC/RR	
084113-003-1	084113-02s	Color Samples	06/04/20	-	-	-	-	06/15/20	JHA	AC	Cover sheet & Scan only
085400-001-1	085400-01s	Fiberglass Windows	03/06/20	-	-	-	-	03/15/20	JHA	AC	
085400-002-1	085400-01s	Fiberglass Windows Shop Drawings	04/01/20	-	-	-	-	04/02/20	JHA	AC	
087100-001-1	087100-01	Door Hardware Schedule	04/13/20	-	-	04/13/20	04/14/20	04/16/20	PHA/JHA	AN/RRfR	
087100-001-2	087100-01sRev1	Door Hardware Schedule	04/29/20	-	-	04/29/20	05/04/20	05/04/20	PHA/JHA	A	
087100-002-1	087100-02	Door Hardware	04/13/20	-	-	04/13/20	04/14/20	04/16/20	PHA/JHA	AN/RRfR	
087100-002-2	087100-02s	Door Hardware PD	04/29/20	-	-	04/29/20	05/04/20	05/04/20	PHA/JHA	A	
087100-003-1	088000-02s	Hardware PD	05/18/20	-	-	05/18/20	05/26/20	05/27/20	PHA	R	
087113-001-1	087113-01s	Automatic Doors	02/12/20	-	-	-	-	02/14/20	JHA	AC	
088000-001-1	088000-03s	Float Glass PD	05/18/20	-	-	-	-	05/27/20	JHA	AC	
089119-001-1	089119-01s	Louver SD & Color Chart	02/24/20	-	-	-	-	02/27/20	JHA	AC	
089119-002-1	089119-02s	Louver Color Samples	04/21/20	-	-	-	-	05/27/20	JHA	R	Siding Samples Rec'd 5/15
089119-002-2	089119-02s Rev1	Louver Color Samples	06/03/20	-	-	-	-	06/15/20	JHA	AC	Cover sheet & Scan only
DIVISION 9 - FINISHES											
092100-001-1	092100-01s	Gypsum Board	03/30/20	-	-	-	-	03/31/20	JHA	AC/R	Only Impact Gypsum was Rejected
092100-002-1	092100-02s	National Gypsum	04/04/20	-	-	-	-	04/06/20	JHA	R	
092100-003-1	092100-03s	Cold-Formed Steel Exterior Framing	04/20/20	-	-	04/20/20	04/28/20	04/29/20	SA/JHA	RR	
092100-003-2	092100-03s rev1	Cold-Formed Steel Exterior Framing	06/05/20	-	-	06/05/20	06/09/20	06/10/20	SA/JHA	AC	
093000-001-1	093000-01s	Tile Products	06/22/20	-	-	06/22/20			CAMA		
093000-002-1	093000-02s	Grout & Sealant	06/22/20	-	-	06/22/20			CAMA		
093000-003-1	093000-03s	Setting Materials	06/22/20	-	-	06/22/20			CAMA		
093000-004-1	093000-04s	Stainless Steel Metal Trim	06/22/20	-	-	06/22/20			CAMA		
093000-005-1	093000-05s	CWT-04	06/22/20	-	-	06/22/20			CAMA		
094000-001-1	094000-01s	Industrial Floor System	02/07/20	-	-	-	-	02/07/20	JHA	R	AC Only if Samples are Approved
094000-002-1	094000-02s	Industrial Floor Color Samples	03/04/20	-	-	-	-	03/30/20	JHA	A	Samples Received 3/12/20

SHOP DRAWING LOG

PROJECT: New Facility for the Carver Police Department, 3 Center Street, Carver, Massachusetts							STATE PROJECT No.:				
G.C.: Tower Construction Corporation							JHA PROJECT No.: 1830				
TEAM: JH Architects (JHA); Garcia-Galuska-DeSousa (GGD); Linden Landscape Architects (LLA); Szewczak Associates (SA); Paul Hawley Associates (PHA); CAMA (CAMA); Building Engineering Resources (BER)							G.C. PROJECT No.: 2252				
JHA SHOP DRAWING NUMBER	G.C. SHOP DRAWING NUMBER	DESCRIPTION	DATE REC'D - From - G.C.	DATE SENT - To - Owner	DATE REC'D - From - Owner	DATE SENT - To - Consult	DATE REC'D - From - Consult	DATE RTN'D - To - G.C.	REVIEWER	ACTION / REMARK	COMMENTS
095113-001-1	095113-01 095113-02 095113-03 095113-04 095113-05	Acoustical Ceiling Panels	01/02/20	-	-	-	-	01/07/20	JHA	AC	
095113-002-1	095113-06	Acoustical Ceiling Samples	01/13/20	-	-	-	-	03/15/20	JHA	A/R	<i>Samples Received 3/12/20</i>
096500-001-1	096500-01s	Solid Vinyl Tile (SVT-01)(SVT-02)(SVT-03)	01/30/20	-	-	01/30/20	02/06/20	02/07/20	CAMA	A	
096500-002-1	096500-02s	Luxury Vinyl Tile (LVT-01)	01/30/20	-	-	01/30/20	02/06/20	02/07/20	CAMA	AC	
096500-003-1	096500-03s	Rubber Anti-Static Tile (ESD-01)(ESD-02)(ESD-03)	01/30/20	-	-	01/30/20	02/06/20	02/07/20	CAMA	AC	
096500-004-1	096500-04s	Resilient Base	01/30/20	-	-	01/30/20	02/06/20	02/07/20	CAMA	AC	
096500-005-1	096500-05s	Samples	01/30/20	-	-	01/30/20	02/06/20	02/07/20	CAMA	AC	
097200-001-1	097200-01s	RWC-01 Impact Wall Resistant Solution	07/01/20	-	-	07/01/20	-	-	CAMA		
097200-002-1	097200-02s	VWC-01 Denovo Ledge 04	07/01/20	-	-	07/01/20	-	-	CAMA		
097200-003-1	097200-03s	VWC-02 Denovo Milestone 05	07/01/20	-	-	07/01/20	-	-	CAMA		
097200-004-1	097200-04s	Samples	07/01/20	-	-	07/01/20	-	-	CAMA		<i>Awaiting receipt of physical samples</i>
099000-001-1	099000-01	Painting Product Data	01/15/20	-	-	01/15/20	01/29/20	01/29/20	CAMA	RR	
099000-001-2	099000-01 R1	Painting Product Data	01/31/20	-	-	01/31/20	02/06/20	02/07/20	CAMA	AC	
DIVISION 10 - SPECIALTIES											
102213-001-1	102213-01s	Wire Mesh Partitions	03/13/20	-	-	03/15/20	-	03/15/20	JHA	RR	
102800-001-1	102800-01s	Toilet and Bath Accessories	05/20/20	-	-	-	-	05/27/20	JHA	AC/R	
104416-001-1	104416-01s	Fire Extinguishers	05/20/20	-	-	-	-	05/27/20	JHA	A	
105113-001-1	105113-01s	Metal Locker SD	03/13/20	03/16/20	03/25/20	03/15/20	03/20/20	03/31/20	JHA	AC	
105500-001-1	105500-01s	High Security Key Box	04/22/20	-	-	-	-	04/23/20	JHA	AC	
107516-001-1	107516-01s	Flag Poles	05/28/20	-	-	-	-	06/10/20	JHA	A	
DIVISION 11 - EQUIPMENT											
115000-001-1	115000-01s	Canopy Hood	04/27/20	-	-	-	-	04/27/20	JHA	AC	
115000-002-1	115000-01s	Canopy Hood	04/28/20	-	-	-	-	04/28/20	JHA	AC	
111900-001-1	111900-01s	Detention Equipment	04/01/20	-	-	-	-	04/02/20	JHA	AC	

SHOP DRAWING LOG

PROJECT: New Facility for the Carver Police Department, 3 Center Street, Carver, Massachusetts								STATE PROJECT No.:			
G.C.: Tower Construction Corporation								JHA PROJECT No.: 1830			
TEAM: JH Architects (JHA); Garcia-Galuska-DeSousa (GGD); Linden Landscape Architects (LLA); Szewczak Associates (SA); Paul Hawley Associates (PHA); CAMA (CAMA); Building Engineering Resources (BER)								G.C. PROJECT No.: 2252			
JHA SHOP DRAWING NUMBER	G.C. SHOP DRAWING NUMBER	DESCRIPTION <div style="font-size: small; margin-top: 5px;"> = Reviewed & Returned = Under JHA Review = Under Consultant Review = Under Owner Review = Awaiting G.C. Response </div>	DATE REC'D	DATE SENT	DATE REC'D	DATE SENT	DATE REC'D	DATE RTN'D	REVIEWER	ACTION / REMARK	COMMENTS
			- From - G.C.	- To - Owner	- From - Owner	- To - Consult	- From - Consult	- To - G.C.			
DIVISION 12 - FURNISHINGS											
123216-001-1	123216-01s	Casework Shop Drawings	03/24/20	-	-	-	-	04/02/20	JHA	RR	
129313-001-1	129313-01s	Bike Rack	04/28/20	-	-	04/28/20	04/29/20	04/29/20	LLA	A	
DIVISION 13 - SPECIAL CONSTRUCTION											
134700-001-1	134700-01 134700-02 134700-03	Bullet Resistant Protection	02/24/20	-	-	-	-	02/27/20	JHA	AC	
DIVISION 14 - CONVEYING EQUIPMENT											
DIVISION 21 - FIRE SUPPRESSION											
210000-001-1	210000-01S	Fire Protection	01/17/20	-	-	01/17/20	-	-	BER	-	VOIDED BY GTC on 4/8/20
210000-002-1	210000-01s	Underground Fire Service	04/29/20	-	-	04/29/20	05/08/20	05/11/20	BER	A	
210000-003-1	210000-02s	Wet Sprinkler Piping	04/29/20	-	-	04/29/20	05/08/20	05/11/20	BER	A	
210000-004-1	210000-03s	Dry Pipe Sprinkler	04/29/20	-	-	04/29/20	05/08/20	05/11/20	BER	A	
210000-005-1	210000-04s	Valves	04/29/20	-	-	04/29/20	-	-	-	-	SUPERSEDED by FPC ON 5/6/20
210000-005-2	210000-04 Rev1s	Valves	05/06/20	-	-	05/07/20	05/13/20	05/13/20	BER	A	
210000-006-1	210000-05s	Hangers and Supports	04/29/20	-	-	04/29/20	05/13/20	05/13/20	BER	A	
210000-007-1	210000-06s	FDC	04/29/20	-	-	04/29/20	05/13/20	05/13/20	BER	A	
210000-008-1	210000-07s	Sprinkler Heads	04/29/20	-	-	04/29/20	05/13/20	05/13/20	BER	A	
210000-009-1	210000-08s	Sprinkler Cabinet	04/29/20	-	-	04/29/20	05/13/20	05/13/20	BER	A	

SHOP DRAWING LOG

PROJECT: New Facility for the Carver Police Department, 3 Center Street, Carver, Massachusetts							STATE PROJECT No.:				
G.C.: Tower Construction Corporation							JHA PROJECT No.: 1830				
TEAM: JH Architects (JHA); Garcia-Galuska-DeSousa (GGD); Linden Landscape Architects (LLA); Szewczak Associates (SA); Paul Hawley Associates (PHA); CAMA (CAMA); Building Engineering Resources (BER)							G.C. PROJECT No.: 2252				
JHA SHOP DRAWING NUMBER	G.C. SHOP DRAWING NUMBER	DESCRIPTION <div style="font-size: small; margin-top: 5px;"> = Reviewed & Returned = Under JHA Review = Under Consultant Review = Under Owner Review = Awaiting G.C. Response </div>	DATE REC'D	DATE SENT	DATE REC'D	DATE SENT	DATE REC'D	DATE RTN'D	REVIEWER	ACTION / REMARK	COMMENTS
			- From - G.C.	- To - Owner	- From - Owner	- To - Consult	- From - Consult	- To - G.C.			
210000-010-1	210000-09s	Signaling Devices	04/29/20	-	-	04/29/20	-	-	-	-	<i>SUPERSEDED by FPC ON 5/6/20</i>
210000-010-2	210000-09 Rev1s	Signaling Devices	05/06/20	-	-	05/07/20	05/27/20	05/27/20	BER	A	
210000-011-1	210000-10s	Water Pressure Gauges	04/29/20	-	-	04/29/20	-	-	-	-	<i>SUPERSEDED by FPC ON 5/6/20</i>
210000-011-2	210000-10 Rev1s	Water Pressure Gauges	05/06/20	-	-	05/07/20	05/27/20	05/27/20	BER	A	
210000-012-1	210000-11s	Sleeves and Penetrations	04/29/20	-	-	04/29/20	05/13/20	05/13/20	BER	A	
210000-013-1	210000-12s	Fire Hydrants	04/29/20	05/13/20	05/14/20	04/29/20	05/13/20	05/14/20	BER	AC	
210000-014-1	210000-13s	Hydraulic Calcs & Drawings	05/06/20	-	-	05/07/20	05/27/20	05/27/20	BER	RR	
210000-015-1	210000-14s	FP Drawings	05/06/20	-	-	05/07/20	-	-	BER	RR	<i>Engineer Comments in 210000-014-1</i>
210000-016-1	210000-15s	Fire Pump	05/06/20	-	-	05/07/20	05/27/20	05/27/20	BER	AC	
210000-017-1	210000-16s	Underground Water Storage Tank	05/13/20	-	-	05/13/20	05/27/20	05/27/20	BER	AC	
210000-018-1	210000-17s	Sprinkler Coordination Drawings	06/08/20	-	-	06/08/20	06/22/20	06/22/20	BER	A	
DIVISION 22 - PLUMBING											
220000-001-1	220000-01s	Tight Tank	02/17/20	-	-	02/17/20	03/02/20	03/02/20	BER	AC	
220000-002-1	220000-02s	Water Heaters	02/17/20	-	-	02/17/20	03/02/20	03/02/20	BER	A	
220000-003-1	220000-03s	Pumps	02/17/20	-	-	02/17/20	03/02/20	03/02/20	BER	A	
220000-004-1	220000-04s	Pipe I.D.	02/17/20	-	-	02/17/20	03/02/20	03/02/20	BER	A	
220000-005-1	220000-05s	Water Meter	02/17/20	-	-	02/17/20	03/02/20	03/02/20	BER	A	
220000-006-1	220000-06s	Cross Connection Points	02/17/20	-	-	02/17/20	03/02/20	03/02/20	BER	A	
220000-007-1	220000-07s	Pipe Supports	02/21/20	-	-	02/24/20	03/02/20	03/02/20	BER	A	
220000-008-1	220000-08s	Sleeves, Insers, Fire Stopping & Escutcheons	02/21/20	-	-	02/24/20	03/02/20	03/02/20	BER	A	
220000-009-1	220000-09s	Pipe Materials	02/21/20	-	-	02/24/20	03/02/20	03/02/20	BER	A	
220000-010-1	220000-10s	Copper Pipe	02/21/20	-	-	02/24/20	03/02/20	03/02/20	BER	A	
220000-011-1	220000-11s	Sanitary Waste & Vent	02/21/20	-	-	02/24/20	03/02/20	03/02/20	BER	A	
220000-012-1	220000-12s	Press & Temp Control Devices	02/21/20	-	-	02/24/20	03/02/20	03/02/20	BER	A	
220000-013-1	220000-13s	Insulation	02/21/20	-	-	02/24/20	03/02/20	03/02/20	BER	A	
220000-014-1	220000-14s	Traps & Strainers	02/21/20	-	-	02/24/20	03/02/20	03/02/20	BER	AC	
220000-015-1	220000-15s	Thermometers & Pressure Gauges	02/21/20	-	-	02/24/20	03/02/20	03/02/20	BER	A	
220000-016-1	220000-16s	Wall Hydrants & Hose Bibbs	02/21/20	-	-	02/24/20	03/02/20	03/02/20	BER	A	
220000-017-1	220000-17s	Water Hammer Arrestors	02/21/20	-	-	02/24/20	03/02/20	03/02/20	BER	A	
220000-018-1	220000-18s	Drains	03/10/20	-	-	03/10/20	03/24/20	03/24/20	BER	A	

SHOP DRAWING LOG

PROJECT: New Facility for the Carver Police Department, 3 Center Street, Carver, Massachusetts								STATE PROJECT No.:			
G.C.: Tower Construction Corporation								JHA PROJECT No.: 1830			
TEAM: JH Architects (JHA); Garcia-Galuska-DeSousa (GGD); Linden Landscape Architects (LLA); Szewczak Associates (SA); Paul Hawley Associates (PHA); CAMA (CAMA); Building Engineering Resources (BER)								G.C. PROJECT No.: 2252			
JHA SHOP DRAWING NUMBER	G.C. SHOP DRAWING NUMBER	DESCRIPTION <div style="font-size: small; margin-top: 5px;"> = Reviewed & Returned = Under JHA Review = Under Consultant Review = Under Owner Review = Awaiting G.C. Response </div>	DATE REC'D	DATE SENT	DATE REC'D	DATE SENT	DATE REC'D	DATE RTN'D	REVIEWER	ACTION / REMARK	COMMENTS
			- From - G.C.	- To - Owner	- From - Owner	- To - Consult	- From - Consult	- To - G.C.			
220000-019-1	220000-19s	Plumbing Fixtures - Water Closets	03/10/20	-	-	03/10/20	03/24/20	03/24/20	BER/JHA	AC	
220000-020-1	220000-20s	Plumbing Fixtures - Urinals	03/10/20	-	-	03/10/20	03/24/20	03/24/20	BER/JHA	AC	
220000-021-1	220000-21s	Plumbing Fixtures - Sinks & Faucets	03/10/20	-	-	03/10/20	03/24/20	03/24/20	BER/JHA	AC	
220000-022-1	220000-22s	Plumbing Fixtures - Shower	03/10/20	-	-	03/10/20	03/24/20	03/24/20	BER/JHA	AC	
220000-023-1	220000-23s	Plumbing Fixtures - Lavatories	03/10/20	-	-	03/10/20	03/24/20	03/24/20	BER/JHA	A	
220000-024-1	220000-24s	Plumbing Fixtures - Ice Maker Box	03/10/20	-	-	03/10/20	03/24/20	03/24/20	BER/JHA	A	
220000-025-1	220000-25s	Plumbing Fixtures - Laundry Washing Machine Box	03/10/20	-	-	03/10/20	03/24/20	03/24/20	BER/JHA	A	
220000-026-1	220000-26s	Exterior Wall Hydrant	03/10/20	-	-	03/10/20	03/24/20	03/24/20	BER/JHA	AC	
220000-027-1	220000-27s	Plumbing Fixtures - Emergency Eye Wash & Shower	03/10/20	-	-	03/10/20	03/24/20	03/24/20	BER/JHA	A	
220000-028-1	220000-28s	Plumbing Fixtures - Detention Grade Shower System	03/10/20	-	-	03/10/20	03/24/20	03/24/20	BER/JHA	AC	
220000-029-1	220000-29s	Plumbing Fixtures - Drinking Fountain	03/10/20	-	-	03/10/20	03/24/20	03/24/20	BER/JHA	A	
220000-030-1	220000-30s	Plumbing Fixtures - Combination Lav-Toilets	03/10/20	-	-	03/10/20	03/24/20	03/24/20	BER/JHA	RR	
220000-031-1	220000-31s	Thermostatic Mixing Valves	03/10/20	-	-	03/10/20	03/24/20	03/24/20	BER	A	
220000-032-1	220000-32s	Plumbing Fixtures - Detention Grade Shower Valve	03/10/20	-	-	03/10/20	03/24/20	03/24/20	BER/JHA	R	
220000-033-1	220000-33s	Plumbing Fixtures - Boot Wash Hose Bib	03/10/20	-	-	03/10/20	03/24/20	03/24/20	BER/JHA	AC	
DIVISION 23 - HVAC											
230000-001-1	230000-01s	Ductwork & Air Distribution Equipment	03/12/20	-	-	03/12/20	03/25/20	03/25/20	BER	A	
230000-002-1	230000-02s	Centrifugal Fans	03/12/20	-	-	03/12/20	03/25/20	03/25/20	BER	A	
230000-003-1	230000-03s	RGDs	03/12/20	-	-	03/12/20	03/25/20	03/25/20	BER/JHA	A/AC	
230000-004-1	230000-04s	ERV & VRF	03/12/20	-	-	03/12/20	03/25/20	03/25/20	BER	AC	
230000-005-1	230000-05s	Duct & Pipe Insulation	03/17/20	-	-	03/18/20	03/25/20	03/25/20	BER	A	
230000-006-1	230000-06s	Electrical Heaters	03/18/20	-	-	03/18/20	03/25/20	03/25/20	BER	AC	
230000-007-1	230000-07s	Motorized Dampers	03/18/20	-	-	03/18/20	03/25/20	03/25/20	BER	A	
230000-008-1	230000-08s	Outbuilding HVAC Equipment	04/29/20	-	-	04/29/20	05/13/20	05/13/20	BER	A	
DIVISION 26 - ELECTRICAL											

SHOP DRAWING LOG

PROJECT: New Facility for the Carver Police Department, 3 Center Street, Carver, Massachusetts								STATE PROJECT No.:			
G.C.: Tower Construction Corporation								JHA PROJECT No.: 1830			
TEAM: JH Architects (JHA); Garcia-Galuska-DeSousa (GGD); Linden Landscape Architects (LLA); Szewczak Associates (SA); Paul Hawley Associates (PHA); CAMA (CAMA); Building Engineering Resources (BER)								G.C. PROJECT No.: 2252			
JHA SHOP DRAWING NUMBER	G.C. SHOP DRAWING NUMBER	DESCRIPTION	DATE REC'D - From - G.C.	DATE SENT - To - Owner	DATE REC'D - From - Owner	DATE SENT - To - Consult	DATE REC'D - From - Consult	DATE RTN'D - To - G.C.	REVIEWER	ACTION / REMARK	COMMENTS
260000-001-1	260000-01s	Fire Alarm System	02/12/20	-	-	02/12/20	02/14/20	02/14/20	BER	A/AC/RR	
260000-001-2	260000-01s Rev 1	Fire Alarm System	03/17/20	-	-	03/18/20	03/19/20	03/19/20	BER	A/AC/RR	
260000-001-3	260000-01s Rev 2	Fire Alarm System	05/15/20	-	-	05/15/20	05/18/20	-	BER	-	VOIDED by 260000-001-4
260000-001-4	260000-01s Rev 3	Fire Alarm System	05/20/20	-	-	05/26/20	05/27/20	05/27/20	BER	A/AC	
260000-002-1	260000-02s	Engine Generator System	02/12/20	-	-	02/12/20	02/14/20	02/14/20	BER	AC/RR	
260000-002-2	260000-02s Rev 1	Engine Generator System	03/12/20	-	-	03/12/20	03/16/20	03/16/20	BER	AC/RR	
260000-002-3	260000-02s Rev 2	Engine Generator System	03/19/20	-	-	03/19/20	03/19/20	03/19/20	BER	AC	
260000-003-1	260000-03s	Lightning Protection	02/12/20	-	-	02/12/20	02/14/20	02/14/20	BER	A/AC/RR	
260000-003-2	260000-03s Rev1	Lightning Protection	02/20/20	-	-	02/20/20	02/20/20	02/24/20	BER/JHA	A/AC	
260000-004-1	260000-04s	Storm Switch (ATS)	02/20/20	-	-	02/20/20	02/21/20	02/24/20	BER	AC	
260000-005-1	260000-05s	Encl for Indiv Mntd Overcurrent & Switching Dev	03/17/20	-	-	03/18/20	03/19/20	03/19/20	BER	A/AC	
260000-006-1	260000-06s	Panelboards	03/17/20	-	-	03/18/20	03/19/20	03/19/20	BER	A/AC	
260000-007-1	260000-07s	Cartridge Fuses	03/17/20	-	-	03/18/20	03/19/20	03/19/20	BER	AC	
260000-008-1	260000-08s	Branch Panel SPD Protection	03/17/20	-	-	03/18/20	03/19/20	03/19/20	BER	A	
260000-009-1	260000-09s	Lighting Fixture	03/18/20	-	-	03/18/20	03/20/20	03/20/20	BER/JHA	A/AC	
260000-009-02	260000-09s Rev 1	Lighting Fixture	04/13/20	-	-	04/13/20	04/14/20	04/14/20	BER/JHA	A/AC	
260000-010-1	260000-10s	Lighting Control	03/18/20	-	-	03/18/20	03/20/20	03/20/20	BER/JHA	A/AC/R	
260000-011-1	260000-11s	Raceways & Fittings	03/18/20	-	-	03/18/20	03/19/20	03/19/20	BER	A	
260000-012-1	260000-12s	Cable Tray	03/18/20	-	-	03/18/20	03/19/20	03/19/20	BER	A/R	
260000-013-1	260000-13s	Uninterruptible Power System	03/24/20	-	-	03/24/20	03/25/20	03/25/20	BER	R	
260000-013-2	260000-13 Rev 1	Uninterruptible Power System	03/30/20	-	-	03/30/20	03/31/20	03/31/20	BER	AC	
260000-014-1	260000-14s	Grounding System	03/26/20	-	-	03/29/20	03/30/20	03/30/20	BER	A	
260000-015-1	260000-15s	Phasing & Color Coding	03/26/20	-	-	03/29/20	03/30/20	03/30/20	BER	A	
260000-016-1	260000-16s	Wiring Materials	03/26/20	-	-	03/29/20	03/30/20	03/30/20	BER	A/AC	
260000-017-1	260000-17s	Wiring Devices	03/26/20	-	-	03/29/20	03/30/20	03/30/20	BER	A/AC	
260000-018-1	260000-18s	Access Panels	03/26/20	-	-	03/29/20	03/30/20	03/30/20	BER	AC	
260000-019-1	260000-19s	Outlet, Junction, Pull Boxes	03/26/20	-	-	03/29/20	03/30/20	03/30/20	BER	A/AC	
260000-020-1	260000-20s	Trough	03/26/20	-	-	03/29/20	03/30/20	03/30/20	BER	A	
260000-021-1	260000-21s	Floor Boxes	03/26/20	-	-	03/29/20	03/30/20	03/30/20	BER	AC	
260000-022-1	260000-22s	Motor Control	03/30/20	-	-	03/30/20	03/31/20	03/31/20	BER	AC	
260000-023-1	260000-23s	Integrated Technology Infrastructure Support	03/30/20	-	-	03/30/20	03/31/20	03/31/20	BER	AC	

SHOP DRAWING LOG

PROJECT: New Facility for the Carver Police Department, 3 Center Street, Carver, Massachusetts								STATE PROJECT No.:			
G.C.: Tower Construction Corporation								JHA PROJECT No.: 1830			
TEAM: JH Architects (JHA); Garcia-Galuska-DeSousa (GGD); Linden Landscape Architects (LLA); Szewczak Associates (SA); Paul Hawley Associates (PHA); CAMA (CAMA); Building Engineering Resources (BER)								G.C. PROJECT No.: 2252			
JHA SHOP DRAWING NUMBER	G.C. SHOP DRAWING NUMBER	DESCRIPTION	DATE REC'D	DATE SENT	DATE REC'D	DATE SENT	DATE REC'D	DATE RTN'D	REVIEWER	ACTION / REMARK	COMMENTS
			- From - G.C.	- To - Owner	- From - Owner	- To - Consult	- From - Consult	- To - G.C.			
260000-024-1	260000-24s	Equipment Racks	04/01/20	-	-	04/01/20	04/02/20	04/02/20	BER	AC	
260000-025-1	260000-25s	Surge Protected Power Strip	04/01/20	-	-	04/01/20	04/02/20	04/02/20	BER	A	
260000-026-1	260000-26s	Cable Supports	04/01/20	-	-	04/01/20	04/02/20	04/02/20	BER	A	
260000-027-1	260000-27s	Bonding & Grounding Jumper Cable	04/01/20	-	-	04/01/20	04/02/20	04/02/20	BER	A	
260000-028-1	260000-28s	Unshielded Twisted Pair Cable	04/01/20	-	-	04/01/20	04/02/20	04/02/20	BER	AC	
260000-029-1	260000-29s	Broadband RF Cabling System	04/01/20	-	-	04/01/20	04/02/20	04/02/20	BER	AC	
260000-030-1	260000-30s	Underground Enclosures	04/01/20	-	-	04/01/20	04/02/20	04/02/20	BER	AC	
260000-031-1	260000-31s	Lighting Factory Drawings	04/30/20	-	-	04/30/20	05/01/20	05/01/20	BER	AC	
260000-032-1	260000-32s	Lighting - Factory Drawings Vode	05/13/20	-	-	05/13/20	05/14/20	05/14/20	BER	AC	
DIVISION 27 - COMMUNICATIONS											
DIVISION 31 - EARTHWORK											
312000-001-1	312000-01s	K-RAP Base	03/06/20	-	-	03/06/20	03/09/20	03/09/20	GGD	AC	
312500-001-1	312500-01s	Erosion Control	01/17/20	-	-	01/17/20	01/27/20	01/28/20	LLA	A	
312500-002-1	312500-02s	SWPPP	02/17/20	-	-	02/17/20	02/25/20	02/25/20	GGD	RR	
312500-002-2	312500-02s Rev 1	SWPPP	03/02/20	-	-	03/02/20	03/09/20	03/09/20	GGD	AC	
DIVISION 32 - EXTERIOR IMPROVEMENTS											
321313-001-1	033004-03s	Exterior Flatwork	02/19/20	-	-	02/19/20	02/24/20	02/24/20	LLA	A	
321313-002-1	321313-02s	Site Tactile Warning Tiles	04/29/20	04/30/20	04/30/20	04/29/20	04/30/20	04/30/20	LLA	AC	
321613-001-1	321613-01s	Precast Concrete Curb	04/21/20	-	-	04/21/20	04/22/20	04/22/20	LLA	A	
323913-001-1	323913-01s	Steel Bollards and Bollard Covers	04/29/20	-	-	04/29/20	04/30/20	04/30/20	LLA	AC	
DIVISION 33 - UTILITIES											
330000-001-1	330000-01	Manhole and Precast Concrete Structure	01/08/20	-	-	01/08/20	01/16/20	01/17/20	GGD	RR	

SHOP DRAWING LOG

PROJECT: New Facility for the Carver Police Department, 3 Center Street, Carver, Massachusetts								STATE PROJECT No.:			
G.C.: Tower Construction Corporation								JHA PROJECT No.: 1830			
TEAM: JH Architects (JHA); Garcia-Galuska-DeSousa (GGD); Linden Landscape Architects (LLA); Szewczak Associates (SA); Paul Hawley Associates (PHA); CAMA (CAMA); Building Engineering Resources (BER)								G.C. PROJECT No.: 2252			
JHA SHOP DRAWING NUMBER	G.C. SHOP DRAWING NUMBER	DESCRIPTION <div style="font-size: small; margin-top: 5px;"> = Reviewed & Returned = Under JHA Review = Under Consultant Review = Under Owner Review = Awaiting G.C. Response </div>	DATE REC'D	DATE SENT	DATE REC'D	DATE SENT	DATE REC'D	DATE RTN'D	REVIEWER	ACTION / REMARK	COMMENTS
			- From - G.C.	- To - Owner	- From - Owner	- To - Consult	- From - Consult	- To - G.C.			
330000-001-2	330000-01s	Manhole and Precast Concrete Structure	02/17/20	-	-	02/17/20	02/25/20	02/25/20	GGD	AC	
330000-002-1	330000-01s	Site Utilities	01/17/20	-	-	01/17/20	01/28/20	01/28/20	GGD	AC	
330000-003-1	330000-02s	Sewers and Pipes	01/17/20	-	-	01/17/20	01/24/20	01/24/20	GGD	RR	
330000-004-1	033004-01s	Concrete Ductbank	02/19/20	-	-	02/19/20	02/24/20	02/24/20	GGD	RR	
330000-004-2	033004-01s Rev 1	Concrete Ductbank	03/05/20	-	-	03/06/20	03/17/20	03/17/20	GGD	A	
330000-005-1	330000-03s	K-RAP Base	02/27/20	-	-	02/27/20	-	-	-	-	VOIDED by GC - See 312000-001-1

PROJECT: Carver Police Station	PROJECT #:	Report Number: 78
---------------------------------------	-------------------	--------------------------

Contract Time:	Date: 6-01-2020	
Days Elapsed:	Day: Monday	
Extensions:	Weather: Cloudy	
Days Remaining:	Temperature Cycle at 7 AM: 47 – 63 deg.	
Site Condition:	Dry	

Contractor	Workforce	
Tower Construction	1 Superintendent, 1 laborer – Kevin Thompson (site supervision)	2
Dig It	0 operator, 0 laborers, 0 foreman (sitework)	0
S&S Concrete Forms	0 carpenter, 0 laborers, 0 ironworker, 0 operator (formwork)	0
Delta	0 sprinkler fitters (fire protection)	0
American Electrical	0 foreman, 0 journeyman, 0 apprentice (electrical)	0
Lapan	0 foreman, 0 journeyman, 0 apprentice (mechanical)	0
Engineering Welding & Fabricating	0 iron workers (structural steel)	0
Outback Surveying	0 surveyors	0
John Oliveira & Sons	0 foreman, 3 concrete formers	3
Total Workforce		5

Miscellaneous Others		
CHA	Alyssa Chatani	1
Town of Carver	Bill Harriman	1
Empire	1 rep (framing)	1
Total Misc. Workforce		3

Construction Activity:

Dig It: Not on site.

S&S Concrete Forms: Not on site.

Delta: Not on site.

American Electrical: Not on site.

Lapan: Not on site.

Engineering Welding and Fabricating: Not on site.

Outback Surveying: Not on site.

John Oliveira & Sons: Sidewalk prep. and removing wood column boxes from the slab.

Clerk's remarks: Tower had a laborer on site to remove the curing blankets.

Site Visitors/Meetings: Bill and Empire rep.

Deliveries: none

Equipment Used: Dig It: (2) CAT Excavators 325F, 335F (1) CAT Wheel Loader



**ON-SITE REPRESENTATIVE
DAILY REPORT**

PROJECT: Carver Police Station	PROJECT #:	Report Number: 79
---------------------------------------	-------------------	--------------------------

Contract Time:	Date: 6-02-2020	
Days Elapsed:	Day: Tuesday	
Extensions:	Weather: Partly Cloudy	
Days Remaining:	Temperature Cycle at 7 AM: 56 – 68 deg.	
Site Condition:	Dry	

Contractor	Workforce	
Tower Construction	1 Superintendent, 0 laborer – Kevin Thompson (site supervision)	1
Dig It	0 operator, 0 laborers, 0 foreman (sitework)	0
S&S Concrete Forms	0 carpenter, 0 laborers, 0 ironworker, 0 operator (formwork)	0
Delta	0 sprinkler fitters (fire protection)	0
American Electrical	0 foreman, 0 journeyman, 0 apprentice (electrical)	0
Lapan	0 foreman, 0 journeyman, 0 apprentice (mechanical)	0
Engineering Welding & Fabricating	5 iron workers, 1 operator (structural steel)	6
Outback Surveying	0 surveyors	0
John Oliveira & Sons	0 foreman, 0 concrete formers	0
	Total Workforce	7

Miscellaneous Others		
CHA	Alyssa Chatani	1
Town of Carver	Bill Harriman, Dave S.	1
	Total Misc. Workforce	2

Construction Activity:

Dig It: Not on site.

S&S Concrete Forms: Not on site.

Delta: Not on site.

American Electrical: Not on site.

Lapan: Not on site.

Engineering Welding and Fabricating: Began steel erection. Set all 44 columns.

Outback Surveying: Not on site.

John Oliveira & Sons: Not on site.

Clerk's remarks: none

Site Visitors/Meetings: Bill

Deliveries: none

Equipment Used: Dig It: (2) CAT Excavators 325F, 335F (1) CAT Wheel Loader

PROJECT: Carver Police Station	PROJECT #:	Report Number: 80
---------------------------------------	-------------------	--------------------------

Contract Time:	Date: 6-03-2020	
Days Elapsed:	Day: Wednesday	
Extensions:	Weather: Sunny	
Days Remaining:	Temperature Cycle at 7 AM: 56 – 79 deg.	
Site Condition:	Dry	

Contractor	Workforce	
Tower Construction	1 Superintendent, 0 laborer – Kevin Thompson (site supervision)	1
Dig It	0 operator, 0 laborers, 1 foreman (sitework)	1
S&S Concrete Forms	0 carpenter, 0 laborers, 0 ironworker, 0 operator (formwork)	0
Delta	0 sprinkler fitters (fire protection)	0
American Electrical	0 foreman, 0 journeyman, 0 apprentice (electrical)	0
Lapan	0 foreman, 0 journeyman, 0 apprentice (mechanical)	0
Engineering Welding & Fabricating	4 iron workers, 1 operator (structural steel)	5
Outback Surveying	0 surveyors	0
John Oliveira & Sons	0 foreman, 0 concrete formers	0
	Total Workforce	7

Miscellaneous Others		
CHA	Alyssa Chatani	1
Tower Construction	Patrick Fitzgerald	1
	Total Misc. Workforce	2

Construction Activity:

Dig It: Laying out concrete curbing.

S&S Concrete Forms: Not on site.

Delta: Not on site.

American Electrical: Not on site.

Lapan: Not on site.

Engineering Welding and Fabricating: Continued erecting steel beams. Completed steel erection.

Outback Surveying: Not on site.

John Oliveira & Sons: Not on site.

Clerk's remarks: none

Site Visitors/Meetings: Weekly meeting

Deliveries: none

Equipment Used: Dig It: (2) CAT Excavators 325F, 335F (1) CAT Wheel Loader

PROJECT: Carver Police Station	PROJECT #:	Report Number: 81
---------------------------------------	-------------------	--------------------------

Contract Time:	Date: 6-04-2020	
Days Elapsed:	Day: Thursday	
Extensions:	Weather: Sunny	
Days Remaining:	Temperature Cycle at 7 AM: 63 – 84 deg.	
Site Condition:	Dry	

Contractor	Workforce	
Tower Construction	1 Superintendent, 0 laborer – Kevin Thompson (site supervision)	1
Dig It	1 operator, 2 laborers, 1 foreman (sitework)	4
S&S Concrete Forms	0 carpenter, 0 laborers, 0 ironworker, 0 operator (formwork)	0
Delta	0 sprinkler fitters (fire protection)	0
American Electrical	0 foreman, 0 journeyman, 0 apprentice (electrical)	0
Lapan	0 foreman, 0 journeyman, 0 apprentice (mechanical)	0
Engineering Welding & Fabricating	4 iron workers, 1 operator (structural steel)	5
Outback Surveying	0 surveyors	0
John Oliveira & Sons	10 concrete formers	10
	Total Workforce	20

Miscellaneous Others		
CHA	Alyssa Chatani	1
	Total Misc. Workforce	1

Construction Activity:

Dig It: Setting curbing on Center Street to about the start of the library. Removed 2 trees from the library.

S&S Concrete Forms: Not on site.

Delta: Not on site.

American Electrical: Not on site.

Lapan: Not on site.

Engineering Welding and Fabricating: Began welding and straightening ensuring steel is plumb.

Outback Surveying: Not on site.

John Oliveira & Sons: Poured concrete sidewalk by the library and finished it.

Clerk's remarks: none

Site Visitors/Meetings: none

Deliveries: approx. 40CY concrete, lumber

Equipment Used: Dig It: (2) CAT Excavators 325F, 335F (1) CAT Wheel Loader

PROJECT: Carver Police Station	PROJECT #:	Report Number: 82
---------------------------------------	-------------------	--------------------------

Contract Time:	Date: 6-05-2020	
Days Elapsed:	Day: Friday	
Extensions:	Weather: Cloudy/Light Rain	
Days Remaining:	Temperature Cycle at 7 AM:	63 – 76 deg.
Site Condition:	Dry	

Contractor	Workforce	
Tower Construction	1 Superintendent, 0 laborer – Kevin Thompson (site supervision)	1
Dig It	1 operator, 2 laborers, 1 foreman (sitework)	4
S&S Concrete Forms	0 carpenter, 0 laborers, 0 ironworker, 0 operator (formwork)	0
Delta	0 sprinkler fitters (fire protection)	0
American Electrical	0 foreman, 0 journeyman, 0 apprentice (electrical)	0
Lapan	0 foreman, 0 journeyman, 0 apprentice (mechanical)	0
Engineering Welding & Fabricating	5 iron workers, 0 operator (structural steel)	5
Outback Surveying	0 surveyors	0
Empire	3 carpenters (framing)	3
John Oliveira & Sons	0 concrete formers	0
Total Workforce		13

Miscellaneous Others		
CHA	Alyssa Chatani	1
Town of Carver	Dave S., Bill Harriman	2
Briggs	1 rep on site for structural steel inspection	1
Barber Drywall	3 reps to meet about upcoming work	3
Total Misc. Workforce		7

Construction Activity:

Dig It: Continuing setting curbing at the library.

S&S Concrete Forms: Not on site.

Delta: Not on site.

American Electrical: Not on site.

Empire: Began wood blocking on steel beams.

Lapan: Not on site.

Engineering Welding and Fabricating: Continued welding and straightening ensuring steel is plumb.

Outback Surveying: Not on site.

John Oliveira & Sons: Not on site.

Clerk's remarks: none

Site Visitors/Meetings: none

Deliveries: none

Equipment Used: Dig It: (2) CAT Excavators 325F, 335F (1) CAT Wheel Loader

PROJECT: Carver Police Station	PROJECT #:	Report Number: 83
---------------------------------------	-------------------	--------------------------

Contract Time:	Date: 6-08-2020	
Days Elapsed:	Day: Monday	
Extensions:	Weather: Sunny	
Days Remaining:	Temperature Cycle at 7 AM:	54 – 76 deg.
Site Condition:	Dry	

Contractor	Workforce	
Tower Construction	1 Superintendent, 0 laborer – Kevin Thompson (site supervision)	1
Dig It	1 operator, 2 laborers, 1 foreman (sitework)	4
S&S Concrete Forms	0 carpenter, 0 laborers, 0 ironworker, 0 operator (formwork)	0
Delta	0 sprinkler fitters (fire protection)	0
American Electrical	0 foreman, 0 journeyman, 0 apprentice (electrical)	0
Lapan	0 foreman, 0 journeyman, 0 apprentice (mechanical)	0
Engineering Welding & Fabricating	5 iron workers, 0 operator (structural steel)	5
Outback Surveying	0 surveyors	0
Empire	3 carpenters (framing)	3
John Oliveira & Sons	0 concrete formers	0
Total Workforce		13

Miscellaneous Others		
CHA	Alyssa Chatani	1
Town of Carver	Bill Harriman	1
Total Misc. Workforce		2

Construction Activity:

Dig It: Continuing setting curbing at the library.

S&S Concrete Forms: Not on site.

Delta: Not on site.

American Electrical: Not on site.

Empire: Continued wood blocking on steel beams.

Lapan: Not on site.

Engineering Welding and Fabricating: Continued welding and straightening ensuring steel is plumb.

Outback Surveying: Not on site.

John Oliveira & Sons: Not on site.

Clerk's remarks: Last day of curbing installation. Tank delivery is still approx. 4 weeks out.

Site Visitors/Meetings: none

Deliveries: Conex for Empire

Equipment Used: Dig It: (2) CAT Excavators 325F, 335F (1) CAT Wheel Loader

PROJECT: Carver Police Station	PROJECT #:	Report Number: 84
---------------------------------------	-------------------	--------------------------

Contract Time:	Date: 6-09-2020	
Days Elapsed:	Day: Tuesday	
Extensions:	Weather: Fair	
Days Remaining:	Temperature Cycle at 7 AM: 59 – 77 deg.	
Site Condition:	Dry	

Contractor	Workforce	
Tower Construction	1 Superintendent, 0 laborer – Kevin Thompson (site supervision)	1
Dig It	0 operator, 0 laborers, 0 foreman (sitework)	0
S&S Concrete Forms	0 carpenter, 0 laborers, 0 ironworker, 0 operator (formwork)	0
Delta	0 sprinkler fitters (fire protection)	0
American Electrical	1 foreman, 0 journeyman, 0 apprentice (electrical)	1
Lapan	0 foreman, 0 journeyman, 0 apprentice (mechanical)	0
Engineering Welding & Fabricating	5 iron workers, 0 operator (structural steel)	5
Outback Surveying	0 surveyors	0
Empire	3 carpenters (framing)	3
John Oliveira & Sons	0 concrete formers	0
Total Workforce		10

Miscellaneous Others		
CHA	Alyssa Chatani	1
Town of Carver	Bill Harriman, Dave Siedentopf	2
Szewczak Associates	Richard Szewczak	1
Total Misc. Workforce		4

Construction Activity:

Dig It: Not on site.

S&S Concrete Forms: Not on site.

Delta: Not on site.

American Electrical: Began working on temporary power to the building.

Empire: Continued wood blocking on steel beams.

Lapan: Not on site.

Engineering Welding and Fabricating: Finalized bolts and welds.

Outback Surveying: Not on site.

John Oliveira & Sons: Not on site.

Clerk's remarks: Structural engineer visited the site; no issues noted while on site. Field report to follow.

Site Visitors/Meetings: Bill, Richard

Deliveries: none

Equipment Used: Empire: Boom Lift 600s

PROJECT: Carver Police Station	PROJECT #:	Report Number: 85
---------------------------------------	-------------------	--------------------------

Contract Time:	Date: 6-10-2020	
Days Elapsed:	Day: Wednesday	
Extensions:	Weather: Sunny	
Days Remaining:	Temperature Cycle at 7 AM:	64 – 74 deg.
Site Condition:	Dry	

Contractor	Workforce	
Tower Construction	1 Superintendent, 0 laborer – Kevin Thompson (site supervision)	1
Dig It	0 operator, 0 laborers, 0 foreman (sitework)	0
S&S Concrete Forms	0 carpenter, 0 laborers, 0 ironworker, 0 operator (formwork)	0
Delta	0 sprinkler fitters (fire protection)	0
American Electrical	1 foreman, 1 journeyman, 0 apprentice (electrical)	2
Lapan	0 foreman, 0 journeyman, 0 apprentice (mechanical)	0
Engineering Welding & Fabricating	0 iron workers, 0 operator (structural steel)	0
Outback Surveying	0 surveyors	0
Empire	3 carpenters (framing)	3
John Oliveira & Sons	0 concrete formers	0
Total Workforce		6

Miscellaneous Others		
CHA	Alyssa Chatani, Joe Sullivan	2
Town of Carver	Bill Harriman, Dave Siedentopf, Chief Duphily	3
JHA	Brian Humes	1
Tower Construction	Patrick Fitzgerald	1
Briggs	Structural Steel Inspector	1
Total Misc. Workforce		8

Construction Activity:

Dig It: Not on site.

S&S Concrete Forms: Not on site.

Delta: Not on site.

American Electrical: Continued working on temporary power to the building.

Empire: Continued wood blocking on steel beams.

Lapan: Not on site.

Engineering Welding and Fabricating: Not on site.

Outback Surveying: Not on site.

John Oliveira & Sons: Not on site.

Clerk's remarks: Structural steel inspection passed; no issues noted while on site. Inspection report to follow.

Site Visitors/Meetings: See above; weekly meeting took place on site

Deliveries: none

Equipment Used: Empire: Boom Lift 600s



**ON-SITE REPRESENTATIVE
DAILY REPORT**

PROJECT: Carver Police Station	PROJECT #:	Report Number: 86
---------------------------------------	-------------------	--------------------------

Contract Time:	Date: 6-11-2020	
Days Elapsed:	Day: Thursday	
Extensions:	Weather: Cloudy/Rain	
Days Remaining:	Temperature Cycle at 7 AM: 65 – 75 deg.	
Site Condition:	Wet	

Contractor	Workforce	
Tower Construction	1 Superintendent, 0 laborer – Kevin Thompson (site supervision)	1
Dig It	0 operator, 0 laborers, 0 foreman (sitework)	0
S&S Concrete Forms	0 carpenter, 0 laborers, 0 ironworker, 0 operator (formwork)	0
Delta	0 sprinkler fitters (fire protection)	0
American Electrical	0 foreman, 0 journeyman, 0 apprentice (electrical)	0
Lapan	0 foreman, 0 journeyman, 0 apprentice (mechanical)	0
Engineering Welding & Fabricating	0 iron workers, 0 operator (structural steel)	0
Outback Surveying	0 surveyors	0
Empire	5 carpenters (framing)	5
John Oliveira & Sons	0 concrete formers	0
Commercial Masonry	0 foreman (masonry)	0
Total Workforce		6

Miscellaneous Others		
CHA	Alyssa Chatani, Joe Sullivan	1
Town of Carver	Bill Harriman	1
Total Misc. Workforce		2

Construction Activity:

Dig It: Not on site.

S&S Concrete Forms: Not on site.

Delta: Not on site.

American Electrical: Not on site.

Empire: Continued wood blocking on steel beams.

Lapan: Not on site.

Engineering Welding and Fabricating: Not on site.

Outback Surveying: Not on site.

John Oliveira & Sons: Not on site.

Clerk's remarks: Concrete testing on Friday pushing from 8am to 10am.

Site Visitors/Meetings: Bill, Joe

Deliveries: Flashing, Boom Lift for Empire, Sand

Equipment Used: Empire: (2) Boom Lift 600s



**ON-SITE REPRESENTATIVE
DAILY REPORT**

PROJECT: Carver Police Station	PROJECT #:	Report Number: 87
---------------------------------------	-------------------	--------------------------

Contract Time:	Date: 6-12-2020	
Days Elapsed:	Day: Friday	
Extensions:	Weather: Cloudy/Sunny	
Days Remaining:	Temperature Cycle at 7 AM: 55 – 81 deg.	
Site Condition:	Dry	

Contractor	Workforce	
Tower Construction	1 Superintendent, 0 laborer – Kevin Thompson (site supervision)	1
Dig It	0 operator, 0 laborers, 0 foreman (sitework)	0
S&S Concrete Forms	0 carpenter, 0 laborers, 0 ironworker, 0 operator (formwork)	0
Delta	0 sprinkler fitters (fire protection)	0
American Electrical	0 foreman, 0 journeyman, 0 apprentice (electrical)	0
Lapan	0 foreman, 0 journeyman, 0 apprentice (mechanical)	0
Engineering Welding & Fabricating	0 iron workers, 0 operator (structural steel)	0
Outback Surveying	0 surveyors	0
Empire	5 carpenters (framing)	5
John Oliveira & Sons	3 concrete formers	3
Commercial Masonry	1 foreman, 1 tender (masonry)	2
Total Workforce		11

Miscellaneous Others		
CHA	Alyssa Chatani	1
Town of Carver	Bill Harriman	1
Total Misc. Workforce		2

Construction Activity:

Dig It: Not on site.

S&S Concrete Forms: Not on site.

Commercial Masonry: Began layout and installation of CMU block at Sally Port.

Delta: Not on site.

American Electrical: Not on site.

Empire: Continued wood blocking on steel beams.

Lapan: Not on site.

Engineering Welding and Fabricating: Not on site.

Outback Surveying: Not on site.

John Oliveira & Sons: Installing expansion joints at columns to prepare for concrete infill. Poured 8CY concrete.

Clerk's remarks: Extra cylinders taken for the ISE mixture.

Site Visitors/Meetings: Bill

Deliveries: Concrete, metal studs, CMU block, brick ties

Equipment Used: Empire: (2) Boom Lift 600s

PROJECT: Carver Police Station	PROJECT #:	Report Number: 88
---------------------------------------	-------------------	--------------------------

Contract Time:	Date: 6-15-2020	
Days Elapsed:	Day: Monday	
Extensions:	Weather: Partly Cloudy	
Days Remaining:	Temperature Cycle at 7 AM: 51 – 65 deg.	
Site Condition:	Dry	

Contractor	Workforce	
Tower Construction	1 Superintendent, 0 laborer – Kevin Thompson (site supervision)	1
Dig It	0 operator, 0 laborers, 0 foreman (sitework)	0
S&S Concrete Forms	0 carpenter, 0 laborers, 0 ironworker, 0 operator (formwork)	0
Delta	0 sprinkler fitters (fire protection)	0
American Electrical	1 foreman, 0 journeyman, 0 apprentice (electrical)	1
Lapan	0 foreman, 0 journeyman, 0 apprentice (mechanical)	0
Engineering Welding & Fabricating	0 iron workers, 0 operator (structural steel)	0
Outback Surveying	0 surveyors	0
Empire	1 foreman, 2 carpenters (framing)	3
John Oliveira & Sons	2 concrete formers	2
Commercial Masonry	1 foreman, 2 bricklayers (masonry)	3
Total Workforce		10

Miscellaneous Others		
CHA	Alyssa Chatani	1
Town of Carver	Bill Harriman, Dave Siedentopf	2
Total Misc. Workforce		3

Construction Activity:

Dig It: Not on site.

S&S Concrete Forms: Not on site.

Commercial Masonry: Continued installation of CMU block at Sally Port.

Delta: Not on site.

American Electrical: Worked on tying in electrical conduit to door frames.

Empire: Completed wood blocking on steel beams.

Lapan: Not on site.

Engineering Welding and Fabricating: Not on site.

Outback Surveying: Not on site.

John Oliveira & Sons: Removing forms from the sidewalk.

Clerk's remarks: none

Site Visitors/Meetings: Bill, Dave S.

Deliveries: none

Equipment Used: Empire: (2) Boom Lift 600s

PROJECT: Carver Police Station	PROJECT #:	Report Number: 89
---------------------------------------	-------------------	--------------------------

Contract Time:	Date: 6-16-2020	
Days Elapsed:	Day: Tuesday	
Extensions:	Weather: Sunny	
Days Remaining:	Temperature Cycle at 7 AM: 47 – 72 deg.	
Site Condition:	Dry	

Contractor	Workforce	
Tower Construction	1 Superintendent, 0 laborer – Kevin Thompson (site supervision)	1
Dig It	0 operator, 0 laborers, 0 foreman (sitework)	0
S&S Concrete Forms	0 carpenter, 0 laborers, 0 ironworker, 0 operator (formwork)	0
Delta	0 sprinkler fitters (fire protection)	0
American Electrical	1 foreman, 0 journeyman, 0 apprentice (electrical)	1
Lapan	0 foreman, 0 journeyman, 0 apprentice (mechanical)	0
Engineering Welding & Fabricating	0 iron workers, 0 operator (structural steel)	0
Outback Surveying	0 surveyors	0
Empire	0 foreman, 0 carpenters (framing)	0
John Oliveira & Sons	0 concrete formers	0
Commercial Masonry	1 foreman, 2 bricklayers (masonry)	3
G&H	1 foreman (HVAC)	1
	Total Workforce	6

Miscellaneous Others		
CHA	Alyssa Chatani	1
AEC	Dawn	1
Briggs	1 rep.	1
Lapan	Mike	1
National Lumber	1 rep.	1
	Total Misc. Workforce	5

Construction Activity:

Dig It: Not on site.

S&S Concrete Forms: Not on site.

Commercial Masonry: Continued installation of CMU block at Sally Port.

G&H: Began control wiring.

Delta: Not on site.

American Electrical: Continuing conduit in the masonry wall.

Empire: Not on site.

Lapan: Rep on site to review status of work.

Engineering Welding and Fabricating: Not on site.

John Oliveira & Sons: Not on site.

Clerk's remarks: Briggs picked up samples. National Lumber on site to review shop drawings.

Site Visitors/Meetings: See above.

Deliveries: none

Equipment Used: Empire: (2) Boom Lift 600s

PROJECT: Carver Police Station	PROJECT #:	Report Number: 90
---------------------------------------	-------------------	--------------------------

Contract Time:	Date: 6-17-2020	
Days Elapsed:	Day: Wednesday	
Extensions:	Weather: Sunny	
Days Remaining:	Temperature Cycle at 7 AM: 50 – 76 deg.	
Site Condition:	Dry	

Contractor	Workforce	
Tower Construction	1 Superintendent, 0 laborer – Kevin Thompson (site supervision)	1
Dig It	1 operator, 2 laborers, 0 foreman (sitework)	3
S&S Concrete Forms	0 carpenter, 0 laborers, 0 ironworker, 0 operator (formwork)	0
Delta	0 sprinkler fitters (fire protection)	0
American Electrical	1 foreman, 0 journeyman, 0 apprentice (electrical)	1
Lapan	0 foreman, 0 journeyman, 0 apprentice (mechanical)	0
Engineering Welding & Fabricating	0 iron workers, 0 operator (structural steel)	0
Outback Surveying	0 surveyors	0
Empire	0 foreman, 0 carpenters (framing)	0
John Oliveira & Sons	0 concrete formers	0
Commercial Masonry	1 foreman, 2 bricklayers (masonry)	3
G&H	0 foreman (HVAC)	0
Barber Drywall	1 foreman, 2 carpenters	3
	Total Workforce	11

Miscellaneous Others		
CHA	Alyssa Chatani	1
Town of Carver	Bill Harriman, Chief Duphily, Rick LaFond, Dave S.	4
Tower Construction	Patrick Fitzgerald	1
	Total Misc. Workforce	6

Construction Activity:

Dig It: Began filling loam at curbing and compacting.

S&S Concrete Forms: Not on site.

Commercial Masonry: Continued installation of CMU block at Sally Port.

G&H: Not on site.

Barber: Began exterior cold metal framing.

Delta: Not on site.

American Electrical: Continuing the conduit in the masonry.

Empire: Not on site.

Lapan: Not on site.

Engineering Welding and Fabricating: Not on site.

John Oliveira & Sons: Not on site.

Clerk's remarks: none

Site Visitors/Meetings: See above, Weekly Construction Meeting

Deliveries: 2 scissor lifts, dumpster swapped

Equipment Used: Empire: (2) Boom Lift 600s, Barber (2) Scissor Lift, Commercial: Lull 944E, Mini Bobcat

PROJECT: Carver Police Station	PROJECT #:	Report Number: 91
---------------------------------------	-------------------	--------------------------

Contract Time:	Date: 6-18-2020	
Days Elapsed:	Day: Thursday	
Extensions:	Weather: Sunny	
Days Remaining:	Temperature Cycle at 7 AM: 58 – 82 deg.	
Site Condition:	Dry	

Contractor	Workforce	
Tower Construction	1 Superintendent, 0 laborer – Kevin Thompson (site supervision)	1
Dig It	1 operator, 2 laborers, 0 foreman (sitework)	3
S&S Concrete Forms	0 carpenter, 0 laborers, 0 ironworker, 0 operator (formwork)	0
Delta	0 sprinkler fitters (fire protection)	0
American Electrical	1 foreman, 0 journeyman, 0 apprentice (electrical)	1
Lapan	0 foreman, 0 journeyman, 0 apprentice (mechanical)	0
Engineering Welding & Fabricating	0 iron workers, 0 operator (structural steel)	0
Outback Surveying	0 surveyors	0
Empire	0 foreman, 0 carpenters (framing)	0
John Oliveira & Sons	0 concrete formers	0
Commercial Masonry	1 foreman, 2 bricklayers (masonry)	3
G&H	0 foreman (HVAC)	0
Barber Drywall	1 foreman, 2 carpenters	3
	Total Workforce	11

Miscellaneous Others		
CHA	Alyssa Chatani	1
Town of Carver	Bill Harriman, Dave S.	2
	Total Misc. Workforce	3

Construction Activity:

Dig It: Continued filling loam at curbing and compacting.

S&S Concrete Forms: Not on site.

Commercial Masonry: Continued installation of CMU block at Sally Port and began forming cell block.

G&H: Not on site.

Barber: Continued cold metal framing and laying down membrane flashing.

Delta: Not on site.

American Electrical: Continuing conduit in the masonry wall.

Empire: Not on site.

Lapan: Not on site.

Engineering Welding and Fabricating: Not on site.

John Oliveira & Sons: Not on site.

Clerk's remarks: none

Site Visitors/Meetings: Bill Harriman, Dave S.

Deliveries: TGIs, (5) detention frames

Equipment Used: Empire: (2) Boom Lift 600s, Barber (2) Scissor Lift, Commercial: Lull 944E, Mini Bobcat

PROJECT: Carver Police Station	PROJECT #:	Report Number: 92
---------------------------------------	-------------------	--------------------------

Contract Time:	Date: 6-19-2020	
Days Elapsed:	Day: Friday	
Extensions:	Weather: Sunny	
Days Remaining:	Temperature Cycle at 7 AM: 63 – 84 deg.	
Site Condition:	Dry	

Contractor	Workforce	
Tower Construction	1 Superintendent, 0 laborer – Kevin Thompson (site supervision)	1
Dig It	0 operator, 0 laborers, 0 foreman (sitework)	0
S&S Concrete Forms	0 carpenter, 0 laborers, 0 ironworker, 0 operator (formwork)	0
Delta	0 sprinkler fitters (fire protection)	0
American Electrical	1 foreman, 0 journeyman, 0 apprentice (electrical)	1
Lapan	0 foreman, 0 journeyman, 0 apprentice (mechanical)	0
Engineering Welding & Fabricating	0 iron workers, 0 operator (structural steel)	0
Outback Surveying	0 surveyors	0
Empire	1 foreman, 2 carpenters (framing)	3
John Oliveira & Sons	0 concrete formers	0
Commercial Masonry	1 foreman, 2 bricklayers (masonry)	3
G&H	0 foreman (HVAC)	0
Barber Drywall	1 foreman, 2 carpenters (exterior framing)	3
	Total Workforce	11

Miscellaneous Others		
CHA	Alyssa Chatani	1
Lapan	Mike	1
G&H	Gary	1
Barber	Jay	1
Town of Carver	Dave S.	1
	Total Misc. Workforce	5

Construction Activity:

Dig It: Not on site.

Commercial Masonry: Continued installation of CMU block at Sally Port and continued forming cell block.

G&H: Not on site.

Barber: Continued cold metal framing and laying down membrane flashing.

Delta: Not on site.

American Electrical: Not on site.

Empire: Began installing joists at roofing across Sally Port.

Lapan: Not on site.

Engineering Welding and Fabricating: Not on site.

John Oliveira & Sons: Not on site.

Clerk's remarks: none

Site Visitors/Meetings: See above.

Deliveries: none

Equipment Used: Empire: (2) Boom Lift 600s, Barber (2) Scissor Lift, Commercial: Lull 944E, Mini Bobcat



**ON-SITE REPRESENTATIVE
DAILY REPORT**

PROJECT: Carver Police Station	PROJECT #:	Report Number: 93
---------------------------------------	-------------------	--------------------------

Contract Time:	Date: 6-22-2020	
Days Elapsed:	Day: Monday	
Extensions:	Weather: Sunny	
Days Remaining:	Temperature Cycle at 7 AM: 66 – 73 deg.	
Site Condition:	Dry	

Contractor	Workforce	
Tower Construction	1 Superintendent, 0 laborer – Kevin Thompson (site supervision)	1
Dig It	0 operator, 0 laborers, 0 foreman (sitework)	0
S&S Concrete Forms	0 carpenter, 0 laborers, 0 ironworker, 0 operator (formwork)	0
Delta	0 sprinkler fitters (fire protection)	0
American Electrical	1 foreman, 0 journeyman, 0 apprentice (electrical)	1
Lapan	0 foreman, 0 journeyman, 0 apprentice (mechanical)	0
Engineering Welding & Fabricating	0 iron workers, 0 operator (structural steel)	0
Outback Surveying	0 surveyors	0
Empire	0 foreman, 0 carpenters (framing)	0
John Oliveira & Sons	0 concrete formers	0
Commercial Masonry	1 foreman, 1 bricklayers (masonry)	2
G&H	0 foreman (HVAC)	0
Barber Drywall	1 foreman, 2 carpenters (exterior framing)	3
	Total Workforce	7

Miscellaneous Others		
CHA	Alyssa Chatani	1
Town of Carver	Bill Harriman	1
United Rental	1 rep.	1
	Total Misc. Workforce	3

Construction Activity:

Dig It: Not on site.

Commercial Masonry: Continued installation of CMU block at Sally Port and continued forming cell blocks.

G&H: Not on site.

Barber: Continued cold metal framing and laying down membrane flashing.

Delta: Not on site.

American Electrical: Not on site.

Empire: Not on site.

Lapan: Not on site.

Engineering Welding and Fabricating: Not on site.

John Oliveira & Sons: Not on site.

Clerk's remarks: none

Site Visitors/Meetings: See above.

Deliveries: Hunter Panels

Equipment Used: Empire: (2) Boom Lift 600s, Barber (2) Scissor Lift, Commercial: Lull 944E, Mini Bobcat

PROJECT: Carver Police Station	PROJECT #:	Report Number: 94
---------------------------------------	-------------------	--------------------------

Contract Time:	Date: 6-23-2020	
Days Elapsed:	Day: Tuesday	
Extensions:	Weather: Sunny	
Days Remaining:	Temperature Cycle at 7 AM: 65 – 84 deg.	
Site Condition:	Dry	

Contractor	Workforce	
Tower Construction	1 Superintendent, 0 laborer – Kevin Thompson (site supervision)	1
Dig It	0 operator, 0 laborers, 0 foreman (sitework)	0
S&S Concrete Forms	0 carpenter, 0 laborers, 0 ironworker, 0 operator (formwork)	0
Delta	0 sprinkler fitters (fire protection)	0
American Electrical	1 foreman, 0 journeyman, 0 apprentice (electrical)	1
Lapan	1 foreman, 0 journeyman, 0 apprentice (mechanical)	0
Engineering Welding & Fabricating	0 iron workers, 0 operator (structural steel)	0
Outback Surveying	0 surveyors	0
Empire	1 foreman, 2 carpenters (framing)	3
John Oliveira & Sons	0 concrete formers	0
Commercial Masonry	1 foreman, 3 bricklayers, 1 tender (masonry)	5
G&H	0 foreman (HVAC)	0
Barber Drywall	1 foreman, 2 carpenters (exterior framing)	3
	Total Workforce	13

Miscellaneous Others		
CHA	Alyssa Chatani	1
Town of Carver	Bill Harriman	1
AEC	Dawn	1
	Total Misc. Workforce	3

Construction Activity:

Dig It: Not on site.

Commercial Masonry: Continued installation of CMU block at Sally Port and continued forming cell blocks.

G&H: Not on site.

Barber: Continued cold metal framing and laying down membrane flashing.

Delta: Not on site.

American Electrical: Not on site.

Empire: Began installing trusses on the roof.

Lapan: Checking measurements and laying out piping at Sally Port.

Engineering Welding and Fabricating: Not on site.

John Oliveira & Sons: Not on site.

Clerk's remarks: none

Site Visitors/Meetings: See above.

Deliveries: Truss delivery

Equipment Used: Empire: (2) Boom Lift 600s, Barber (2) Scissor Lift, Commercial: Lull 944E, Mini Bobcat

PROJECT: Carver Police Station	PROJECT #:	Report Number: 95
---------------------------------------	-------------------	--------------------------

Contract Time:	Date: 6-24-2020	
Days Elapsed:	Day: Wednesday	
Extensions:	Weather: Sunny	
Days Remaining:	Temperature Cycle at 7 AM:	67 – 81 deg.
Site Condition:	Dry	

Contractor	Workforce	
Tower Construction	1 Superintendent, 0 laborer – Kevin Thompson (site supervision)	1
Dig It	0 operator, 0 laborers, 0 foreman (sitework)	0
S&S Concrete Forms	0 carpenter, 0 laborers, 0 ironworker, 0 operator (formwork)	0
Delta	0 sprinkler fitters (fire protection)	0
American Electrical	1 foreman, 0 journeyman, 0 apprentice (electrical)	1
Lapan	1 foreman, 0 journeyman, 0 apprentice (mechanical)	0
Engineering Welding & Fabricating	0 iron workers, 0 operator (structural steel)	0
Outback Surveying	0 surveyors	0
Empire	1 foreman, 5 carpenters (framing)	6
John Oliveira & Sons	2 concrete formers	2
Commercial Masonry	1 foreman, 2 bricklayers, 0 tender (masonry)	3
G&H	0 foreman (HVAC)	0
Barber Drywall	1 foreman, 2 carpenters (exterior framing)	3
	Total Workforce	16

Miscellaneous Others		
CHA	Alyssa Chatani, Joe Sullivan	2
Town of Carver	Bill Harriman, Dave S., Chief Duphily, Dave R., Rick LaFond	5
AEC	Dawn	1
	Total Misc. Workforce	8

Construction Activity:

Dig It: Not on site.

Commercial Masonry: Continued installation of CMU block at Sally Port and continued forming cell blocks.

G&H: Not on site.

Barber: Continued cold metal framing and laying down membrane flashing.

Delta: Not on site.

American Electrical: Installing conduit in the Sally Port.

Empire: Continued trusses on the roof.

Lapan: Not on site.

Engineering Welding and Fabricating: Not on site.

John Oliveira & Sons: Not on site.

Clerk's remarks: none

Site Visitors/Meetings: See above.

Deliveries: none

Equipment Used: Empire: (2) Boom Lift 600s, Barber (2) Scissor Lift, Commercial: Lull 944E, Mini Bobcat



**ON-SITE REPRESENTATIVE
DAILY REPORT**

PROJECT: Carver Police Station	PROJECT #:	Report Number: 96
---------------------------------------	-------------------	--------------------------

Contract Time:	Date: 6-25-2020	
Days Elapsed:	Day: Thursday	
Extensions:	Weather: Sunny	
Days Remaining:	Temperature Cycle at 7 AM: 61 – 85 deg.	
Site Condition:	Dry	

Contractor	Workforce	
Tower Construction	1 Superintendent, 0 laborer – Kevin Thompson (site supervision)	1
Dig It	0 operator, 0 laborers, 0 foreman (sitework)	0
S&S Concrete Forms	0 carpenter, 0 laborers, 0 ironworker, 0 operator (formwork)	0
Delta	0 sprinkler fitters (fire protection)	0
American Electrical	1 foreman, 0 journeyman, 0 apprentice (electrical)	1
Lapan	0 foreman, 0 journeyman, 0 apprentice (mechanical)	0
Engineering Welding & Fabricating	0 iron workers, 0 operator (structural steel)	0
Outback Surveying	0 surveyors	0
Empire	1 foreman, 5 carpenters (framing)	6
John Oliveira & Sons	0 concrete formers	0
Commercial Masonry	1 foreman, 4 bricklayers, 0 tender (masonry)	3
G&H	0 foreman (HVAC)	0
Barber Drywall	1 foreman, 2 carpenters (exterior framing)	3
	Total Workforce	14

Miscellaneous Others		
CHA	Alyssa Chatani	1
Town of Carver	Bill Harriman	1
AEC	Dawn	1
	Total Misc. Workforce	3

Construction Activity:

Dig It: Not on site.

Commercial Masonry: Continued installation of CMU block at intermediate block wall Sally Port.

G&H: Not on site.

Barber: Continued cold metal framing and laying down membrane flashing at Training Room.

Delta: Not on site.

American Electrical: Installing conduit at the masonry wall.

Empire: Continued trusses on the roof.

Lapan: Not on site.

Engineering Welding and Fabricating: Not on site.

John Oliveira & Sons: Not on site.

Clerk's remarks: none

Site Visitors/Meetings: See above.

Deliveries: Truss delivery

Equipment Used: Empire: (2) Boom Lift 600s, Barber (2) Scissor Lift, Commercial: Lull 944E, Mini Bobcat

PROJECT: Carver Police Station	PROJECT #:	Report Number: 97
---------------------------------------	-------------------	--------------------------

Contract Time:	Date: 6-26-2020	
Days Elapsed:	Day: Friday	
Extensions:	Weather: Sunny	
Days Remaining:	Temperature Cycle at 7 AM:	62 – 81 deg.
Site Condition:	Dry	

Contractor	Workforce	
Tower Construction	1 Superintendent, 0 laborer – Kevin Thompson (site supervision)	1
Dig It	0 operator, 0 laborers, 0 foreman (sitework)	0
S&S Concrete Forms	0 carpenter, 0 laborers, 0 ironworker, 0 operator (formwork)	0
Delta	0 sprinkler fitters (fire protection)	0
American Electrical	1 foreman, 0 journeyman, 0 apprentice (electrical)	1
Lapan	0 foreman, 0 journeyman, 0 apprentice (mechanical)	0
Engineering Welding & Fabricating	0 iron workers, 0 operator (structural steel)	0
Outback Surveying	0 surveyors	0
Empire	1 foreman, 5 carpenters (framing)	6
John Oliveira & Sons	0 concrete formers	0
Commercial Masonry	1 foreman, 3 bricklayers, 0 tender (masonry)	4
G&H	0 foreman (HVAC)	0
Barber Drywall	1 foreman, 2 carpenters (exterior framing)	3
	Total Workforce	15

Miscellaneous Others		
CHA	Alyssa Chatani	1
Town of Carver	Bill Harriman, Dave S.	2
Briggs	Janice	1
	Total Misc. Workforce	4

Construction Activity:

Dig It: Not on site.

Commercial Masonry: Continued installation of CMU block at intermediate block wall Sally Port.

G&H: Not on site.

Barber: Continued cold metal framing and wood bracing.

Delta: Not on site.

American Electrical: Installing conduit at the masonry wall.

Empire: Continued trusses on the roof.

Lapan: Not on site.

Engineering Welding and Fabricating: Not on site.

John Oliveira & Sons: Not on site.

Clerk's remarks: none

Site Visitors/Meetings: See above.

Deliveries: Truss delivery, sand delivery

Equipment Used: Empire: (2) Boom Lift 600s, Barber (2) Scissor Lift, Commercial: Lull 944E, Mini Bobcat
