

Carver Police Station Carver, MA

MONTHLY PROGRESS REPORT December 2020



Architect:



Jacunski Humes Architects, LLC

General Contractor:



Tower Construction Corp.

Owner's Project Manager:



prepared by:
Daedalus Projects, Inc.

PROJECT

Carver Police Station

PROJECT MANAGER

Joe Sullivan

CONTRACTOR

Tower Construction

ON SITE REPRESENTATIVE

Alyssa Chatani

MONTHLY PROGRESS REPORT – DECEMBER 2020**GENERAL COMMENTARY OF MONTHLY PROGRESS**

During the month of December, sitework continued with Dig It spreading loam, installing the wood guardrail, placing fill inside impound area and setting precast curbing around the impound lot area. They finished installing the remaining curbing and removed both trailers from the site. Hastie Fence installed the permanent fence on the site. John Oliveira & Sons removed concrete forms from the sidewalks. T&C Woodworking continued trim in the training room, placed the countertops inside of dispatch area and fastened the cabinets. They continued to install the baseboard and wainscoting in the training room. Barber Drywall continued misc. items such as boarding and taping the outbuilding ceilings and walls at the fitness room, finishing the attic access area and installing the door frame at the attic. They also taped the dispatch area and touched up the bathroom walls. Dandis Painting continued with painting doors and frames at the sally port, exterior door frames at the outbuilding, the remaining exterior columns, and various door frames in the main building. They continued with painting window trim, detention areas, and the corridor. They primed the fitness room, training room, and fire pump room. A/C Painting installed the wallcovering at the corridor and the conference room. Empire finalized the fiberglass columns at the exterior. Belcour finished the copper cupola and installed the boots at the sally port roof. Tower installed curb forms for boot wash and applied sealant on columns. They also installed doors inside detention area, sally port and attic areas. Debrino sealed the overhead door trim, window casings, cell areas and exterior trim. Hareld Glass continued placing glass inside storefront doors and continued associated caulking. They also placed the glass at the aluminum door frames. Central Ceilings installed drop ceiling grid in the dispatch room and completed the lighting tie in. Next Generation Doors installed the overhead door at the outbuilding. CJM Services completed the communication room flooring, and other various resilient flooring locations. Capital continued ceramic tile at the lobby, training room, and men's and women's locker rooms. New England Floors began prepping the detention area floors for epoxy. Quality Insulation completed the insulation at the attic. American Electrical continued lighting, wiring, and installing fire alarm devices and wiring. G&H continued installing RGDs, placing ductwork connections in the grills and diffusers, set the last exterior HVAC unit (heat pump) on the exterior pad and finished outbuilding ductwork and sally port existing louver connections. Delta continued connecting sprinkler piping in fire pump room, sprinkler heads in detention area and installed fire pump equipment inside of the outbuilding fire pump room. They also set sprinkler heads inside of the ceiling grid. The Town's building inspector was on site for a walk-through and noted no issues. New Era was on site pulling access control wiring into the communications room and installed the back box for the intercom at the lobby. All activities are outlined below.

HOT ITEMS

Above ceiling inspections were completed this month by BER.
The Select Board walked through the building on 12/16/2020.

SCHEDULE COMMENTARY

Tower Construction provided a master schedule with an occupancy date of March 8, 2021.

SAFETY COMPLIANCE

Ongoing safety walks are performed. No outstanding issues. Extra precautions are being taken due to COVID-19; a handwashing sink has been installed on site and all meetings are virtual. Tower Construction had a discussion with subcontractors on site on following safety protocol. They are each filling out a daily COVID-19 safety sheet. CHA is filling out daily health certifications as well.

DIVISION 06 – 06 - WOOD, PLASTICS, AND COMPOSITES**Section 06 10 53 Misc. Rough Carpentry, 06 40 23 Interior Architectural Woodwork**

Week of November 30

- Not on site.

Week of December 7

- Applying wood trim along windows in training room.

Week of December 14

- Continue trim in training room.
- Working on the bullnose trim in training room.

Week of December 21

- Placing trim along the training room at the wainscoting areas.
- Placing countertops inside of dispatch area and fastening to cabinets.
- Placing baseboard and wainscoting in training room.

Week of December 28

- Installing baseboard and window trim in the training room.
- Installing chair railing in corridor areas.
- Placing baseboard trim inside training storage room and cutting in sinks.

DIVISION 07 – ROOFING & SIDING**Section 07 40 00 Roofing and Siding**

Week of November 30

- Setting last fiberglass columns at the entry area.

Week of December 7

- Continue copper roofing at the cupola.
- Installed boots on sally port roof.

Week of December 14, 21, and 28

- Not on site.

DIVISION 09 – FINISHES**Section 09 12 00 Gypsum Board Assemblies, 09 30 00 Tiling, 09 91 00 Painting****Week of November 30**

- Topping the outbuilding ceiling and walls in the fitness room.
- Taping second coat in outbuilding and booking room inside.
- Taping the ceiling of the outbuilding and fitness walls.
- Applying sheet rock finishes at attic area and outbuilding.
- Taping attic sections and installing door frame in attic.
- Set up communication room flooring.
- Completed the installation of the communications room flooring.
- Setting flooring inside of room 150 and 151.
- Installing tile in main lobby area, and border tile in training room.
- Placing border tiles in lobby area and Men's Locker Room bathrooms.
- Finished men's locker room bathrooms at wet wall areas.
- Placing tile on the walls of the women's locker room and men's locker room.
- Installing floor tile in the lobby bathrooms.
- Continue painting door frames and doors in Sally Port.
- Painting exterior doors and frames at outbuilding.
- Painting second coat at exterior doors at the outbuilding.
- Priming and painting the last exterior columns at entry.
- Painting door frames at the main building and continue column painting.

Week of December 7

- Applying final coat of compound in outbuilding.
- Continue taping wallboard at attic area and locker rooms.
- Sanding sheet rock in the outbuilding and inside the attic access area.
- Continue setting tile at the armory floor.
- Sanding down flooring in the women's locker room.
- Continue tile at men's locker room wet walls.
- Installing wall tile in the bathroom #137.
- Placing tile flooring in the training room, finished tile in the bathroom #137.
- Continue installing border tile in training room.
- Continue tile in training room.
- Sanding and painting door frames in corridor and offices.
- Applying window trim paint at interior casework areas.
- Applied door frame paint in detention area and corridor.
- Applying primer and one coat of paint in interior column training room.
- Priming the fitness room in the outbuilding and continue door frames inside lobby.

Week of December 14

- Placing flooring in interview rooms and prepped locker area.
- Installing flooring at the locker room area.
- Installing floor covering.
- Continue training room tile.
- Installing tile in the men's locker room bathroom floor.
- Painting detention area and fitness room.
- Installed final coat of paint along ceiling grid and fitness room.

Week of December 21

- Placing compound in dispatch room and touching up bathrooms.
- Placing floor tile inside of men's locker room bathroom.
- Finishing up remaining floor tile in and around the columns.
- Installing tile flooring in women's locker room and grouting.
- Painting has installed another coat of painting on the detention area.
- Painting training room and around the columns.
- Finishing detention area paint, trim on windows.
- Priming in fire pump room, painted access to attic in the main building.

Week of December 28

- Continue ceramic tile in training room storage room and kitchenette and in men's toilet room.
- Grouting men's locker room and bathroom floor. Setting base tile.
- Finishing flooring in the training room storage room.
- Continue grouting bathroom floors off the corridor area.

DIVISION 21 – FIRE SUPPRESSION**Section 21 00 00 Fire Protection****Week of November 30**

- Continues to install sprinkler heads in detention area and installing piping.
- Continues to install fire suppression piping inside fire pump room.
- Installed fire pump equipment inside of the outbuilding pump room.
- Assembling piping and stands in the fire pump room at the outbuilding.

Week of December 7

- Not on site.

Week of December 14

- Continue firestopping above ceiling.

Week of December 21

- Installing heads inside of the detention room.
- Working on sprinkler head brackets inside main building.

Week of December 28

- Not on site.

DIVISION 22 – PLUMBING**Section 22 00 00 Plumbing**

Week of November 30

- Not on site.

Week of December 7

- Continue fire caulking.

Week of December 14

- Not on site.

Week of December 21

- Not on site.

Week of December 28

- Placing plumbing fixtures in bathrooms.

DIVISION 23 – HVAC**Section 23 00 00 HVAC**

Week of November 30 and December 7

- Not on site.

Week of December 14

- Laying out RGDs in offices.
- Installing grills and connecting ductwork at the RGDs.
- Installing diffusers in offices, connecting the ductwork to grilles.
- Continues to install RGDs in office and conference room.

Week of December 21

- Placing diffusers in ceiling grid in the conference room and chief's office.
- Installing return grills in office room, connecting ductwork to grid.
- Continue to place diffusers in the training room and the dentition areas.

Week of December 28

- Placing ductwork connections in the grills and diffusers.
- Set last exterior HVAC unit (heat pump) on the exterior pad.
- Finished outbuilding ductwork and sally port existing louver connections.

DIVISION 26 – ELECTRICAL**Section 26 00 00 Electrical****Week of November 30**

- Installing ceiling lights in offices and locker rooms.
- Installing grid lighting in Chief's office area and day room sections.
- Fire caulking above ceiling grid, installing lights in day room and locker rooms.
- Continues to install lights inside of the grid at office rooms.
- Placing light fixtures inside of ceiling grid.

Week of December 7

- Continues to install lighting in ceiling grid at bathrooms.
- Installing overhead lighting in corridor areas. Fire caulking above ceiling.
- Pulling secondary wiring into electrical room from new transformer.
- Continue fire caulking above the ceiling.
- Pulling secondary wiring from generator to transfer switched and from the transfer switch to the electrical room.
- Terminating secondary wiring in transfer junction box.
- Completed fire caulking in main building.
- Secured wire in sally port.

Week of December 14

- Installing feeder secondary wiring into main transfer switch.
- Continue the electrical secondary terminations in the electrical room panel.
- Wiring up breaker panels inside of electrical room, installing breaker.
- Wiring up overhead lighting in corridor and finishing up panels in electrical room.

Week of December 21

- Terminating wiring inside the electrical room panels and continue installing lights.
- Continue to terminate wiring inside of Comm. room.
- Working in communications room wiring, connections above panel.
- Installed UPS in the communications room and racks, installed lights in the outbuilding.

Week of December 28

- Continue working on lighting controls.
- Placing devices in the ceiling grid, and finishing light wiring.
- Installing fire alarm devices in the ceiling grid and at the outbuilding.
- Working on communication wiring in the communications room and devices in the lobby area.

DIVISION 31 – EARTHWORK**Section 31 20 00 Earth Moving**

Week of November 30

- Not on site.

Week of December 7

- Installing rain leader catch basin in the front of the building. Continue to spread loam.

Week of December 14

- Assist with the placement of the wood guardrail.

Week of December 21

- Removing snow and placing fill inside impound area.
- Setting precast curbing around the impound lot area.

Week of December 28

- Continue spreading loam.
- Installing the remaining curbing next to sally port.
- Placing concrete around curbing and cleaning up the site.
- Placing concrete around existing curbing along the front of the parking lot.




Copper Roof



Heat Pumps




Training Room

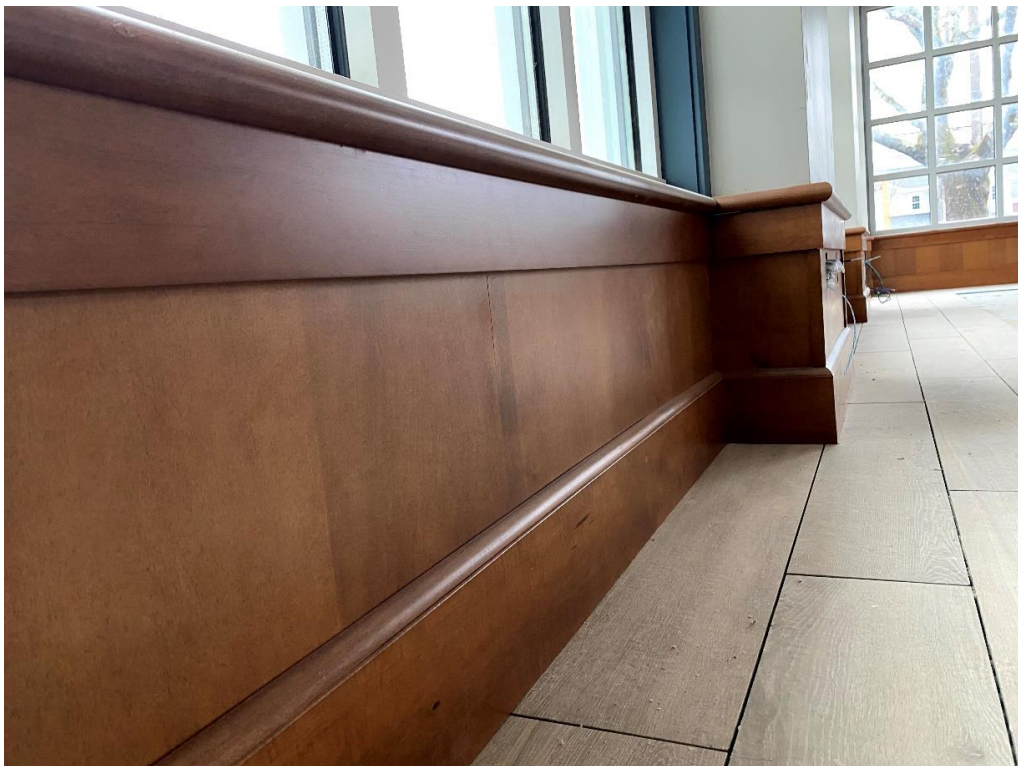


Millwork Continues



Dispatch Lockers

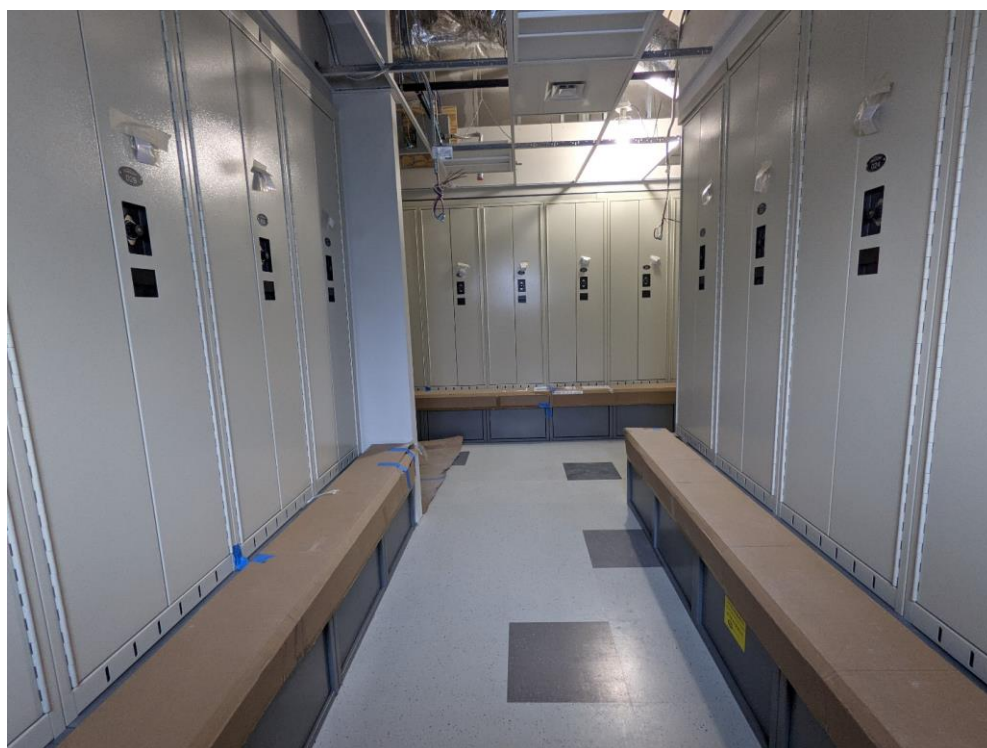

Men's Locker Room

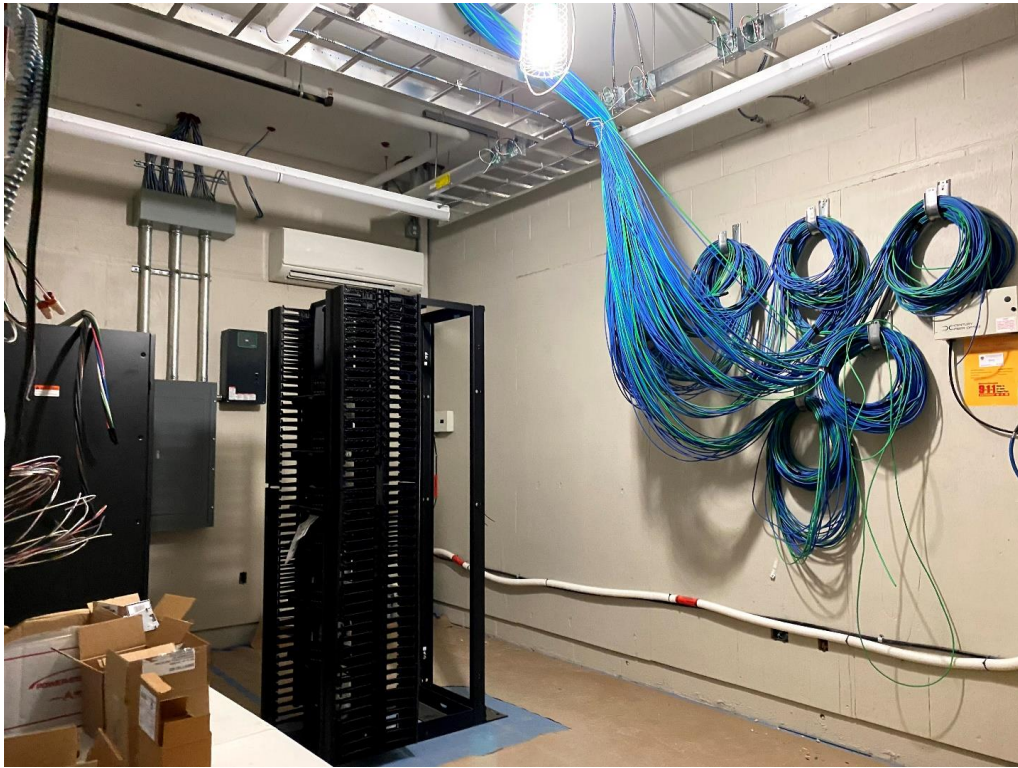


Communications Room



Ceiling Grid Completed



Resilient Flooring

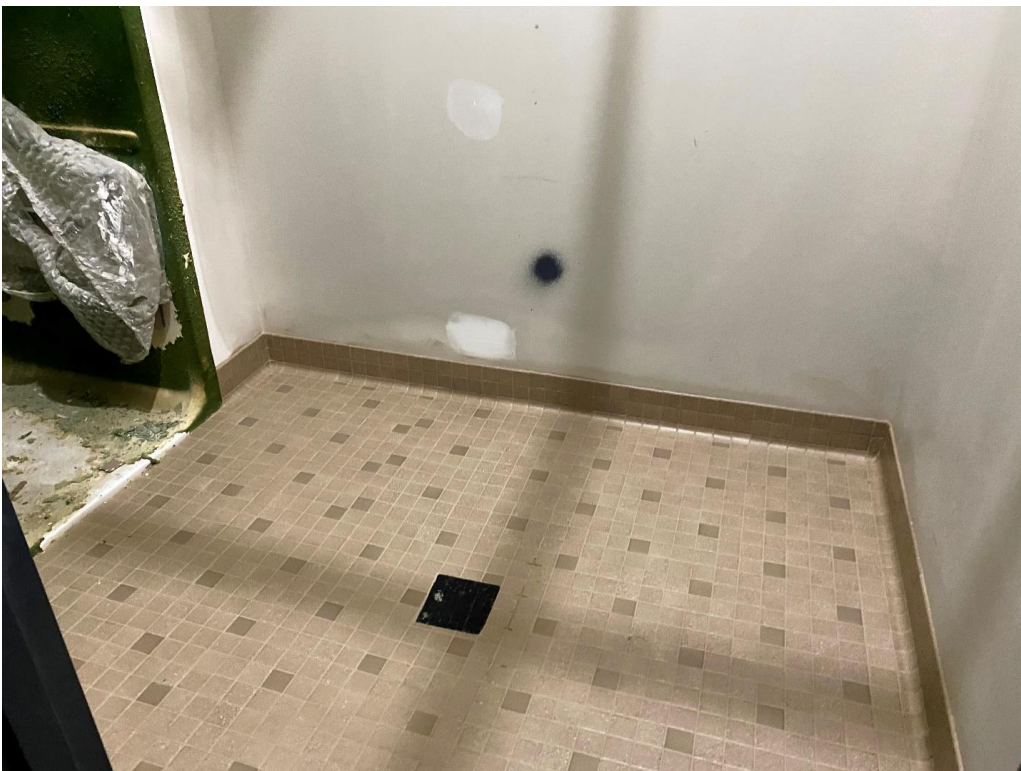

Ceramic Flooring

Carver Police Department

12.02.20

3 WEEK LOOK AHEAD SCHEDULE

	December																					
DATE	29	30	1	2	3	4	5	6	7	8	9	10	11	12	13	14	15	16	17	18	19	COMMENTS
Wallboard finishes		x	x	x	x	x																Barber
Roofing -Cupola										x	x	x	x			x						Belcour Roofing
Fiberglass Columns / Trim		x	x	x																		Empire
Storefront Frames/Glass			x																			Hareld Glass
Interior door frame paint											x	x	x			x	x					Dandis Painting
Interior Electrical		x	x	x	x	x			x	x	x	x	x			x	x	x	x	x		American
Interior wall / floor tile		x	x	x	x	x			x	x	x	x	x			x	x	x	x	x		Capital
Exterior column painting /overhangs					x	x			x													Dandis Painting
Outbuilding grid ceiling / dispatch													x			x	x					Central Ceilings
Casework / Millwork				x	x	x			x	x	x	x	x			x	x	x	x	x		T & C woodworking
Resilant Flooring					x	x			x	x												CJM Services
Site Fire Protection		x	x	x	x	x			x	x	x	x	x			x	x					Delta
Exterior Fencing																						Hastie Fence
HVAC Outbuilding / Main																x	x	x	x	x		G & H HVAC
Main Building Attic Insulation												x	x			x						Quality Insulation
Overhead door Outbuilding/Grille												x	x			x						Next Gen.
Outbuilding Painting / doors				x	x	x							x			x	x					Dandis Painting
Site work loom / Curbing			x						x	x	x	x	x			x	x					Dig-it
Safety		x	x	x	x	x			x	x	x	x	x			x	x	x	x	x		All trades

Carver Police Department

12.16.20

3 WEEK LOOK AHEAD SCHEDULE

	December																						
DATE	13	14	15	16	17	18	19	20	21	22	23	24	25	26	27	28	29	30	31	1	2	COMMENTS	
Wallboard finishes / touch-ups						x																Barber Drywall	
Locker Installation				x		x																Tifton lockers	
Ceiling Tile boarders						x			x	x	x											Central Ceilings	
Interior Glass																	x	x				Hareld Glass	
Interior door frame paint		x	x						x	x												Dandis Painting	
Interior Electrical / terminations		x	x	x		x			x	x	x					x	x	x				American	
Interior wall / floor tile		x	x	x		x			x	x	x					x	x	x				Capital	
Downspouts / Transitions									x	x	x											Belcour	
Outbuilding grid ceiling						x																Central Ceilings	
Casework / Millwork		x		x		x			x	x	x					x	x	x				T & C woodworking	
Bathroom accessories																	x	x				Tower Con.	
Site Fire Protection									x	x	x					x	x	x				Delta	
Exterior Fencing			x	x		x			x	x	x					x	x	x				Hastie Fence	
HVAC Outbuilding																	x	x				G & H HVAC	
Main Building Attic Insulation		x	x																			Quality Insulation	
Overhead door Outbuilding/Grille										x	x											Next Gen.	
Outbuilding interior painting										x	x											Dandis Painting	
Site work loom / Curbing			x						x	x	x					x	x	x				Dig-it	
Secondary Power Inspection						x																Carver / Eversource	
Safety		x	x	x	x	x			x	x	x	x	x			x	x	x	x	x		All trades	


Carver Police Department

12.30.20

3 WEEK LOOK AHEAD SCHEDULE

DATE	December					January																COMMENTS
	27	28	29	30	31	1	2	3	4	5	6	7	8	9	10	11	12	13	14	15	16	
Bathroom fixtures																			x	x		LaPan Plumbing
Ceiling Tile boarders		x	x						x	x	x	x	x									Central Ceilings
Epoxy Flooring				x	x													x	x			New England Floors
Interior finish paint												x	x			x	x	x	x	x		Dandis Painting
Interior Electrical / lighting		x	x	x	x				x	x	x	x	x			x	x	x	x	x		American
Interior wall / floor tile		x	x	x	x				x	x	x	x	x									Capital Flooring
Transitions / Downspouts		x								x	x	x										Belcour / TCC
Wall coverings											x	x	x			x	x	x	x			
Casework / Millwork		x	x	x	x				x	x	x	x	x			x	x	x				T & C woodworking
Bathroom accessories											x	x	x									Tower Con.
Site Fire Protection									x	x	x					x	x	x				Delta
Exterior Fencing		x	x	x	x				x	x	x											Hastie Fence
HVAC Installation / RGD's		x	x		x				x	x	x	x	x			x	x	x				G & H HVAC
Resiliant flooring										x	x	x										CJM
Overhead Grille door												x	x									Next Gen.
Outbuilding interior painting											x	x	x			x	x					Dandis Painting
Site work loom / Curbing		x	x	x	x																	Dig-it
Light pole Installation																x	x	x				American
Commissioning / Start-up																		x	x	x		HVAC / Comm. Agent
Safety		x	x	x	x				x	x	x	x	x			x	x	x	x	x		

Tower Construction
Change Proposal Log

				13-Jan-21	Open Change Proposals		
					Rejected Change Proposals		
					Approved Change Proposals		
CP#	CO#	Date	Description	CP Amount	Amount Approved	Amount Pending	Amount Not Approved
1		03.12.20	Fire Protection File Sub Award	\$ 91,092.02			\$ 91,092.02
1 Rev 1	1	03.16.20	Fire Protection File Sub Award	\$ 49,369.00	\$ 49,369.00		
2		04.07.20	ASI No. 001 - Fire Pump Modifications	\$ 284,304.41			\$ 284,304.41
2 Rev 1	2	04.12.20	ASI No. 001 - Fire Pump Modifications	\$ 273,320.55	\$273,320.55		
3	2	03.12.20	ASI No. 002 BDA Review	\$ (31,268.05)	\$ (31,268.05)		
4		03.12.20	ASI No. 003 - Main Circuit Breaker	\$ 3,067.04			\$ 3,067.04
4 Rev 1	2	04.07.20	ASI No. 003 - Main Circuit Breaker	\$ -	\$ -		
5		04.07.20	Alternate No. 001 - Out Building Construction	\$ 344,000.00			\$ 344,000.00
5 Rev 1	3	04.12.20	Alternate No. 001 - Out Building Construction	\$ 344,000.00	\$344,000.00		
6		03.18.20	Septic System	\$ 44,269.79			\$ 44,269.79
7		04.07.20	Unforeseen Old Foundation Removal	\$ 5,397.34			\$ 5,397.34
7 Rev 1	2	04.12.20	Unforeseen Old Foundation Removal	\$ 5,285.68	\$ 5,285.68		
8		04.07.20	ASI No. 006 - Genset AP	\$ 451.61			\$ 451.61
8 Rev 1	2	04.12.20	ASI No. 006 - Genset AP	\$ 431.08	\$ 431.08		
9		04.08.20	Unsuitable Materials	\$ 36,581.71			\$ 36,581.71
9 Rev 1		04.12.20	Unsuitable Materials	\$ 36,254.87			\$ 36,254.87
9 Rev 2	2	04.14.20	Unsuitable Materials	\$ 19,995.75	\$ 19,995.75		
10	4	04.22.20	ASI No. 008 DS-C Fixture	\$ 1,473.34	\$ 1,473.34		
11		04.22.20	ASI No. 009 Security Revisions	\$ 1,510.74			\$ 1,510.74
11 Rev 1	4	05.13.20	ASI No. 009 Security Revisions	\$ -	\$ -		
12	4	05.13.20	ASI No. 004 Mechanical Equipment Relocation	\$ -	\$ -		
13	4	05.13.20	ASI No. 007 Locker Electrical	\$ 677.88	\$ 677.88		
14	4	07.14.20	ASI No. 010 Wall Type Revision	\$ (964.92)	\$ (964.92)		
15		05.13.20	ASI No. 011 Fire Alarm Revisions	\$ -			\$ -
16	4	05.13.20	ASI No. 012 Door Leaf Type DL-A	\$ -	\$ -		
17		05.13.20	Delete UPS From Project Scope	\$ (30,207.60)			(\$30,207.60)
18		06.16.20	ASI No. 13 Fire Alarm Scope of Work Revisions	\$4,173.60			\$4,173.60
18 Rev 1	5	09.18.20	ASI # 13 R-1 Fire Alarm Revision	\$0.00	\$0.00		
19		08.12.20	ASI # 17 Framing Revision	\$4,361.01			\$4,361.01
19 Rev 1	5	09.18.20	ASI # 17 Framing Revision Revised	\$2,931.11	\$2,931.11		
20		07.30.20	ASI # 16 Library Curbing Replacemnet	\$18,312.71			\$ 18,312.71
20 Rev 1		08.24.20	ASI # 16 Library Curbing Replacemnet	\$14,652.30			\$14,652.30
20 Rev 2	5	09.18.20	ASI # 16 Library Curbing Replacemnet	\$11,161.35	\$11,161.35		
21	5	07.30.20	ASI # 15 Electrical Additions	\$2,975.19	\$2,975.19		
22	5	08.04.20	ASI # 21 CPT- 01 Attick Stock	\$2,076.15	\$2,076.15		
23	5	08.12.20	ASI # 18 Cupola roofing	\$3,264.00	\$3,264.00		
24			ASI # 26 Rear Gate Electrical Infrastructure	\$ 8,264.32			\$ 8,264.32
24 Rev 1	6	10.17.20	ASI # 26 Rear Gate Electrical Infrastructure	\$ 2,101.78	\$ 2,101.78		
25	5	09.19.20	ASI # 14 Aluminum Storefront Colors	\$ -	\$ -		
26	5	09.19.20	ASI # 19 Memorial Revision	\$ -	\$ -		
27	6	10.17.20	ASI # 20 E911 Power	\$ -	\$ -		
28	5	09/19.20	ASI # 22 Column Enclosure Dimensional Adjustment	\$ -	\$ -		
29	6	10.07.20	ASI # 23 Dispatch Casework	\$ -	\$ -		
30			ASI # 24 Fire Pump B02 Revision	\$ 1,934.92			\$ 1,934.92
30 Rev 1	6	11.18.2020	ASI # 24 Fire Pump B02 Revision	\$ 2,467.06	\$ 2,467.06		
31	5	09.19.20	ASI # 25 Dispatch Flooring Colors	\$ -	\$ -		
32	6	10.17.20	ASI # 27 TV Box Mounting Heights	\$ -	\$ -		
33	6	10.07.20	ASI # 28 Owner Requested Data and Power	\$ 1,823.64	\$ 1,823.64		
34	6	10.17.20	ASI # 29 Communication Rm 114 Coordination	\$ -	\$ -		
35	6	10.07.20	ASI # 30 Dispatch Area Revisions	\$ 508.72	\$ 508.72		
36	6	10.17.20	ASI # 31 and ASI # 32 Paint Clarifications	\$ -	\$ -		
37			ASI # 33 Additional Lockers				
37 Rev 1	6	11.11.2020	ASI # 33 Additional Lockers	\$ 28,459.60	\$ 28,459.60		
38		11.18.2020	ASI # 34 Condenser Relocation	\$ 2,886.59		\$ 2,886.59	
39		10.17.20	Cupola Lighting	\$ -	\$ -		
40	6	11.02.20	Lighting Protection	\$ 2,998.80	\$2,998.80		
41		11.10.20	Additional Painting at Metal Gooseneck Extension	\$ 3,925.22			\$3,925.22
42	6	11.11.2020	ASI # 21 CPT Attic Stock - Refund per Millwork	\$ (2,076.15)	\$ (2,076.15)		
43	6	11.18.2020	ASI # 35 Power for OH Door out Building	\$ 4,201.96	\$ 4,201.96		
44		12.0.2020	ASI No. 38	\$ 5,515.65	\$ 5,515.65		
45		12.17.2020	ASI No. 37 Guardrail Modification Lighting & Road Sign	\$ 7,990.61			\$ 7,990.61
46		12.17.2020	HVAC Corridor Diffuser Modifications	\$ 1,071.00	\$ 1,071.00		
47		12.18.2020	RFI No. 52 Fire Protection Manway Cover	\$ 2,865.02	\$ 2,865.02		
48		12.29.2020	Additional Flooring Scope for Evidence Track Room 129	\$ 976.75		\$976.75	
49		01.13.2021	Mirror in Fitness Room	\$ 2,805.00		\$2,805.00	
50		01.13.2021	Controls for Shades at Exterior Door	\$ 2,115.51		\$2,115.51	
51		01.13.2021	ASI 40 Fence Modifications	\$ 2,580.60		\$2,580.60	
			Totals		\$734,665.19	\$ 11,364.45	
					\$ 6,957,500.00		
1			CP 1 R1	\$ 49,369.00	\$ 7,006,869.00		
2			CP 2R1, 3, 4R1, 7R1, 8R1, 9R2	\$ 267,765.01	\$ 7,274,634.01		
3			CP 5R1	\$ 344,000.00	\$ 7,618,634.01		
4			CP 10, 11R1, 12, 13, 14, 16	\$ 1,186.30	\$ 7,619,820.31		
5			CP 18R1, 19R1, 20R2, 21, 22, 23, 25, 26, 28, 31	\$22,407.80	\$ 7,642,228.11		
6			CP 24R1, 27, 29, 30R1, 32, 33, 34, 35, 36, 37R1, 38, 39, 40, 42, 43	\$ 40,485.41	\$ 7,682,713.52		

SHOP DRAWING LOG

PROJECT: New Facility for the Carver Police Department, 3 Center Street, Carver, Massachusetts								STATE PROJECT No.:			
G.C.: Tower Construction Corporation								JHA PROJECT No.: 1830			
TEAM: JH Architects (JHA); Garcia-Galuska-DeSousa (GGD); Linden Landscape Architects (LLA); Szewczak Associates (SA); Paul Hawley Associates (PHA); CAMA (CAMA); Building Engineering Resources (BER)								G.C. PROJECT No.: 2252			
JHA SHOP DRAWING NUMBER	G.C. SHOP DRAWING NUMBER	DESCRIPTION <div> <div></div> = Reviewed & Returned <div></div> = Under JHA Review <div></div> = Under Consultant Review <div></div> = Under Owner Review <div></div> = Awaiting G.C. Response </div>	DATE REC'D - From - G.C.	DATE SENT - To - Owner	DATE REC'D - From - Owner	DATE SENT - To - Consult	DATE REC'D - From - Consult	DATE RTN'D - To - G.C.	REVIEWER	ACTION / REMARK	COMMENTS
DIVISION 0 - OWNER SUBMISSIONS											
DIVISION 1 - GENERAL REQUIREMENTS											
010000-001-1	-	Underslab Coordination Drawings	04/01/20	-	-	04/01/20	04/15/20	04/15/20	BER	AN	
011000-001-1	011000-01s	Carver Site Access Plan	01/29/20	01/29/20	02/20/20	01/29/20	01/29/20	02/20/20	ToC/LLA	AN	
011000-002-1	011000-02	Carver Police Schedule	02/19/20	-	-	-	-	02/27/20	JHA	A	
011000-003-1	011000-03	Above Slab Coordination Drawings	05/06/20	-	-	05/06/20	05/28/20	05/28/20	BER	A	
017700-001-1	017700-01	Septic As-Built's Stamped	09/03/20	-	-	09/03/20	09/15/20	09/15/20	GGD	A	
DIVISION 2 - EXISTING CONDITIONS											
DIVISION 3 - CONCRETE											
032004-001-1	032004-01	Rebar Shop Drawing	01/15/20	-	-	01/15/20	-	-	SA/LLA	-	Incorporated into 032004-001-2
032004-001-2	032004-02	Rebar Shop Drawing	01/22/20	-	-	01/28/20	02/05/20	02/05/20	SA/LLA	AC/RR	
032004-001-2	032004-02	Rebar Shop Drawing	-	-	-	-	-	04/03/20	SA/LLA	AC	Updated marks dated 2020-04-03
032004-001-3	032004-01 Rev2	Rebar Shop Drawing	03/03/20			04/03/20	04/03/20	04/03/20	SA	R	Re-design voided via negotiations
033004-001-1	033004-02s	Concrete Slab on Grade	02/19/20	-	-	02/19/20	02/24/20	02/24/20	SA	AC	
033004-002-1	033004-4s	Footings + Foundation Walls	02/19/20	-	-	02/19/20	02/24/20	02/24/20	SA	AC	
033004-002-2	033004-4s Rev 1	Footings + Foundation Walls	03/06/20	-	-	03/06/20	-	-	SA	-	Received For Record Only
033004-002-3	033004-4s Rev 2	Footings + Foundation Walls	03/10/20	-	-	03/10/20	03/19/20	03/19/20	SA	AC	
033004-003-1	033004-06s	Expansion Joint	03/05/20	-	-	03/06/20	03/13/20	03/13/20	SA	A	
033004-004-1	033004-07s	Non-Shrink Grout	03/05/20	-	-	03/06/20	03/13/20	03/13/20	SA	A	
033004-005-1	033004-08s	Stego Wrap Vapor Barrier 15 Mil	03/05/20	-	-	03/06/20	03/13/20	03/13/20	SA	A	
033004-006-1	033004-09s	Concrete Slab on Grade Layout	05/06/20	-	-	05/06/20	05/14/20	05/14/20	SA/JHA	AC	

SHOP DRAWING LOG

PROJECT: New Facility for the Carver Police Department, 3 Center Street, Carver, Massachusetts								STATE PROJECT No.:			
G.C.: Tower Construction Corporation								JHA PROJECT No.: 1830			
TEAM: JH Architects (JHA); Garcia-Galuska-DeSousa (GGD); Linden Landscape Architects (LLA); Szewczak Associates (SA); Paul Hawley Associates (PHA); CAMA (CAMA); Building Engineering Resources (BER)								G.C. PROJECT No.: 2252			
JHA SHOP DRAWING NUMBER	G.C. SHOP DRAWING NUMBER	DESCRIPTION <div> <div></div> = Reviewed & Returned <div></div> = Under JHA Review <div></div> = Under Consultant Review <div></div> = Under Owner Review <div></div> = Awaiting G.C. Response </div>	DATE REC'D - From - G.C.	DATE SENT - To - Owner	DATE REC'D - From - Owner	DATE SENT - To - Consult	DATE REC'D - From - Consult	DATE RTN'D - To - G.C.	REVIEWER	ACTION / REMARK	COMMENTS
DIVISION 4 - MASONRY											
042000-001-1	042000-01s	Unit Masonry	01/22/20	-	-	01/22/20	01/29/20	02/05/20	JHA	A	
042000-002-1	042000-02s	Masonry Reinforcement Shop Drawings	01/22/20	-	-	01/22/20	01/29/20	01/30/20	SA/JHA	AC	
042000-003-1	042000-03s	Precast Concrete Products	02/14/20	-	-	-	-	02/14/20	JHA	AC	
042000-004-1	042000-04s	Precast Concrete Profile	02/18/20	-	-	-	-	02/19/20	JHA	AC	
042000-005-1	042000-05s	Precast Concrete Color Samples	03/04/20	-	-	-	-	03/16/20	JHA	AC	Samples Received 3/12/20
DIVISION 5 - METALS											
051204-001-1	051204-01	Anchor Bolts Setting Plan & Details	01/15/20	-	-	01/15/20	01/29/20	01/29/20	SA	AC	
051204-002-1	051204-02s	Structural Steel Drawings	02/13/20	-	-	02/13/20	02/27/20	02/27/20	SA	RR	
051204-002-2	051204-02 Rev 1	Structural Steel Drawings	03/21/20	-	-	03/21/20	04/02/20	04/02/20	SA	A/AC	
055133-001-1	051204-03s	Ships Ladder	05/27/20	-	-	-	-	06/10/20	JHA	AC	
DIVISION 6 - WOOD & PLASTICS											
061000-001-1	061000-01s	Lumber	03/26/20	-	-	03/31/20	04/03/20	04/03/20	SA/JHA	AC/RR	
061000-001-2	061000-01s Rev 1	Lumber	04/08/20	-	-	-	-	04/08/20	JHA	-	Not accepted for review
061000-002-1	061000-01s	LVLs	04/10/20	-	-	04/10/20	04/20/20	04/21/20	SA	AC	
061000-003-1	061000-02s	Air Infiltration Barrier and Tape	04/10/20	-	-	-	-	04/15/20	SA/JHA	A	
061000-004-1	061000-03s	Construction Subfloor Adhesive	04/10/20	-	-	04/10/20	-	04/21/20	JHA	AC	
061000-005-1	061000-04s	Exterior Sheathing	04/10/20	-	-	04/10/20	04/20/20	04/21/20	SA	AC	
061000-006-1	061000-05s	Hunter Panels	04/10/20	-	-	-	-	04/15/20	SA/JHA	A	
061000-007-1	061000-06s	Self-Adhered Flashing	04/10/20	-	-	-	-	04/15/20	SA/JHA	R	
061000-007-2	061000-06s Rev 1	Self-Adhered Flashing	04/21/20	-	-	-	-	04/21/20	JHA	A	
061000-008-1	061000-07s	TJI	04/10/20	-	-	04/10/20	04/20/20	04/21/20	SA	AC/R	
061000-009-1	06100-08s	Framing Lumber Materials	04/10/20	-	-	04/10/20	04/20/20	04/21/20	SA	AC	
061000-010-1	061000-09	Soffit Vent	07/28/20	-	-	-	-	07/28/20	JHA	AC	
061754-001-1	061754-01s	Truss Shop Drawing	01/27/20	-	-	01/28/20	02/11/20	02/11/20	SA	RR	
061754-001-2	061754-01s Rev 1	Trusses	03/10/20	-	-	03/10/20	03/24/20	03/24/20	SA	AC	
061754-001-3	061754-01s Rev 2	Truss Seals	05/18/20	-	-	05/18/20	05/28/20	05/28/20	SA	AC	
061754-002-1	061754-02s	Outbuilding Truss SD	04/29/20	-	-	04/29/20	05/08/20	05/12/20	SA	AC	

SHOP DRAWING LOG

PROJECT: New Facility for the Carver Police Department, 3 Center Street, Carver, Massachusetts								STATE PROJECT No.:			
G.C.: Tower Construction Corporation								JHA PROJECT No.: 1830			
TEAM: JH Architects (JHA); Garcia-Galuska-DeSousa (GGD); Linden Landscape Architects (LLA); Szwczak Associates (SA); Paul Hawley Associates (PHA); CAMA (CAMA); Building Engineering Resources (BER)								G.C. PROJECT No.: 2252			
JHA SHOP DRAWING NUMBER	G.C. SHOP DRAWING NUMBER	DESCRIPTION <div> <div></div> = Reviewed & Returned <div></div> = Under JHA Review <div></div> = Under Consultant Review <div></div> = Under Owner Review <div></div> = Awaiting G.C. Response </div>	DATE REC'D - From - G.C.	DATE SENT - To - Owner	DATE REC'D - From - Owner	DATE SENT - To - Consult	DATE REC'D - From - Consult	DATE RTN'D - To - G.C.	REVIEWER	ACTION / REMARK	COMMENTS
064000-001-1	06400-01s	Fiberglass Column	06/10/20	-	-	-	-	06/12/20	JHA	A	
064400-001-1	064400-01s	Moldings and Decorative Millwork	05/06/20	-	-	-	-	05/15/20	JHA	AC	
064400-002-1	081400-02s	Ornamental Woodwork Stain Sample	11/10/20	-	-	-	-	11/10/20	JHA	-	PD & Town to review/approve
066000-001-1	06600-01s	PVC Trim	05/06/20	-	-	-	-	05/13/20	JHA	A	
DIVISION 7 - THERMAL & MOISTURE PROTECTION											
072100-001-1	033004-05s	Dow Insulation	03/05/20	-	-	-	-	03/15/20	JHA	A	
072100-002-1	033004-09s	Tuff II Coating	03/05/20	-	-	-	-	03/15/20	JHA	A	
072100-003-1	072100-01	Building Insulation	07/23/20	-	-	-	-	07/28/20	JHA	A/R	
073113-001-1	073113s	Asphalt Shingles	02/18/20	-	-	-	-	02/20/20	JHA	AC/RR/R	
073113-002-1	073113-25s	Color Samples & Color Chart	03/04/20	-	-	-	-	03/16/20	JHA	AC	Samples Received 3/12/20
073113-003-1	073113-26	Roof Hatch	07/23/20	-	-	-	-	07/24/20	JHA	A	
074600-001-1	074600-01s	NuCedar	04/10/20	-	-	-	-	04/16/20	JHA	AC/RR	
074600-002-1	074600-02	Siding Color Samples	05/07/20	05/20/20	05/20/20	-	-	05/27/20	JHA	AC	Samples Received 5/15/20
074646-001-1	074646-01s	Fiber Cement Siding	04/10/20	-	-	-	-	04/16/20	JHA	AC	
075323-001-1	075323-01s	Membrane Roofing	03/04/20	-	-	-	-	03/15/20	JHA	A/R	Only Flat Insulation Not Approved
075323-002-1	075323-02s	Metal Roofing	06/23/20	-	-	-	-	07/01/20	JHA	AC	
075323-003-1	075323-03s	Metal Roof Color Samples	07/07/20	-	-	-	-	08/07/20	JHA	R	
075323-004-1	075323-04	Substitution Request - Cupola Clips	10/07/20	-	-	-	-	10/07/20	JHA	AC	
079200-001-1	079200-01s	Elastomeric Joint Sealant	01/30/20	-	-	-	-	02/10/20	JHA	R	
079200-002-1	079200-02s	Sealant Color Chart	01/30/20	-	-	-	-	02/10/20	JHA	RR	
079200-003-1	079200-03s	Non-Sag Urethane Sealant	01/30/20	-	-	-	-	02/10/20	JHA	A	
079200-004-1	079200-04s	Acrylic-Emulsion Sealant and Color Chart	01/30/20	-	-	-	-	02/03/20	JHA	AC	
079200-005-1	079200-05s	Security Sealant	01/30/20	-	-	-	-	01/30/20	JHA	R	
079200-005-2	079200-05s Rev1	Security Sealant	02/07/20	-	-	-	-	02/07/20	JHA	A	
079200-006-1	079200-06s	Resilient Silicone Sealant	01/30/20	-	-	-	-	02/03/20	JHA	R	
DIVISION 8 - OPENINGS											
081113-001-1	081113-01	Door and Frame Schedule	04/13/20	-	-	-	-	04/16/20	JHA	AC	
081113-001-2	081113-03s Rev1	Door and Frame Schedule	05/01/20	-	-	-	-	-	JHA	-	Not Reviewed
081113-001-3	081113-03 Rev2	Steel Doors and Frames	08/03/20	-	-	-	-	08/05/20	JHA	R	

SHOP DRAWING LOG

PROJECT: New Facility for the Carver Police Department, 3 Center Street, Carver, Massachusetts								STATE PROJECT No.:			
G.C.: Tower Construction Corporation								JHA PROJECT No.: 1830			
TEAM: JH Architects (JHA); Garcia-Galuska-DeSousa (GGD); Linden Landscape Architects (LLA); Szewczak Associates (SA); Paul Hawley Associates (PHA); CAMA (CAMA); Building Engineering Resources (BER)								G.C. PROJECT No.: 2252			
JHA SHOP DRAWING NUMBER	G.C. SHOP DRAWING NUMBER	DESCRIPTION <div> <div></div> = Reviewed & Returned <div></div> = Under JHA Review <div></div> = Under Consultant Review <div></div> = Under Owner Review <div></div> = Awaiting G.C. Response </div>	DATE REC'D - From - G.C.	DATE SENT - To - Owner	DATE REC'D - From - Owner	DATE SENT - To - Consult	DATE REC'D - From - Consult	DATE RTN'D - To - G.C.	REVIEWER	ACTION / REMARK	COMMENTS
081113-002-1	081113-02	Door Frames	04/13/20	-	-	-	-	04/16/20	JHA	RR	
081113-002-2	081113-03s Rev1	Doors Frames	05/01/20	-	-	-	-	05/13/20	JHA	R	
081113-003-1	081113-03	Steel Doors	04/13/20	-	-	-	-	04/16/20	JHA	AC/RR/R	
081113-003-2	081113-03s Rev1	Steel Doors	05/01/20	-	-	-	-	05/13/20	JHA	A/R	
081400-001-1	081400-01	Wood Doors	04/13/20	-	-	-	-	04/16/20	JHA	AC	
083326-001-1	083616-03s	Shop Drawing and Product Data for Door 125C	04/10/20	-	-	-	-	04/16/20	JHA	AC	
083613-001-1	083613-01s	Shop Drawings for Doors 125B & 118B	03/06/20	-	-	-	-	03/16/20	JHA	AC	
083613-002-1	083616-02s	Product Data Overhead Doors 112B and 118B	04/10/20	-	-	-	-	04/16/20	JHA	AC	
083613-003-1	083616-04s	Motors	04/10/20	-	-	-	-	04/16/20	JHA	RR	
084113-001-1	088000-01s	Door & Frame Product Data	05/18/20	-	-	-	-	05/27/20	JHA	AC	
084113-002-1	084113-01s	Aluminum Entrances & Storefronts	05/28/20	-	-	-	-	06/12/20	JHA	AC/RR	
084113-003-1	084113-02s	Color Samples	06/04/20	-	-	-	-	06/15/20	JHA	AC	Cover sheet & Scan only
085400-001-1	085400-01s	Fiberglass Windows	03/06/20	-	-	-	-	03/15/20	JHA	AC	
085400-002-1	085400-01s	Fiberglass Windows Shop Drawings	04/01/20	-	-	-	-	04/02/20	JHA	AC	
087100-001-1	087100-01	Door Hardware Schedule	04/13/20	-	-	04/13/20	04/14/20	04/16/20	PHA/JHA	AN/RRfR	
087100-001-2	087100-01sRev1	Door Hardware Schedule	04/29/20	-	-	04/29/20	05/04/20	05/04/20	PHA/JHA	A	
087100-002-1	087100-02	Door Hardware	04/13/20	-	-	04/13/20	04/14/20	04/16/20	PHA/JHA	AN/RRfR	
087100-002-2	087100-02s	Door Hardware PD	04/29/20	-	-	04/29/20	05/04/20	05/04/20	PHA/JHA	A	
087100-003-1	088000-02s	Hardware PD	05/18/20	-	-	05/18/20	05/26/20	05/27/20	PHA	R	
087100-004-1	087100-01 Rev2	Aluminum Hardware Schedule	09/23/20	-	-	09/25/20	09/30/20	09/30/20	PHA	RR	
087100-004-2	087100-01 Rev3	Aluminum Hardware Schedule	10/05/20	-	-	10/05/20	10/07/20	10/07/20	PHA	AC	
087100-004-3	087100-01 Rev4	Hardware Schedule & PD	10/19/20	-	-	-	-	-	-	-	Accepted for record only
087113-001-1	087113-01s	Automatic Doors	02/12/20	-	-	-	-	02/14/20	JHA	AC	
088000-001-1	088000-03s	Float Glass PD	05/18/20	-	-	-	-	05/27/20	JHA	AC	
088000-002-1	088000-04	Glass Sample	08/19/20	-	-	-	-	09/16/20	JHA	A	Glass Samples Rec'd 9/15
089119-001-1	089119-01s	Louver SD & Color Chart	02/24/20	-	-	-	-	02/27/20	JHA	AC	
089119-002-1	089119-02s	Louver Color Samples	04/21/20	-	-	-	-	05/27/20	JHA	R	Siding Samples Rec'd 5/15
089119-002-2	089119-02s Rev1	Louver Color Samples	06/03/20	-	-	-	-	06/15/20	JHA	AC	Cover sheet & Scan only
DIVISION 9 - FINISHES											
092100-001-1	092100-01s	Gypsum Board	03/30/20	-	-	-	-	03/31/20	JHA	AC/R	Only Impact Gypsum was Rejected
092100-002-1	092100-02s	National Gypsum	04/04/20	-	-	-	-	04/06/20	JHA	R	
092100-003-1	092100-03s	Cold-Formed Steel Exterior Framing	04/20/20	-	-	04/20/20	04/28/20	04/29/20	SA/JHA	RR	

SHOP DRAWING LOG

PROJECT: New Facility for the Carver Police Department, 3 Center Street, Carver, Massachusetts								STATE PROJECT No.:			
G.C.: Tower Construction Corporation								JHA PROJECT No.: 1830			
TEAM: JH Architects (JHA); Garcia-Galuska-DeSousa (GGD); Linden Landscape Architects (LLA); Szewczak Associates (SA); Paul Hawley Associates (PHA); CAMA (CAMA); Building Engineering Resources (BER)								G.C. PROJECT No.: 2252			
JHA SHOP DRAWING NUMBER	G.C. SHOP DRAWING NUMBER	DESCRIPTION <div> <div></div> = Reviewed & Returned <div></div> = Under JHA Review <div></div> = Under Consultant Review <div></div> = Under Owner Review <div></div> = Awaiting G.C. Response </div>	DATE REC'D - From - G.C.	DATE SENT - To - Owner	DATE REC'D - From - Owner	DATE SENT - To - Consult	DATE REC'D - From - Consult	DATE RTN'D - To - G.C.	REVIEWER	ACTION / REMARK	COMMENTS
092100-003-2	092100-03s rev1	Cold-Formed Steel Exterior Framing	06/05/20	-	-	06/05/20	06/09/20	06/10/20	SA/JHA	AC	
093000-001-1	093000-01s	Tile Products	06/22/20	-	-	06/22/20	07/02/20	07/02/20	CAMA	AC	
093000-002-1	093000-02s	Grout & Sealant	06/22/20	-	-	06/22/20	07/02/20	07/02/20	CAMA	A	
093000-003-1	093000-03s	Setting Materials	06/22/20	-	-	06/22/20	07/02/20	07/02/20	CAMA	A	
093000-004-1	093000-04s	Stainless Steel Metal Trim	06/22/20	-	-	06/22/20	07/02/20	07/02/20	CAMA	A	
093000-005-1	093000-05s	CWT-04	06/22/20	-	-	06/22/20	07/02/20	07/02/20	CAMA	A	
093000-006-1	093000-06s	Tile Products	07/09/20	-	-	07/09/20	07/23/20	07/23/20	CAMA	AC	
093000-007-1	093000-07	Tile Shop Drawings	08/19/20	-	-	08/19/20	08/31/20	08/31/20	CAMA	A	
094000-001-1	094000-01s	Industrial Floor System	02/07/20	-	-	-	-	02/07/20	JHA	R	AC Only if Samples are Approved
094000-002-1	094000-02s	Industrial Floor Color Samples	03/04/20	-	-	-	-	03/30/20	JHA	A	Samples Received 3/12/20
095113-001-1	095113-01 095113-02 095113-03 095113-04 095113-05	Acoustical Ceiling Panels	01/02/20	-	-	-	-	01/07/20	JHA	AC	
095113-002-1	095113-06	Acoustical Ceiling Samples	01/13/20	-	-	-	-	03/15/20	JHA	A/R	Samples Received 3/12/20
096500-001-1	096500-01s	Solid Vinyl Tile (SVT-01)(SVT-02)(SVT-03)	01/30/20	-	-	01/30/20	02/06/20	02/07/20	CAMA	A	
096500-002-1	096500-02s	Luxury Vinyl Tile (LVT-01)	01/30/20	-	-	01/30/20	02/06/20	02/07/20	CAMA	AC	
096500-003-1	096500-03s	Rubber Anti-Static Tile (ESD-01)(ESD-02)(ESD-03)	01/30/20	-	-	01/30/20	02/06/20	02/07/20	CAMA	AC	
096500-004-1	096500-04s	Resilient Base	01/30/20	-	-	01/30/20	02/06/20	02/07/20	CAMA	AC	
096500-005-1	096500-05s	Samples	01/30/20	-	-	01/30/20	02/06/20	02/07/20	CAMA	AC	
096500-006-1	096500-06	Resilient Flooring, Base, and Samples - Alt. No. 1	10/22/20	-	-	10/22/20	10/28/20	10/28/20	CAMA	AC	
096810-001-1	096810-01	Carpet Tile	07/30/20	-	-	07/30/20	07/30/20	07/30/20	CAMA	A	
097200-001-1	097200-01s	RWC-01 Impact Wall Resistant Solution	07/01/20	-	-	07/01/20	07/13/20	07/13/20	CAMA	A	
097200-002-1	097200-02s	VWC-01 Denovo Ledge 04	07/01/20	-	-	07/01/20	07/13/20	07/13/20	CAMA	A	
097200-003-1	097200-03s	VWC-02 Denovo Milestone 05	07/01/20	-	-	07/01/20	07/13/20	07/13/20	CAMA	A	
097200-004-1	097200-04s	Samples	07/01/20	-	-	07/01/20	07/13/20	07/13/20	CAMA	A	
097200-005-1	097200-05s	Corner Guards	12/18/20	-	-	12/21/20	12/28/20	12/28/20	CAMA	A	
099000-001-1	099000-01	Painting Product Data	01/15/20	-	-	01/15/20	01/29/20	01/29/20	CAMA	RR	
099000-001-2	099000-01 R1	Painting Product Data	01/31/20	-	-	01/31/20	02/06/20	02/07/20	CAMA	AC	
099000-002-1	099000-02	Interior Finish - Fire Rated Plywood	08/25/20	-	-	08/25/20	09/08/20	09/09/20	CAMA	A	
099000-003-1	099000-03	Paint Color Samples	09/14/20	-	-	09/14/20	09/28/20	09/29/20	CAMA	AC	
099000-004-1	099000-04	Epoxy Water Emulsion Primer Sealer	10/07/20	-	-	10/07/20	10/20/20	10/20/20	CAMA	A	

SHOP DRAWING LOG

PROJECT: New Facility for the Carver Police Department, 3 Center Street, Carver, Massachusetts								STATE PROJECT No.:			
G.C.: Tower Construction Corporation								JHA PROJECT No.: 1830			
TEAM: JH Architects (JHA); Garcia-Galuska-DeSousa (GGD); Linden Landscape Architects (LLA); Szewczak Associates (SA); Paul Hawley Associates (PHA); CAMA (CAMA); Building Engineering Resources (BER)								G.C. PROJECT No.: 2252			
JHA SHOP DRAWING NUMBER	G.C. SHOP DRAWING NUMBER	DESCRIPTION <div> <div></div> = Reviewed & Returned <div></div> = Under JHA Review <div></div> = Under Consultant Review <div></div> = Under Owner Review <div></div> = Awaiting G.C. Response </div>	DATE REC'D - From - G.C.	DATE SENT - To - Owner	DATE REC'D - From - Owner	DATE SENT - To - Consult	DATE REC'D - From - Consult	DATE RTN'D - To - G.C.	REVIEWER	ACTION / REMARK	COMMENTS
DIVISION 10 - SPECIALTIES											
101100-001-1	101100-01	Visual Displays	07/08/20	-	-	07/09/20	07/17/20	07/22/20	JHA/CAMA	AC	
101419-001-1	101419-01	Plaque	10/20/20	-	-	-	-	10/21/20	JHA	AC	
101419-002-1	101419-01Rev1	Plaque	12/30/21	01/04/21	01/04/21	-	-	01/05/21	JHA	AC	
101423-001-1	101423-01	ADA Signs	10/20/20	-	-	-	-	10/29/20	JHA	AC/RR	
102113-001-1	102113-01	Toilet Compartments	07/15/20	-	-	07/15/20	07/17/20	07/21/20	JHA/CAMA	AC	
102213-001-1	102213-01s	Wire Mesh Partitions	03/13/20	-	-	03/15/20	-	03/15/20	JHA	RR	
102213-001-2	102213-01Rev1	Wire Mesh Partitions	12/03/20	-	-	-	-	12/03/20	JHA	AC	
102800-001-1	102800-01s	Toilet and Bath Accessories	05/20/20	-	-	-	-	05/27/20	JHA	AC/R	
102800-001-2	102800-01Rev1	Paper Towel Dispenser & Waste Receptacle	09/03/20	-	-	-	-	09/03/20	JHA	A	
104416-001-1	104416-01s	Fire Extinguishers	05/20/20	-	-	-	-	05/27/20	JHA	A	
105113-001-1	105113-01s	Metal Locker SD	03/13/20	03/16/20	03/25/20	03/15/20	03/20/20	03/31/20	JHA	AC	
105113-001-2	105113-02	Metal Locker SD	10/20/20	-	-	10/20/20	10/21/20	11/02/20	JHA/BER	AC	
105500-001-1	105500-01s	High Security Key Box	04/22/20	-	-	-	-	04/23/20	JHA	AC	
105516-001-1	105516-01	Postal Specialties	07/15/20	-	-	-	-	07/15/20	JHA	AC	
107516-001-1	107516-01s	Flag Poles	05/28/20	-	-	-	-	06/10/20	JHA	A	
DIVISION 11 - EQUIPMENT											
115000-001-1	115000-01s	Canopy Hood	04/27/20	-	-	-	-	04/27/20	JHA	AC	
115000-002-1	115000-01s	Canopy Hood	04/28/20	-	-	-	-	04/28/20	JHA	AC	
115213-001-1	115213-01	Projection Screen	07/08/20	-	-	-	-	07/09/20	JHA	A	
111900-001-1	111900-01s	Detention Equipment	04/01/20	-	-	-	-	04/02/20	JHA	AC	
DIVISION 12 - FURNISHINGS											
120620-001-1	120620-01	Window Treatments	08/26/20	-	-	08/26/20	09/08/20	09/09/20	JHA/CAMA	AC	
123216-001-1	123216-01s	Casework Shop Drawings	03/24/20	-	-	-	-	04/02/20	JHA	RR	
123216-001-2	123216-01 Rev1	Casework Shop Drawings	08/18/20	-	-	-	-	08/26/20	JHA	AC/RR	RR on Dispatch #107 Only
129313-001-1	129313-01s	Bike Rack	04/28/20	-	-	04/28/20	04/29/20	04/29/20	LLA	A	

SHOP DRAWING LOG

PROJECT: New Facility for the Carver Police Department, 3 Center Street, Carver, Massachusetts								STATE PROJECT No.:			
G.C.: Tower Construction Corporation								JHA PROJECT No.: 1830			
TEAM: JH Architects (JHA); Garcia-Galuska-DeSousa (GGD); Linden Landscape Architects (LLA); Szewczak Associates (SA); Paul Hawley Associates (PHA); CAMA (CAMA); Building Engineering Resources (BER)								G.C. PROJECT No.: 2252			
JHA SHOP DRAWING NUMBER	G.C. SHOP DRAWING NUMBER	DESCRIPTION <div> <div></div> = Reviewed & Returned <div></div> = Under JHA Review <div></div> = Under Consultant Review <div></div> = Under Owner Review <div></div> = Awaiting G.C. Response </div>	DATE REC'D - From - G.C.	DATE SENT - To - Owner	DATE REC'D - From - Owner	DATE SENT - To - Consult	DATE REC'D - From - Consult	DATE RTN'D - To - G.C.	REVIEWER	ACTION / REMARK	COMMENTS
DIVISION 13 - SPECIAL CONSTRUCTION											
134700-001-1	134700-01 134700-02 134700-03	Bullet Resistant Protection	02/24/20	-	-	-	-	02/27/20	JHA	AC	
DIVISION 14 - CONVEYING EQUIPMENT											
DIVISION 21 - FIRE SUPPRESSION											
210000-001-1	210000-01S	Fire Protection	01/17/20	-	-	01/17/20	-	-	BER	-	VOIDED BY GTC on 4/8/20
210000-002-1	210000-01s	Underground Fire Service	04/29/20	-	-	04/29/20	05/08/20	05/11/20	BER	A	
210000-003-1	210000-02s	Wet Sprinkler Piping	04/29/20	-	-	04/29/20	05/08/20	05/11/20	BER	A	
210000-004-1	210000-03s	Dry Pipe Sprinkler	04/29/20	-	-	04/29/20	05/08/20	05/11/20	BER	A	
210000-005-1	210000-04s	Valves	04/29/20	-	-	04/29/20	-	-	-	-	SUPERSEDED by FPC ON 5/6/20
210000-005-2	210000-04 Rev1s	Valves	05/06/20	-	-	05/07/20	05/13/20	05/13/20	BER	A	
210000-006-1	210000-05s	Hangers and Supports	04/29/20	-	-	04/29/20	05/13/20	05/13/20	BER	A	
210000-007-1	210000-06s	FDC	04/29/20	-	-	04/29/20	05/13/20	05/13/20	BER	A	
210000-008-1	210000-07s	Sprinkler Heads	04/29/20	-	-	04/29/20	05/13/20	05/13/20	BER	A	
210000-009-1	210000-08s	Sprinkler Cabinet	04/29/20	-	-	04/29/20	05/13/20	05/13/20	BER	A	
210000-010-1	210000-09s	Signaling Devices	04/29/20	-	-	04/29/20	-	-	-	-	SUPERSEDED by FPC ON 5/6/20
210000-010-2	210000-09 Rev1s	Signaling Devices	05/06/20	-	-	05/07/20	05/27/20	05/27/20	BER	A	
210000-011-1	210000-10s	Water Pressure Gauges	04/29/20	-	-	04/29/20	-	-	-	-	SUPERSEDED by FPC ON 5/6/20
210000-011-2	210000-10 Rev1s	Water Pressure Gauges	05/06/20	-	-	05/07/20	05/27/20	05/27/20	BER	A	
210000-012-1	210000-11s	Sleeves and Penetrations	04/29/20	-	-	04/29/20	05/13/20	05/13/20	BER	A	

SHOP DRAWING LOG

PROJECT: New Facility for the Carver Police Department, 3 Center Street, Carver, Massachusetts								STATE PROJECT No.:			
G.C.: Tower Construction Corporation								JHA PROJECT No.: 1830			
TEAM: JH Architects (JHA); Garcia-Galuska-DeSousa (GGD); Linden Landscape Architects (LLA); Szewczak Associates (SA); Paul Hawley Associates (PHA); CAMA (CAMA); Building Engineering Resources (BER)								G.C. PROJECT No.: 2252			
JHA SHOP DRAWING NUMBER	G.C. SHOP DRAWING NUMBER	DESCRIPTION <div> <div></div> = Reviewed & Returned <div></div> = Under JHA Review <div></div> = Under Consultant Review <div></div> = Under Owner Review <div></div> = Awaiting G.C. Response </div>	DATE REC'D	DATE SENT	DATE REC'D	DATE SENT	DATE REC'D	DATE RTN'D	REVIEWER	ACTION / REMARK	COMMENTS
			- From - G.C.	- To - Owner	- From - Owner	- To - Consult	- From - Consult	- To - G.C.			
210000-013-1	210000-12s	Fire Hydrants	04/29/20	05/13/20	05/14/20	04/29/20	05/13/20	05/14/20	BER	AC	
210000-014-1	210000-13s	Hydraulic Calcs & Drawings	05/06/20	-	-	05/07/20	05/27/20	05/27/20	BER	RR	
210000-014-2	210000-13 Rev1	Hydraulic Calcs & Drawings	07/20/20	-	-	07/21/20	08/03/20	08/03/20	BER	A	
210000-015-1	210000-14s	FP Drawings	05/06/20	-	-	05/07/20	-	-	BER	RR	Engineer Comments in 210000-014-1
210000-016-1	210000-15s	Fire Pump	05/06/20	-	-	05/07/20	05/27/20	05/27/20	BER	AC	
210000-017-1	210000-16s	Underground Water Storage Tank	05/13/20	-	-	05/13/20	05/27/20	05/27/20	BER	AC	
210000-018-1	210000-17s	Sprinkler Coordination Drawings	06/08/20	-	-	06/08/20	06/22/20	06/22/20	BER	A	
DIVISION 22 - PLUMBING											
220000-001-1	220000-01s	Tight Tank	02/17/20	-	-	02/17/20	03/02/20	03/02/20	BER	AC	
220000-002-1	220000-02s	Water Heaters	02/17/20	-	-	02/17/20	03/02/20	03/02/20	BER	A	
220000-003-1	220000-03s	Pumps	02/17/20	-	-	02/17/20	03/02/20	03/02/20	BER	A	
220000-004-1	220000-04s	Pipe I.D.	02/17/20	-	-	02/17/20	03/02/20	03/02/20	BER	A	
220000-005-1	220000-05s	Water Meter	02/17/20	-	-	02/17/20	03/02/20	03/02/20	BER	A	
220000-006-1	220000-06s	Cross Connection Points	02/17/20	-	-	02/17/20	03/02/20	03/02/20	BER	A	
220000-007-1	220000-07s	Pipe Supports	02/21/20	-	-	02/24/20	03/02/20	03/02/20	BER	A	
220000-008-1	220000-08s	Sleeves, Inserts, Fire Stopping & Escutcheons	02/21/20	-	-	02/24/20	03/02/20	03/02/20	BER	A	
220000-009-1	220000-09s	Pipe Materials	02/21/20	-	-	02/24/20	03/02/20	03/02/20	BER	A	
220000-010-1	220000-10s	Copper Pipe	02/21/20	-	-	02/24/20	03/02/20	03/02/20	BER	A	
220000-011-1	220000-11s	Sanitary Waste & Vent	02/21/20	-	-	02/24/20	03/02/20	03/02/20	BER	A	
220000-012-1	220000-12s	Press & Temp Control Devices	02/21/20	-	-	02/24/20	03/02/20	03/02/20	BER	A	
220000-013-1	220000-13s	Insulation	02/21/20	-	-	02/24/20	03/02/20	03/02/20	BER	A	
220000-014-1	220000-14s	Traps & Strainers	02/21/20	-	-	02/24/20	03/02/20	03/02/20	BER	AC	
220000-015-1	220000-15s	Thermometers & Pressure Gauges	02/21/20	-	-	02/24/20	03/02/20	03/02/20	BER	A	
220000-016-1	220000-16s	Wall Hydrants & Hose Bibbs	02/21/20	-	-	02/24/20	03/02/20	03/02/20	BER	A	
220000-017-1	220000-17s	Water Hammer Arrestors	02/21/20	-	-	02/24/20	03/02/20	03/02/20	BER	A	
220000-018-1	220000-18s	Drains	03/10/20	-	-	03/10/20	03/24/20	03/24/20	BER	A	
220000-019-1	220000-19s	Plumbing Fixtures - Water Closets	03/10/20	-	-	03/10/20	03/24/20	03/24/20	BER/JHA	AC	
220000-020-1	220000-20s	Plumbing Fixtures - Urinals	03/10/20	-	-	03/10/20	03/24/20	03/24/20	BER/JHA	AC	
220000-021-1	220000-21s	Plumbing Fixtures - Sinks & Faucets	03/10/20	-	-	03/10/20	03/24/20	03/24/20	BER/JHA	AC	
220000-022-1	220000-22s	Plumbing Fixtures - Shower	03/10/20	-	-	03/10/20	03/24/20	03/24/20	BER/JHA	AC	
220000-023-1	220000-23s	Plumbing Fixtures - Lavatories	03/10/20	-	-	03/10/20	03/24/20	03/24/20	BER/JHA	A	

SHOP DRAWING LOG

PROJECT: New Facility for the Carver Police Department, 3 Center Street, Carver, Massachusetts								STATE PROJECT No.:			
G.C.: Tower Construction Corporation								JHA PROJECT No.: 1830			
TEAM: JH Architects (JHA); Garcia-Galuska-DeSousa (GGD); Linden Landscape Architects (LLA); Szewczak Associates (SA); Paul Hawley Associates (PHA); CAMA (CAMA); Building Engineering Resources (BER)								G.C. PROJECT No.: 2252			
JHA SHOP DRAWING NUMBER	G.C. SHOP DRAWING NUMBER	DESCRIPTION <div> <div></div> = Reviewed & Returned <div></div> = Under JHA Review <div></div> = Under Consultant Review <div></div> = Under Owner Review <div></div> = Awaiting G.C. Response </div>	DATE REC'D - From - G.C.	DATE SENT - To - Owner	DATE REC'D - From - Owner	DATE SENT - To - Consult	DATE REC'D - From - Consult	DATE RTN'D - To - G.C.	REVIEWER	ACTION / REMARK	COMMENTS
220000-024-1	220000-24s	Plumbing Fixtures - Ice Maker Box	03/10/20	-	-	03/10/20	03/24/20	03/24/20	BER/JHA	A	
220000-025-1	220000-25s	Plumbing Fixtures - Laundry Washing Machine Box	03/10/20	-	-	03/10/20	03/24/20	03/24/20	BER/JHA	A	
220000-026-1	220000-26s	Exterior Wall Hydrant	03/10/20	-	-	03/10/20	03/24/20	03/24/20	BER/JHA	AC	
220000-027-1	220000-27s	Plumbing Fixtures - Emergency Eye Wash & Shower	03/10/20	-	-	03/10/20	03/24/20	03/24/20	BER/JHA	A	
220000-028-1	220000-28s	Plumbing Fixtures - Detention Grade Shower System	03/10/20	-	-	03/10/20	03/24/20	03/24/20	BER/JHA	AC	
220000-029-1	220000-29s	Plumbing Fixtures - Drinking Fountain	03/10/20	-	-	03/10/20	03/24/20	03/24/20	BER/JHA	A	
220000-030-1	220000-30s	Plumbing Fixtures - Combination Lav-Toilets	03/10/20	-	-	03/10/20	03/24/20	03/24/20	BER/JHA	RR	
220000-030-2	220000-30s Rev1	Plumbing Fixtures - Combination Lav-Toilets	07/02/20	-	-	07/02/20	07/17/20	07/21/20	BER/JHA	AC	
220000-030-3	220000-34	DS-C Fixture	07/27/20	-	-	07/27/20	08/03/20	08/03/20	BER	A	
220000-031-1	220000-31s	Thermostatic Mixing Valves	03/10/20	-	-	03/10/20	03/24/20	03/24/20	BER	A	
220000-032-1	220000-32s	Plumbing Fixtures - Detention Grade Shower Valve	03/10/20	-	-	03/10/20	03/24/20	03/24/20	BER/JHA	R	
220000-033-1	220000-33s	Plumbing Fixtures - Boot Wash Hose Bib	03/10/20	-	-	03/10/20	03/24/20	03/24/20	BER/JHA	AC	
DIVISION 23 - HVAC											
230000-001-1	230000-01s	Ductwork & Air Distribution Equipment	03/12/20	-	-	03/12/20	03/25/20	03/25/20	BER	A	
230000-002-1	230000-02s	Centrifugal Fans	03/12/20	-	-	03/12/20	03/25/20	03/25/20	BER	A	
230000-003-1	230000-03s	RGDs	03/12/20	-	-	03/12/20	03/25/20	03/25/20	BER/JHA	A/AC	
230000-004-1	230000-04s	ERV & VRF	03/12/20	-	-	03/12/20	03/25/20	03/25/20	BER	AC	
230000-005-1	230000-05s	Duct & Pipe Insulation	03/17/20	-	-	03/18/20	03/25/20	03/25/20	BER	A	
230000-006-1	230000-06s	Electrical Heaters	03/18/20	-	-	03/18/20	03/25/20	03/25/20	BER	AC	
230000-007-1	230000-07s	Motorized Dampers	03/18/20	-	-	03/18/20	03/25/20	03/25/20	BER	A	
230000-008-1	230000-08s	Outbuilding HVAC Equipment	04/29/20	-	-	04/29/20	05/13/20	05/13/20	BER	A	
DIVISION 26 - ELECTRICAL											
260000-001-1	260000-01s	Fire Alarm System	02/12/20	-	-	02/12/20	02/14/20	02/14/20	BER	A/AC/RR	
260000-001-2	260000-01s Rev 1	Fire Alarm System	03/17/20	-	-	03/18/20	03/19/20	03/19/20	BER	A/AC/RR	

SHOP DRAWING LOG

PROJECT: New Facility for the Carver Police Department, 3 Center Street, Carver, Massachusetts								STATE PROJECT No.:			
G.C.: Tower Construction Corporation								JHA PROJECT No.: 1830			
TEAM: JH Architects (JHA); Garcia-Galuska-DeSousa (GGD); Linden Landscape Architects (LLA); Szewczak Associates (SA); Paul Hawley Associates (PHA); CAMA (CAMA); Building Engineering Resources (BER)								G.C. PROJECT No.: 2252			
JHA SHOP DRAWING NUMBER	G.C. SHOP DRAWING NUMBER	DESCRIPTION <div> <div></div> = Reviewed & Returned <div></div> = Under JHA Review <div></div> = Under Consultant Review <div></div> = Under Owner Review <div></div> = Awaiting G.C. Response </div>	DATE REC'D - From - G.C.	DATE SENT - To - Owner	DATE REC'D - From - Owner	DATE SENT - To - Consult	DATE REC'D - From - Consult	DATE RTN'D - To - G.C.	REVIEWER	ACTION / REMARK	COMMENTS
260000-001-3	260000-01s Rev 2	Fire Alarm System	05/15/20	-	-	05/15/20	05/18/20	-	BER	-	VOIDED by 260000-001-4
260000-001-4	260000-01s Rev 3	Fire Alarm System	05/20/20	-	-	05/26/20	05/27/20	05/27/20	BER	A/AC	
260000-002-1	260000-02s	Engine Generator System	02/12/20	-	-	02/12/20	02/14/20	02/14/20	BER	AC/RR	
260000-002-2	260000-02s Rev 1	Engine Generator System	03/12/20	-	-	03/12/20	03/16/20	03/16/20	BER	AC/RR	
260000-002-3	260000-02s Rev 2	Engine Generator System	03/19/20	-	-	03/19/20	03/19/20	03/19/20	BER	AC	
260000-003-1	260000-03s	Lightning Protection	02/12/20	-	-	02/12/20	02/14/20	02/14/20	BER	A/AC/RR	
260000-003-2	260000-03s Rev1	Lightning Protection	02/20/20	-	-	02/20/20	02/20/20	02/24/20	BER/JHA	A/AC	
260000-004-1	260000-04s	Storm Switch (ATS)	02/20/20	-	-	02/20/20	02/21/20	02/24/20	BER	AC	
260000-005-1	260000-05s	Encl for Indiv Mntd Overcurrent & Switching Dev	03/17/20	-	-	03/18/20	03/19/20	03/19/20	BER	A/AC	
260000-006-1	260000-06s	Panelboards	03/17/20	-	-	03/18/20	03/19/20	03/19/20	BER	A/AC	
260000-007-1	260000-07s	Cartridge Fuses	03/17/20	-	-	03/18/20	03/19/20	03/19/20	BER	AC	
260000-008-1	260000-08s	Branch Panel SPD Protection	03/17/20	-	-	03/18/20	03/19/20	03/19/20	BER	A	
260000-009-1	260000-09s	Lighting Fixture	03/18/20	-	-	03/18/20	03/20/20	03/20/20	BER/JHA	A/AC	
260000-009-02	260000-09s Rev 1	Lighting Fixture	04/13/20	-	-	04/13/20	04/14/20	04/14/20	BER/JHA	A/AC	
260000-010-1	260000-10s	Lighting Control	03/18/20	-	-	03/18/20	03/20/20	03/20/20	BER/JHA	A/AC/R	
260000-011-1	260000-11s	Raceways & Fittings	03/18/20	-	-	03/18/20	03/19/20	03/19/20	BER	A	
260000-012-1	260000-12s	Cable Tray	03/18/20	-	-	03/18/20	03/19/20	03/19/20	BER	A/R	
260000-013-1	260000-13s	Uninterruptible Power System	03/24/20	-	-	03/24/20	03/25/20	03/25/20	BER	R	
260000-013-2	260000-13 Rev 1	Uninterruptible Power System	03/30/20	-	-	03/30/20	03/31/20	03/31/20	BER	AC	
260000-013-3	260000-13 Rev 2	Uninterruptible Power System	10/14/20	-	-	10/16/20	10/19/20	10/19/20	BER	AC	
260000-014-1	260000-14s	Grounding System	03/26/20	-	-	03/29/20	03/30/20	03/30/20	BER	A	
260000-015-1	260000-15s	Phasing & Color Coding	03/26/20	-	-	03/29/20	03/30/20	03/30/20	BER	A	
260000-016-1	260000-16s	Wiring Materials	03/26/20	-	-	03/29/20	03/30/20	03/30/20	BER	A/AC	
260000-017-1	260000-17s	Wiring Devices	03/26/20	-	-	03/29/20	03/30/20	03/30/20	BER	A/AC	
260000-018-1	260000-18s	Access Panels	03/26/20	-	-	03/29/20	03/30/20	03/30/20	BER	AC	
260000-019-1	260000-19s	Outlet, Junction, Pull Boxes	03/26/20	-	-	03/29/20	03/30/20	03/30/20	BER	A/AC	
260000-020-1	260000-20s	Trough	03/26/20	-	-	03/29/20	03/30/20	03/30/20	BER	A	
260000-021-1	260000-21s	Floor Boxes	03/26/20	-	-	03/29/20	03/30/20	03/30/20	BER	AC	
260000-022-1	260000-22s	Motor Control	03/30/20	-	-	03/30/20	03/31/20	03/31/20	BER	AC	
260000-023-1	260000-23s	Integrated Technology Infrastructure Support	03/30/20	-	-	03/30/20	03/31/20	03/31/20	BER	AC	
260000-024-1	260000-24s	Equipment Racks	04/01/20	-	-	04/01/20	04/02/20	04/02/20	BER	AC	
260000-025-1	260000-25s	Surge Protected Power Strip	04/01/20	-	-	04/01/20	04/02/20	04/02/20	BER	A	

SHOP DRAWING LOG

PROJECT: New Facility for the Carver Police Department, 3 Center Street, Carver, Massachusetts								STATE PROJECT No.:			
G.C.: Tower Construction Corporation								JHA PROJECT No.: 1830			
TEAM: JH Architects (JHA); Garcia-Galuska-DeSousa (GGD); Linden Landscape Architects (LLA); Szewczak Associates (SA); Paul Hawley Associates (PHA); CAMA (CAMA); Building Engineering Resources (BER)								G.C. PROJECT No.: 2252			
JHA SHOP DRAWING NUMBER	G.C. SHOP DRAWING NUMBER	DESCRIPTION <div> = Reviewed & Returned = Under JHA Review = Under Consultant Review = Under Owner Review = Awaiting G.C. Response </div>	DATE REC'D	DATE SENT	DATE REC'D	DATE SENT	DATE REC'D	DATE RTN'D	REVIEWER	ACTION / REMARK	COMMENTS
			- From - G.C.	- To - Owner	- From - Owner	- To - Consult	- From - Consult	- To - G.C.			
260000-026-1	260000-26s	Cable Supports	04/01/20	-	-	04/01/20	04/02/20	04/02/20	BER	A	
260000-027-1	260000-27s	Bonding & Grounding Jumper Cable	04/01/20	-	-	04/01/20	04/02/20	04/02/20	BER	A	
260000-028-1	260000-28s	Unshielded Twisted Pair Cable	04/01/20	-	-	04/01/20	04/02/20	04/02/20	BER	AC	
260000-029-1	260000-29s	Broadband RF Cabling System	04/01/20	-	-	04/01/20	04/02/20	04/02/20	BER	AC	
260000-030-1	260000-30s	Underground Enclosures	04/01/20	-	-	04/01/20	04/02/20	04/02/20	BER	AC	
260000-031-1	260000-31s	Lighting Factory Drawings	04/30/20	-	-	04/30/20	05/01/20	05/01/20	BER	AC	
260000-032-1	260000-32s	Lighting - Factory Drawings Vode	05/13/20	-	-	05/13/20	05/14/20	05/14/20	BER	AC	
260000-033-1	260000-33	Power System Studies	08/03/20	-	-	08/03/20	08/06/20	08/07/20	BER	AC	
260000-034-1	260000-34	Lighting - Cupola	10/15/20	-	-	10/16/20	10/20/20	10/21/20	BER	AC	
DIVISION 27 - COMMUNICATIONS											
DIVISION 31 - EARTHWORK											
312000-001-1	312000-01s	K-RAP Base	03/06/20	-	-	03/06/20	03/09/20	03/09/20	GGD	AC	
312500-001-1	312500-01s	Erosion Control	01/17/20	-	-	01/17/20	01/27/20	01/28/20	LLA	A	
312500-002-1	312500-02s	SWPPP	02/17/20	-	-	02/17/20	02/25/20	02/25/20	GGD	RR	
312500-002-2	312500-02s Rev 1	SWPPP	03/02/20	-	-	03/02/20	03/09/20	03/09/20	GGD	AC	
DIVISION 32 - EXTERIOR IMPROVEMENTS											
321313-001-1	033004-03s	Exterior Flatwork	02/19/20	-	-	02/19/20	02/24/20	02/24/20	LLA	A	
321313-002-1	321313-02s	Site Tactile Warning Tiles	04/29/20	04/30/20	04/30/20	04/29/20	04/30/20	04/30/20	LLA	AC	
321613-001-1	321613-01s	Precast Concrete Curb	04/21/20	-	-	04/21/20	04/22/20	04/22/20	LLA	A	
323113-001-1	323113-01s	Shop Drawings	07/01/20	-	-	07/01/20	07/03/20	07/06/20	LLA	A	
323913-001-1	323913-01s	Steel Bollards and Bollard Covers	04/29/20	-	-	04/29/20	04/30/20	04/30/20	LLA	AC	
DIVISION 33 - UTILITIES											

SHOP DRAWING LOG

PROJECT: New Facility for the Carver Police Department, 3 Center Street, Carver, Massachusetts								STATE PROJECT No.:			
G.C.: Tower Construction Corporation								JHA PROJECT No.: 1830			
TEAM: JH Architects (JHA); Garcia-Galuska-DeSousa (GGD); Linden Landscape Architects (LLA); Szewczak Associates (SA); Paul Hawley Associates (PHA); CAMA (CAMA); Building Engineering Resources (BER)								G.C. PROJECT No.: 2252			
JHA SHOP DRAWING NUMBER	G.C. SHOP DRAWING NUMBER	DESCRIPTION <div><div></div> = Reviewed & Returned <div></div> = Under JHA Review <div></div> = Under Consultant Review <div></div> = Under Owner Review <div></div> = Awaiting G.C. Response</div>	DATE REC'D - From - G.C.	DATE SENT - To - Owner	DATE REC'D - From - Owner	DATE SENT - To - Consult	DATE REC'D - From - Consult	DATE RTN'D - To - G.C.	REVIEWER	ACTION / REMARK	COMMENTS
330000-001-1	330000-01	Manhole and Precast Concrete Structure	01/08/20	-	-	01/08/20	01/16/20	01/17/20	GGD	RR	
330000-001-2	330000-01s	Manhole and Precast Concrete Structure	02/17/20	-	-	02/17/20	02/25/20	02/25/20	GGD	AC	
330000-002-1	330000-01s	Site Utilities	01/17/20	-	-	01/17/20	01/28/20	01/28/20	GGD	AC	
330000-003-1	330000-02s	Sewers and Pipes	01/17/20	-	-	01/17/20	01/24/20	01/24/20	GGD	RR	
330000-004-1	033004-01s	Concrete Ductbank	02/19/20	-	-	02/19/20	02/24/20	02/24/20	GGD	RR	
330000-004-2	033004-01s Rev 1	Concrete Ductbank	03/05/20	-	-	03/06/20	03/17/20	03/17/20	GGD	A	
330000-005-1	330000-03s	K-RAP Base	02/27/20	-	-	02/27/20	-	-	-	-	VOIDED by GC - See 312000-001-1



ON-SITE REPRESENTATIVE DAILY REPORT

PROJECT:	Carver Police Station	PROJECT #:		Report Number:	203
-----------------	-----------------------	-------------------	--	-----------------------	-----

Contract Time:	Date: 11-30-2020	
Days Elapsed:	Day: Monday	
Extensions:	Weather: Clear	
Days Remaining:	Temperature Cycle at 7 AM:	32 – 63 deg.
Site Condition:	Dry	

Contractor	Workforce	
Tower Construction	1 Superintendent, 0 laborer, 0 carpenters – Kevin Thompson (site supervision)	1
Dig It	0 operator, 0 laborer, 0 foreman, 0 dirtworks (sitework)	0
Dandis	1 painter (painting)	1
Delta	2 sprinkler fitters (fire protection)	2
American Electrical	1 foreman, 1 journeyman, 1 apprentice (electrical)	3
Lapan	0 foreman, 0 journeyman, 0 apprentice, 0 insulator (mechanical)	0
Belcour	0 roofers (roofing)	0
Central Ceilings	0 carpenter (acoustical ceilings)	0
Hareld Glass	0 glazers (storefront)	0
Debrino	1 caulker (join sealant)	1
Empire	2 carpenters (rough carpentry)	2
T&C	0 carpenters (millwork)	0
John Oliveira & Sons	0 carpenters (formwork)	0
G&H	0 foreman, 0 apprentice, 0 journeyman, 0 insulator (HVAC)	0
Capital	3 tilers (ceramic)	3
Barber Drywall	0 foreman, 0 apprentice, 2 carpenters, 0 taper (exterior framing)	2
	Total Workforce	15

Miscellaneous Others		
CHA	Alyssa Chatani	1
Town of Carver	Bill Harriman	1
	Total Misc. Workforce	2

Construction Activity:

American Electrical: Installing ceiling lights in offices and locker rooms.

Delta: Connecting sprinkler piping in fire pump room.

Dandis: Continue painting door frames and doors in Sally Port.

Empire: Setting last fiberglass columns at the entry area.

Barber: Topping the outbuilding ceiling and walls in the fitness room.

Debrino: Sealing around overhead door trim.

T&C: Not on site.

Capital: Installing tile in main lobby area, and border tile in training room.

Clerk's remarks: none

Site Visitors/Meetings: See above, Eversource crew working on site.

Deliveries: none

Equipment Used: Empire: (2) Boom Lift 600s, Barber (2) Scissor Lift, Commercial: Lull 944E, Mini Bobcat



ON-SITE REPRESENTATIVE DAILY REPORT

PROJECT:	Carver Police Station	PROJECT #:		Report Number:	204
-----------------	-----------------------	-------------------	--	-----------------------	-----

Contract Time:	Date: 12-01-2020	
Days Elapsed:	Day: Tuesday	
Extensions:	Weather: Clear	
Days Remaining:	Temperature Cycle at 7 AM:	44 – 64 deg.
Site Condition:	Dry	

Contractor	Workforce	
Tower Construction	1 Superintendent, 0 laborer, 2 carpenters – Kevin Thompson (site supervision)	3
Dig It	0 operator, 0 laborer, 0 foreman, 0 dirtworks (sitework)	0
Dandis	1 painter (painting)	1
Delta	2 sprinkler fitters (fire protection)	2
American Electrical	1 foreman, 1 journeyman, 1 apprentice (electrical)	3
Lapan	0 foreman, 0 journeyman, 0 apprentice, 0 insulator (mechanical)	0
Belcour	0 roofers (roofing)	0
Central Ceilings	0 carpenter (acoustical ceilings)	0
Hareld Glass	0 glazers (storefront)	0
Debrino	1 caulker (join sealant)	1
Empire	2 carpenters (rough carpentry)	2
T&C	0 carpenters (millwork)	0
John Oliveira & Sons	0 carpenters (formwork)	0
G&H	0 foreman, 0 apprentice, 0 journeyman, 0 insulator (HVAC)	0
Capital	2 tilers (ceramic)	2
Barber Drywall	0 foreman, 0 apprentice, 2 carpenters, 0 taper (exterior framing)	2
	Total Workforce	16

Miscellaneous Others		
CHA	Alyssa Chatani	1
Town of Carver	Bill Harriman, Dave Siedentopf	2
Dig It	Removing trailers from the site	2
	Total Misc. Workforce	5

Construction Activity:

American Electrical: Installing grid lighting in Chief's office area and day room sections.

Delta: Continues to install sprinkler heads in detention area and installing piping.

Dandis: Painting exterior doors and frames at outbuilding.

Empire: Completed the fiberglass columns at entry area.

Barber: Taping second coat in outbuilding and booking room inside.

Debrino: Sealing window casings from the inside for exterior windows.

T&C: Not on site.

Capital: Placing border tiles in lobby area and Men's Locker Room bathrooms.

Clerk's remarks: Installing curb forms for boot wash and sealant on columns.

Site Visitors/Meetings: see above

Deliveries: none

Equipment Used: Empire: (2) Boom Lift 600s, Barber (2) Scissor Lift, Commercial: Lull 944E, Mini Bobcat

PROJECT:	Carver Police Station	PROJECT #:		Report Number:	205
-----------------	-----------------------	-------------------	--	-----------------------	-----

Contract Time:	Date: 12-02-2020	
Days Elapsed:	Day: Wednesday	
Extensions:	Weather: Cloudy	
Days Remaining:	Temperature Cycle at 7 AM:	30 – 46 deg.
Site Condition:	Dry	

Contractor	Workforce	
Tower Construction	1 Superintendent, 0 laborer, 2 carpenters – Kevin Thompson (site supervision)	3
Dig It	0 operator, 0 laborer, 0 foreman, 0 dirtworks (sitework)	0
Dandis	1 painter (painting)	1
Delta	2 sprinkler fitters (fire protection)	2
American Electrical	1 foreman, 1 journeyman, 1 apprentice (electrical)	3
Lapan	0 foreman, 0 journeyman, 0 apprentice, 0 insulator (mechanical)	0
Belcour	0 roofers (roofing)	0
Central Ceilings	0 carpenter (acoustical ceilings)	0
Hareld Glass	0 glazers (storefront)	0
Debrino	1 caulker (join sealant)	1
CJM Services	2 carpenters (resilient)	2
T&C	0 carpenters (millwork)	0
John Oliveira & Sons	0 carpenters (formwork)	0
G&H	0 foreman, 0 apprentice, 0 journeyman, 0 insulator (HVAC)	0
Capital	2 tilers (ceramic)	2
Barber Drywall	0 foreman, 0 apprentice, 2 carpenters, 0 taper (exterior framing)	2
	Total Workforce	

Miscellaneous Others		
CHA	Alyssa Chatani, Joe Sullivan	2
Town of Carver	Bill Harriman, Dave Siedentopf, Dave Robertson	3
Tower Construction	Patrick Fitzgerald	1
	Total Misc. Workforce	6

Construction Activity:

American Electrical: Fire caulking above ceiling grid, installing lights in day room and locker rooms.

Delta: Continues to install fire suppression piping inside fire pump room.

Dandis: Painting second coat at exterior doors at the outbuilding.

CJM Services: Set up communication room flooring.

Barber: Taping the ceiling of the outbuilding and fitness walls.

Debrino: Placing caulking around the interior trim of the windows.

T&C: Not on site.

Capital: Finished men's locker room bathrooms at wet wall areas.

Clerk's remarks: Tower is applying sealant at fiberglass columns at the exterior.

Site Visitors/Meetings: see above

Deliveries: Resilient flooring, corridor lights

Equipment Used: Empire: (2) Boom Lift 600s, Barber (2) Scissor Lift, Commercial: Lull 944E, Mini Bobcat

PROJECT:	Carver Police Station	PROJECT #:		Report Number:	206
-----------------	-----------------------	-------------------	--	-----------------------	-----

Contract Time:	Date: 12-03-2020	
Days Elapsed:	Day: Thursday	
Extensions:	Weather: Cloudy	
Days Remaining:	Temperature Cycle at 7 AM:	39 – 52 deg.
Site Condition:	Dry	

Contractor	Workforce	
Tower Construction	1 Superintendent, 0 laborer, 1 carpenters – Kevin Thompson (site supervision)	2
Dig It	0 operator, 0 laborer, 0 foreman, 0 dirtworks (sitework)	0
Dandis	1 painter (painting)	1
Delta	4 sprinkler fitters (fire protection)	4
American Electrical	1 foreman, 2 journeyman, 1 apprentice (electrical)	4
Lapan	0 foreman, 0 journeyman, 0 apprentice, 0 insulator (mechanical)	0
Belcour	0 roofers (roofing)	0
Central Ceilings	0 carpenter (acoustical ceilings)	0
Hareld Glass	0 glazers (storefront)	0
Debrino	1 caulker (join sealant)	1
CJM Services	1 carpenter (resilient)	1
T&C	0 carpenters (millwork)	0
John Oliveira & Sons	0 carpenters (formwork)	0
G&H	0 foreman, 0 apprentice, 0 journeyman, 0 insulator (HVAC)	0
Capital	2 tilers (ceramic)	2
Barber Drywall	0 foreman, 1 apprentice, 3 carpenters, 0 taper (exterior framing)	4
	Total Workforce	19

Miscellaneous Others		
CHA	Alyssa Chatani	1
Town of Carver	Bill Harriman	1
Carver Fire / Carver Police	Eric & Jesse / Bill & Mike	4
Cavicchio	Sean – rep.	1
	Total Misc. Workforce	7

Construction Activity:

American Electrical: Continues to install lights inside of the grid at office rooms.

Delta: Installed fire pump equipment inside of the outbuilding pump room.

Dandis: Priming and painting the last exterior columns at entry.

CJM Services: Completed the installation of the communications room flooring.

Barber: Applying sheet rock finishes at attic area and outbuilding.

Debrino: Installing sealant inside cell areas and exterior trim.

T&C: Not on site.

Capital: Placing tile on the walls of the women's locker room and men's locker room.

Clerk's remarks: Tower is removing forms and a general cleanup.

Site Visitors/Meetings: see above

Deliveries: Resilient flooring, corridor lights

Equipment Used: Empire: (2) Boom Lift 600s, Barber (2) Scissor Lift, Commercial: Lull 944E, Mini Bobcat

PROJECT:	Carver Police Station	PROJECT #:		Report Number:	207
-----------------	-----------------------	-------------------	--	-----------------------	-----

Contract Time:	Date: 12-04-2020	
Days Elapsed:	Day: Friday	
Extensions:	Weather: Clear	
Days Remaining:	Temperature Cycle at 7 AM:	42 – 54 deg.
Site Condition:	Dry	

Contractor	Workforce	
Tower Construction	1 Superintendent, 0 laborer, 0 carpenters – Kevin Thompson (site supervision)	1
Dig It	0 operator, 0 laborer, 0 foreman, 0 dirtworks (sitework)	0
Dandis	1 painter (painting)	1
Delta	2 sprinkler fitters (fire protection)	2
American Electrical	1 foreman, 2 journeyman, 1 apprentice (electrical)	4
Lapan	0 foreman, 0 journeyman, 0 apprentice, 0 insulator (mechanical)	0
Belcour	0 roofers (roofing)	0
Central Ceilings	0 carpenter (acoustical ceilings)	0
Hareld Glass	2 glazers (storefront)	2
Debrino	0 caulker (join sealant)	0
CJM Services	1 carpenter (resilient)	1
T&C	0 carpenters (millwork)	0
John Oliveira & Sons	0 carpenters (formwork)	0
G&H	0 foreman, 0 apprentice, 0 journeyman, 0 insulator (HVAC)	0
Capital	2 tilers (ceramic)	2
Barber Drywall	0 foreman, 1 apprentice, 3 carpenters, 0 taper (exterior framing)	4
	Total Workforce	17

Miscellaneous Others		
CHA	Alyssa Chatani	1
Town of Carver	Bill Harriman	1
Carver Police	Pete & Mike	2
	Total Misc. Workforce	4

Construction Activity:

American Electrical: Placing light fixtures inside of ceiling grid.

Delta: Assembling piping and stands in the fire pump room at the outbuilding.

Dandis: Painting door frames at the main building and continue column painting.

CJM Services: Setting flooring inside of room 150 and 151.

Barber: Taping attic sections and installing door frame in attic.

Debrino: Not on site.

Hareld: Placing glass inside of storefront door at rear entry and continue caulking.

Capital: Installing floor tile in the lobby bathrooms.

Clerk's remarks: none

Site Visitors/Meetings: see above

Deliveries: none

Equipment Used: Empire: (2) Boom Lift 600s, Barber (2) Scissor Lift, Commercial: Lull 944E, Mini Bobcat

PROJECT:	Carver Police Station	PROJECT #:		Report Number:	208
-----------------	-----------------------	-------------------	--	-----------------------	-----

Contract Time:	Date: 12-07-2020	
Days Elapsed:	Day: Monday	
Extensions:	Weather: Clear	
Days Remaining:	Temperature Cycle at 7 AM:	42 – 54 deg.
Site Condition:	Dry	

Contractor	Workforce	
Tower Construction	1 Superintendent, 0 laborer, 0 carpenters – Kevin Thompson (site supervision)	1
Dig It	0 operator, 0 laborer, 0 foreman, 0 dirtworks (sitework)	0
Dandis	1 painter (painting)	1
Delta	0 sprinkler fitters (fire protection)	0
American Electrical	1 foreman, 2 journeyman, 1 apprentice (electrical)	4
Lapan	1 foreman, 0 journeyman, 0 apprentice, 0 insulator (mechanical)	1
Belcour	1 roofer (roofing)	1
Central Ceilings	0 carpenter (acoustical ceilings)	0
Hareld Glass	0 glazers (storefront)	0
Debrino	0 caulker (join sealant)	0
CJM Services	1 carpenter (resilient)	1
T&C	2 carpenters (millwork)	2
John Oliveira & Sons	1 carpenters (formwork)	1
G&H	0 foreman, 0 apprentice, 0 journeyman, 0 insulator (HVAC)	0
Capital	2 tilers (ceramic)	2
Barber Drywall	0 foreman, 1 apprentice, 3 carpenters, 0 taper (exterior framing)	4
	Total Workforce	18

Miscellaneous Others		
CHA	Alyssa Chatani	1
Town of Carver	Bill Harriman, Dave S.	2
	Total Misc. Workforce	3

Construction Activity:

American Electrical: Continues to install lighting in ceiling grid at bathrooms.

Lapan: Continue fire caulking.

Dandis: Sanding and painting door frames in corridor and offices.

CJM Services: Continue setting tile at the armory floor.

Barber: Applying final coat of compound in outbuilding.

Belcour: Continue copper roofing at the cupola.

T&C: Applying wood trim along windows in training room.

Capital: Continue tile at men's locker room wet walls.

John Oliveira & Sons: Removed concrete forms from sidewalks.

Clerk's remarks: none

Site Visitors/Meetings: see above

Deliveries: none

Equipment Used: Empire: (2) Boom Lift 600s, Barber (2) Scissor Lift, Commercial: Lull 944E, Mini Bobcat

PROJECT:	Carver Police Station	PROJECT #:		Report Number:	209
-----------------	-----------------------	-------------------	--	-----------------------	-----

Contract Time:	Date: 12-08-2020	
Days Elapsed:	Day: Tuesday	
Extensions:	Weather: Cloudy	
Days Remaining:	Temperature Cycle at 7 AM:	44 – 37 deg.
Site Condition:	Dry	

Contractor	Workforce	
Tower Construction	1 Superintendent, 0 laborer, 0 carpenters – Kevin Thompson (site supervision)	1
Dig It	0 operator, 0 laborer, 0 foreman, 0 dirtworks (sitework)	0
Dandis	1 painter (painting)	1
Delta	0 sprinkler fitters (fire protection)	0
American Electrical	1 foreman, 3 journeyman, 1 apprentice (electrical)	5
Lapan	0 foreman, 0 journeyman, 0 apprentice, 0 insulator (mechanical)	0
Belcour	1 roofer (roofing)	1
Central Ceilings	0 carpenter (acoustical ceilings)	0
Hareld Glass	2 glazers (storefront)	2
Debrino	0 caulker (join sealant)	0
CJM Services	1 carpenter (resilient)	1
T&C	0 carpenters (millwork)	0
John Oliveira & Sons	0 carpenters (formwork)	0
G&H	0 foreman, 0 apprentice, 0 journeyman, 0 insulator (HVAC)	0
Capital	2 tilers (ceramic)	2
Barber Drywall	0 foreman, 1 apprentice, 1 carpenters, 0 taper (exterior framing)	2
	Total Workforce	15

Miscellaneous Others		
CHA	Alyssa Chatani	1
Town of Carver	Bill Harriman, Dave S.	2
JHA	Brian Humes	1
Alrington Towing	2 reps.	2
Dig It	Removing office trailer.	2
	Total Misc. Workforce	8

Construction Activity:

American Electrical: Installing overhead lighting in corridor areas. Fire caulking above ceiling.

Belcour: Continue copper at roof cupola.

Dandis: Applying window trim paint at interior casework areas.

CJM Services: Sanding down flooring in the women's locker room.

Barber: Continue taping wallboard at attic area and locker rooms.

Hareld: Placing glass panels inside of door frames along corridor areas.

Capital: Installing wall tile in the bathroom #137.

Clerk's remarks: none

Site Visitors/Meetings: see above

Deliveries: none

Equipment Used: Empire: (2) Boom Lift 600s, Barber (2) Scissor Lift, Commercial: Lull 944E, Mini Bobcat



ON-SITE REPRESENTATIVE DAILY REPORT

PROJECT:	Carver Police Station	PROJECT #:		Report Number:	210
-----------------	-----------------------	-------------------	--	-----------------------	-----

Contract Time:	Date: 12-09-2020	
Days Elapsed:	Day: Wednesday	
Extensions:	Weather: Cloudy	
Days Remaining:	Temperature Cycle at 7 AM:	28 – 36 deg.
Site Condition:	Dry	

Contractor	Workforce	
Tower Construction	1 Superintendent, 0 laborer, 2 carpenters – Kevin Thompson (site supervision)	3
Dig It	0 operator, 0 laborer, 0 foreman, 0 dirtworks (sitework)	0
Dandis	1 painter (painting)	1
Delta	0 sprinkler fitters (fire protection)	0
American Electrical	1 foreman, 2 journeyman, 1 apprentice (electrical)	4
Lapan	0 foreman, 0 journeyman, 0 apprentice, 0 insulator (mechanical)	0
Belcour	0 roofer (roofing)	0
Central Ceilings	0 carpenter (acoustical ceilings)	0
Hareld Glass	0 glazers (storefront)	0
Debrino	0 caulker (join sealant)	0
CJM Services	0 carpenter (resilient)	0
T&C	0 carpenters (millwork)	0
John Oliveira & Sons	0 carpenters (formwork)	0
G&H	0 foreman, 0 apprentice, 0 journeyman, 0 insulator (HVAC)	0
Capital	2 tilers (ceramic)	2
Barber Drywall	0 foreman, 1 apprentice, 1 carpenters, 0 taper (exterior framing)	2
	Total Workforce	12

Miscellaneous Others		
CHA	Alyssa Chatani, Joe Sullivan	2
Town of Carver	Bill Harriman	1
	Total Misc. Workforce	3

Construction Activity:

American Electrical: Pulling secondary wiring into electrical room from new transformer. Continue fire caulking above the ceiling.

Dandis: Applied door frame paint in detention area and corridor.

CJM Services: Not on site.

Barber: Sanding sheet rock in the outbuilding and inside the attic access area.

Debrino: Not on site.

Hareld: Not on site.

Capital: Placing tile flooring in the training room, finished tile in the bathroom #137.

Clerk's remarks: Tower is installing doors inside detention area, sally port and attic areas.

Site Visitors/Meetings: see above

Deliveries: door delivery from national lumber

Equipment Used: Empire: (2) Boom Lift 600s, Barber (2) Scissor Lift, Commercial: Lull 944E, Mini Bobcat

PROJECT:	Carver Police Station	PROJECT #:		Report Number:	211
-----------------	-----------------------	-------------------	--	-----------------------	-----

Contract Time:	Date: 12-10-2020	
Days Elapsed:	Day: Thursday	
Extensions:	Weather: Clear	
Days Remaining:	Temperature Cycle at 7 AM:	29 – 48 deg.
Site Condition:	Dry	

Contractor	Workforce	
Tower Construction	1 Superintendent, 0 laborer, 0 carpenters – Kevin Thompson (site supervision)	1
Dig It	0 operator, 0 laborer, 0 foreman, 0 dirtworks (sitework)	0
Dandis	1 painter (painting)	1
Delta	0 sprinkler fitters (fire protection)	0
American Electrical	1 foreman, 3 journeyman, 1 apprentice (electrical)	5
Lapan	0 foreman, 0 journeyman, 0 apprentice, 0 insulator (mechanical)	0
Belcour	1 roofer (roofing)	1
Central Ceilings	0 carpenter (acoustical ceilings)	0
Hareld Glass	0 glazers (storefront)	0
Debrino	0 caulker (join sealant)	0
CJM Services	0 carpenter (resilient)	0
T&C	0 carpenters (millwork)	0
John Oliveira & Sons	0 carpenters (formwork)	0
G&H	0 foreman, 0 apprentice, 0 journeyman, 0 insulator (HVAC)	0
Capital	1 tiler (ceramic)	1
Barber Drywall	0 foreman, 0 apprentice, 0 carpenters, 0 taper (exterior framing)	0
	Total Workforce	9

Miscellaneous Others		
CHA	Alyssa Chatani	1
Town of Carver	Bill Harriman, Dave Siedentopf	2
Carver Police	Mike Shaw	1
E911	Scott Gray	1
Quality Insulation	Continue insulating main building attic.	2
	Total Misc. Workforce	7

Construction Activity:

American Electrical: Pulling secondary wiring from generator to transfer switched and from the transfer switch to the electrical room. Continue fire caulking above ceiling.

Delta: Not on site.

Dandis: Applying primer and one coat of paint in interior column training.

CJM Services: Not on site.

Belcour: Continue copper cupola.

Debrino: Not on site.

Capital: Continue installing border tile in training room.

Clerk's remarks: none

Site Visitors/Meetings: see above

Deliveries: door delivery from national lumber

Equipment Used: Empire: (2) Boom Lift 600s, Barber (2) Scissor Lift, Commercial: Lull 944E, Mini Bobcat

PROJECT:	Carver Police Station	PROJECT #:		Report Number:	212
-----------------	-----------------------	-------------------	--	-----------------------	-----

Contract Time:	Date: 12-11-2020	
Days Elapsed:	Day: Thursday	
Extensions:	Weather: Clear	
Days Remaining:	Temperature Cycle at 7 AM:	28 – 53 deg.
Site Condition:	Dry	

Contractor	Workforce	
Tower Construction	1 Superintendent, 0 laborer, 0 carpenters – Kevin Thompson (site supervision)	1
Dig It	1 operator, 2 laborer, 1 foreman, 0 dirtworks (sitework)	4
Dandis	1 painter (painting)	1
Delta	0 sprinkler fitters (fire protection)	0
American Electrical	1 foreman, 3 journeyman, 1 apprentice (electrical)	5
Lapan	0 foreman, 0 journeyman, 0 apprentice, 0 insulator (mechanical)	0
Belcour	2 roofer (roofing)	2
Central Ceilings	1 carpenter (acoustical ceilings)	1
Hareld Glass	0 glazers (storefront)	0
Debrino	0 caulker (join sealant)	0
CJM Services	0 carpenter (resilient)	0
T&C	0 carpenters (millwork)	0
John Oliveira & Sons	0 carpenters (formwork)	0
G&H	0 foreman, 0 apprentice, 0 journeyman, 0 insulator (HVAC)	0
Capital	1 tiler (ceramic)	1
Barber Drywall	0 foreman, 0 apprentice, 0 carpenters, 0 taper (exterior framing)	0
	Total Workforce	15

Miscellaneous Others		
CHA	Alyssa Chatani	1
Town of Carver	Bill Harriman	1
Carver Police	Mike Shaw	1
New Era	Installing security wiring in Comm. room.	2
	Total Misc. Workforce	5

Construction Activity:

American Electrical: Terminating secondary wiring in transfer junction box. Completed fire caulking in main building. Secured wire in sally port.

Dig It: Installing rain leader catch basin in the front of the building. Continue to spread loam.

Dandis: Priming the fitness room in the outbuilding and continue door frames inside lobby.

Central: Installed drop ceiling grid in the dispatch room and lighting tie in.

Belcour: Completed copper roofing at the cupola. Installed boots on sally port roof.

Debrino: Not on site.

Capital: Continue tile in training room.

Clerk's remarks: none

Site Visitors/Meetings: see above

Deliveries: door delivery from national lumber

Equipment Used: Empire: (2) Boom Lift 600s, Barber (2) Scissor Lift, Commercial: Lull 944E, Mini Bobcat

PROJECT:	Carver Police Station	PROJECT #:		Report Number:	213
-----------------	-----------------------	-------------------	--	-----------------------	-----

Contract Time:	Date: 12-14-2020	
Days Elapsed:	Day: Monday	
Extensions:	Weather: Clear	
Days Remaining:	Temperature Cycle at 7 AM:	34 – 45 deg.
Site Condition:	Dry	

Contractor	Workforce	
Tower Construction	1 Superintendent, 0 laborer, 0 carpenters – Kevin Thompson (site supervision)	1
Dig It	0 operator, 0 laborer, 0 foreman, 0 dirtworks (sitework)	0
Dandis	1 painter (painting)	1
Delta	0 sprinkler fitters (fire protection)	0
American Electrical	1 foreman, 1 journeyman, 0 apprentice (electrical)	2
Lapan	0 foreman, 0 journeyman, 0 apprentice, 0 insulator (mechanical)	0
Belcour	0 roofer (roofing)	0
Central Ceilings	0 carpenter (acoustical ceilings)	0
Hareld Glass	0 glazers (storefront)	0
Debrino	0 caulker (join sealant)	0
CJM Services	2 carpenter (resilient)	2
T&C	2 carpenters (millwork)	2
John Oliveira & Sons	0 carpenters (formwork)	0
G&H	0 foreman, 1 apprentice, 1 journeyman, 0 insulator (HVAC)	2
Capital	1 tiler (ceramic)	1
Barber Drywall	0 foreman, 0 apprentice, 0 carpenters, 0 taper (exterior framing)	0
	Total Workforce	11

Miscellaneous Others		
CHA	Alyssa Chatani	1
Town of Carver	Bill Harriman	1
Carver Police	Chief Duphily	1
Quality Insulation	Continue insulation at attic.	2
	Total Misc. Workforce	5

Construction Activity:

American Electrical: Installing feeder secondary wiring into main transfer switch.

Dig It: Not on site.

Dandis: Painting detention area and fitness room.

CJM Services: Placing flooring in interview rooms and prepped locker area.

G&H: Laying out RGDs in offices.

T&C: Continue trim in training room.

Capital: Continue training room tile.

Clerk's remarks: none

Site Visitors/Meetings: see above

Deliveries: none

Equipment Used: Empire: (2) Boom Lift 600s, Barber (2) Scissor Lift, Commercial: Lull 944E, Mini Bobcat

PROJECT:	Carver Police Station	PROJECT #:		Report Number:	214
-----------------	-----------------------	-------------------	--	-----------------------	-----

Contract Time:	Date: 12-15-2020	
Days Elapsed:	Day: Tuesday	
Extensions:	Weather: Clear	
Days Remaining:	Temperature Cycle at 7 AM:	26 – 38 deg.
Site Condition:	Dry	

Contractor	Workforce	
Tower Construction	1 Superintendent, 0 laborer, 0 carpenters – Kevin Thompson (site supervision)	1
Dig It	0 operator, 0 laborer, 1 foreman, 0 dirtworks (sitework)	1
Dandis	1 painter (painting)	1
Delta	0 sprinkler fitters (fire protection)	0
American Electrical	1 foreman, 1 journeyman, 1 apprentice (electrical)	3
Lapan	0 foreman, 0 journeyman, 0 apprentice, 0 insulator (mechanical)	0
Belcour	0 roofer (roofing)	0
Central Ceilings	0 carpenter (acoustical ceilings)	0
Hareld Glass	0 glazers (storefront)	0
Debrino	0 caulker (join sealant)	0
CJM Services	2 carpenter (resilient)	2
T&C	0 carpenters (millwork)	0
John Oliveira & Sons	0 carpenters (formwork)	0
G&H	0 foreman, 0 apprentice, 2 journeyman, 0 insulator, 2 controls (HVAC)	4
Capital	2 tilers (ceramic)	2
Barber Drywall	0 foreman, 0 apprentice, 0 carpenters, 0 taper (exterior framing)	0
	Total Workforce	14

Miscellaneous Others		
CHA	Alyssa Chatani	1
Town of Carver	Bill Harriman, Dave Siedentopf	1
Carver Fire	Chief Weston & Elaine, Deputy Eric, Asst Deputy Jesse Boyle	4
Quality Insulation	Completed the main building insulation at the attic.	2
Hastie	Started exterior wood guardrail.	4
	Total Misc. Workforce	12

Construction Activity:

American Electrical: Continue the electrical secondary terminations in the electrical room panel.

Dig It: Assist with the placement of the wood guardrail.

Dandis: Installed final coat of paint along ceiling grid and fitness room.

CJM Services: Installing flooring at the locker room area.

G&H: Installing grills and connecting ductwork at the RGDs.

T&C: Not on site.

Capital: Placing tile around the training room.

Clerk's remarks: Above head inspection by CFD

Site Visitors/Meetings: see above

Deliveries: none

Equipment Used: Empire: (2) Boom Lift 600s, Barber (2) Scissor Lift, Commercial: Lull 944E, Mini Bobcat

PROJECT:	Carver Police Station	PROJECT #:		Report Number:	215
-----------------	-----------------------	-------------------	--	-----------------------	-----

Contract Time:	Date: 12-16-2020	
Days Elapsed:	Day: Wednesday	
Extensions:	Weather: Cloudy	
Days Remaining:	Temperature Cycle at 7 AM:	26 – 39 deg.
Site Condition:	Dry	

Contractor	Workforce	
Tower Construction	1 Superintendent, 0 laborer, 0 carpenters – Kevin Thompson (site supervision)	1
Dig It	0 operator, 0 laborer, 0 foreman, 0 dirtworks (sitework)	0
Dandis	0 painter (painting)	0
Delta	0 sprinkler fitters (fire protection)	0
American Electrical	1 foreman, 1 journeyman, 0 apprentice (electrical)	2
Lapan	0 foreman, 0 journeyman, 0 apprentice, 0 insulator (mechanical)	0
Belcour	0 roofer (roofing)	0
Central Ceilings	0 carpenter (acoustical ceilings)	0
Hareld Glass	0 glazers (storefront)	0
Debrino	0 caulker (join sealant)	0
CJM Services	2 carpenter (resilient)	2
T&C	2 carpenters (millwork)	2
PSI	6 installers (lockers)	6
G&H	0 foreman, 0 apprentice, 2 journeyman, 0 insulator, 0 controls (HVAC)	2
Capital	2 tilers (ceramic)	2
Barber Drywall	0 foreman, 0 apprentice, 0 carpenters, 0 taper (exterior framing)	0
	Total Workforce	17

Miscellaneous Others		
CHA	Alyssa Chatani	1
Town of Carver	Bill Harriman, Town Administrator Rick LaFond, Admin. Assistant Elaine Weston	3
Carver Police	Chief Duphily, Sgt. Bryan Berriault, Mike Shaw	3
Select Board	Sarah Hewins-Chair, Mark Townsend, James Hoffman, Jennifer Bogat	4
Hastie Fence	Started privacy fencing behind sally port.	4
	Total Misc. Workforce	15

Construction Activity:

American Electrical: Wiring up breaker panels inside of electrical room, installing breaker.

PSI: Started the locker installation in men's and women's locker rooms.

Dandis: Not on site.

CJM Services: Installing floor covering.

G&H: Installing diffusers in offices, connecting the ductwork to grilles.

T&C: Working on the bullnose trim in training room.

Capital: Continues to work on tile in training room.

Clerk's remarks: Select board walk-through.

Site Visitors/Meetings: see above

Deliveries: ceiling tiles, lockers, diffusers

Equipment Used: Empire: (2) Boom Lift 600s, Barber (2) Scissor Lift, Commercial: Lull 944E, Mini Bobcat



ON-SITE REPRESENTATIVE DAILY REPORT

PROJECT:	Carver Police Station	PROJECT #:		Report Number:	216
-----------------	-----------------------	-------------------	--	-----------------------	-----

Contract Time:	Date: 12-17-2020	
Days Elapsed:	Day: Thursday	
Extensions:	Weather: Snow	
Days Remaining:	Temperature Cycle at 7 AM:	
Site Condition:	Dry	

Contractor	Workforce	
Tower Construction	0 Superintendent, 0 laborer, 0 carpenters – Kevin Thompson (site supervision)	0
Dig It	0 operator, 0 laborer, 0 foreman, 0 dirtworks (sitework)	0
Dandis	0 painter (painting)	0
Delta	0 sprinkler fitters (fire protection)	0
American Electrical	0 foreman, 0 journeyman, 0 apprentice (electrical)	0
Lapan	0 foreman, 0 journeyman, 0 apprentice, 0 insulator (mechanical)	0
Belcour	0 roofer (roofing)	0
Central Ceilings	0 carpenter (acoustical ceilings)	0
Hareld Glass	0 glazers (storefront)	0
Debrino	0 caulker (join sealant)	0
CJM Services	0 carpenter (resilient)	0
T&C	0 carpenters (millwork)	0
PSI	6 installers (lockers)	6
G&H	0 foreman, 0 apprentice, 0 journeyman, 0 insulator, 0 controls (HVAC)	0
Capital	0 tilers (ceramic)	0
Barber Drywall	0 foreman, 0 apprentice, 0 carpenters, 0 taper (exterior framing)	0
	Total Workforce	6

Miscellaneous Others		
CHA	Alyssa Chatani	0
Town of Carver	Bill Harriman, Dave Siedentopf	2
	Total Misc. Workforce	2

Construction Activity:

American Electrical: Not on site.

PSI: Continue locker installation in men's and women's locker rooms.

Dandis: Not on site.

CJM Services: Not on site.

G&H: Not on site.

T&C: Not on site.

Capital: Not on site.

Clerk's remarks: Snow Day

Site Visitors/Meetings: see above

Deliveries: none

Equipment Used: Empire: (2) Boom Lift 600s, Barber (2) Scissor Lift, Commercial: Lull 944E, Mini Bobcat

PROJECT:	Carver Police Station	PROJECT #:		Report Number:	217
-----------------	-----------------------	-------------------	--	-----------------------	-----

Contract Time:	Date: 12-18-2020	
Days Elapsed:	Day: Friday	
Extensions:	Weather: Cloudy	
Days Remaining:	Temperature Cycle at 7 AM:	26 – 32 deg.
Site Condition:	Dry	

Contractor	Workforce	
Tower Construction	1 Superintendent, 0 laborer, 1 carpenter – Kevin Thompson (site supervision)	2
Dig It	0 operator, 0 laborer, 0 foreman, 0 dirtworks (sitework)	0
Dandis	0 painter (painting)	0
Delta	1 sprinkler fitter (fire protection)	1
American Electrical	1 foreman, 1 journeyman, 0 apprentice (electrical)	2
Lapan	0 foreman, 0 journeyman, 0 apprentice, 0 insulator (mechanical)	0
Belcour	0 roofer (roofing)	0
Central Ceilings	0 carpenter (acoustical ceilings)	0
Hareld Glass	0 glazers (storefront)	0
Debrino	0 caulker (join sealant)	0
CJM Services	0 carpenter (resilient)	0
T&C	2 carpenters (millwork)	2
PSI	6 installers (lockers)	6
G&H	0 foreman, 1 apprentice, 1 journeyman, 0 insulator, 0 controls (HVAC)	2
Capital	1 tiler (ceramic)	1
Barber Drywall	0 foreman, 0 apprentice, 0 carpenters, 0 taper (exterior framing)	0
	Total Workforce	17

Miscellaneous Others		
CHA	Alyssa Chatani	1
Town of Carver	Bill Harriman, Dave Siedentopf	2
BER	Electrical Engineer, Mechanical Engineer	2
Carver Police	Chief Duphily, Mike Shaw, Bill Kelley, Austin Alves	4
Hastie Fence	Completed fencing next to the transformer.	4
New Era	Pulling wiring into intercom box at lobby.	1
	Total Misc. Workforce	14

Construction Activity:

American Electrical: Wiring up overhead lighting in corridor and finishing up panels in electrical room.

PSI: Continue locker installation.

Delta: Continue firestopping above ceiling.

CJM Services: Not on site.

G&H: Continues to install RGDs in office and conference room.

T&C: Continue wood trim in training room.

Capital: Installing tile in the men's locker room bathroom floor.

Clerk's remarks: Above ceiling inspections. Tower cut recessed electrical box in lobby.

Site Visitors/Meetings: see above

Deliveries: none

Equipment Used: Empire: (2) Boom Lift 600s, Barber (2) Scissor Lift, Commercial: Lull 944E, Mini Bobcat

PROJECT:	Carver Police Station	PROJECT #:		Report Number:	218
-----------------	-----------------------	-------------------	--	-----------------------	-----

Contract Time:	Date: 12-21-2020	
Days Elapsed:	Day: Monday	
Extensions:	Weather: Cloudy	
Days Remaining:	Temperature Cycle at 7 AM:	26 – 38 deg.
Site Condition:	Dry	

Contractor	Workforce	
Tower Construction	1 Superintendent, 0 laborer, 0 carpenter – Kevin Thompson (site supervision)	1
Dig It	0 operator, 0 laborer, 0 foreman, 0 dirtworks (sitework)	0
Dandis	1 painter (painting)	1
Delta	2 sprinkler fitters (fire protection)	2
American Electrical	1 foreman, 1 journeyman, 0 apprentice (electrical)	2
Lapan	0 foreman, 0 journeyman, 0 apprentice, 0 insulator (mechanical)	0
Belcour	0 roofer (roofing)	0
Central Ceilings	0 carpenter (acoustical ceilings)	0
Hareld Glass	0 glazers (storefront)	0
Debrino	0 caulker (join sealant)	0
CJM Services	0 carpenter (resilient)	0
T&C	2 carpenters (millwork)	2
PSI	0 installers (lockers)	0
G&H	0 foreman, 1 apprentice, 1 journeyman, 0 insulator, 0 controls (HVAC)	2
Capital	2 tilers (ceramic)	2
Barber Drywall	0 foreman, 0 apprentice, 0 carpenters, 1 taper (exterior framing)	1
	Total Workforce	13

Miscellaneous Others		
CHA	Alyssa Chatani	1
Town of Carver	Bill Harriman, Dave Siedentopf, Dave Robertson	3
Hastie Fence	Placing vinyl fencing along the backside of the transformer area.	3
	Total Misc. Workforce	7

Construction Activity:

American Electrical: Terminating wiring inside the electrical room panels and continue installing lights.

Dandis: Painting has installed another coat of painting on the detention area.

Delta: Installing heads inside of the detention room.

T&C: Placing trim along the training room at the wainscoting areas.

G&H: Placing diffusers in ceiling grid in the conference room and chief's office.

Barber: Placing compound in dispatch room and touching up bathrooms.

Capital: Placing floor tile inside of men's locker room bathroom.

Clerk's remarks: none

Site Visitors/Meetings: see above

Deliveries: none

Equipment Used: Empire: (2) Boom Lift 600s, Barber (2) Scissor Lift, Commercial: Lull 944E, Mini Bobcat

PROJECT:	Carver Police Station	PROJECT #:		Report Number:	219
-----------------	-----------------------	-------------------	--	-----------------------	-----

Contract Time:	Date: 12-22-2020	
Days Elapsed:	Day: Tuesday	
Extensions:	Weather: Cloudy	
Days Remaining:	Temperature Cycle at 7 AM:	28 – 39 deg.
Site Condition:	Dry	

Contractor	Workforce	
Tower Construction	1 Superintendent, 0 laborer, 0 carpenter – Kevin Thompson (site supervision)	1
Dig It	1 operator, 1 laborer, 1 foreman, 0 dirtworks (sitework)	3
Dandis	1 painter (painting)	1
Delta	2 sprinkler fitters (fire protection)	2
American Electrical	1 foreman, 1 journeyman, 0 apprentice (electrical)	2
Lapan	0 foreman, 0 journeyman, 0 apprentice, 0 insulator (mechanical)	0
Belcour	0 roofer (roofing)	0
Central Ceilings	0 carpenter (acoustical ceilings)	0
Hareld Glass	0 glazers (storefront)	0
Debrino	0 caulker (join sealant)	0
CJM Services	0 carpenter (resilient)	0
T&C	2 carpenters (millwork)	2
Division 10	2 installers (specialties)	2
G&H	0 foreman, 0 apprentice, 0 journeyman, 0 insulator, 0 controls (HVAC)	0
Capital	1 tiler (ceramic)	1
Barber Drywall	0 foreman, 0 apprentice, 0 carpenters, 0 taper (exterior framing)	0
	Total Workforce	14

Miscellaneous Others		
CHA	Alyssa Chatani	1
Town of Carver	Bill Harriman, Dave Siedentopf	2
Carver Police	Chief Duphily	1
Hastie Fence	Continue with fence towards outbuilding and setting poles.	3
	Total Misc. Workforce	7

Construction Activity:

American Electrical: Continue to terminate wiring inside of Comm. room.

Dandis: Painting training room and around the columns.

Delta: Working on sprinkler head brackets inside main building.

Dig It: Removing snow and placing fill inside impound area.

Division 10: Installed overhead projection screen in the training room.

T&C: Placing countertops inside of dispatch area and fastening to cabinets.

Capital: Finishing up remaining floor tile in and around the columns.

Clerk's remarks: none

Site Visitors/Meetings: see above

Deliveries: none

Equipment Used: Empire: (2) Boom Lift 600s, Barber (2) Scissor Lift, Commercial: Lull 944E, Mini Bobcat

PROJECT:	Carver Police Station	PROJECT #:		Report Number:	220
-----------------	-----------------------	-------------------	--	-----------------------	-----

Contract Time:	Date: 12-23-2020	
Days Elapsed:	Day: Wednesday	
Extensions:	Weather: Overcast	
Days Remaining:	Temperature Cycle at 7 AM:	31 – 44 deg.
Site Condition:	Dry	

Contractor	Workforce	
Tower Construction	1 Superintendent, 0 laborer, 0 carpenter – Kevin Thompson (site supervision)	1
Dig It	1 operator, 2 laborer, 1 foreman, 0 dirtworks (sitework)	4
Dandis	2 painters (painting)	2
Delta	0 sprinkler fitters (fire protection)	0
American Electrical	1 foreman, 1 journeyman, 0 apprentice (electrical)	2
Lapan	0 foreman, 0 journeyman, 0 apprentice, 0 insulator (mechanical)	0
Belcour	0 roofer (roofing)	0
Central Ceilings	0 carpenter (acoustical ceilings)	0
Hareld Glass	0 glazers (storefront)	0
Debrino	0 caulker (join sealant)	0
CJM Services	0 carpenter (resilient)	0
T&C	2 carpenters (millwork)	2
Division 10	0 installers (specialties)	0
G&H	0 foreman, 1 apprentice, 1 journeyman, 0 insulator, 0 controls (HVAC)	2
Capital	2 tilers (ceramic)	2
Barber Drywall	0 foreman, 0 apprentice, 0 carpenters, 0 taper (exterior framing)	0
	Total Workforce	15

Miscellaneous Others		
CHA	Alyssa Chatani	0
Town of Carver	Bill Harriman, Bob Francis	2
Hastie Fence	Placing chain link from outbuilding to secondary road.	3
	Total Misc. Workforce	5

Construction Activity:

American Electrical: Working in communications room wiring, connections above panel.

Dandis: Finishing detention area paint, trim on windows.

Delta: Not on site.

Dig It: Setting precast curbing around the impound lot area.

G&H: Installing return grills in office room, connecting ductwork to grid.

T&C: Placing baseboard and wainscoting in training room.

Capital: Installing tile flooring in women's locker room and grouting.

Clerk's remarks: Bob Francis inspected above ceiling and signed permit card.

Site Visitors/Meetings: see above

Deliveries: communication racks

Equipment Used: Empire: (2) Boom Lift 600s, Barber (2) Scissor Lift, Commercial: Lull 944E, Mini Bobcat

PROJECT:	Carver Police Station	PROJECT #:		Report Number:	221
-----------------	-----------------------	-------------------	--	-----------------------	-----

Contract Time:	Date: 12-24-2020	
Days Elapsed:	Day: Thursday	
Extensions:	Weather: Clear	
Days Remaining:	Temperature Cycle at 7 AM:	31 – 52 deg.
Site Condition:	Dry	

Contractor	Workforce	
Tower Construction	1 Superintendent, 0 laborer, 0 carpenter – Kevin Thompson (site supervision)	1
Dig It	0 operator, 0 laborer, 0 foreman, 0 dirtworks (sitework)	0
Dandis	1 painter (painting)	1
Delta	0 sprinkler fitters (fire protection)	0
American Electrical	1 foreman, 1 journeyman, 1 apprentice (electrical)	3
Lapan	0 foreman, 0 journeyman, 0 apprentice, 0 insulator (mechanical)	0
Belcour	0 roofer (roofing)	0
Central Ceilings	0 carpenter (acoustical ceilings)	0
Hareld Glass	0 glazers (storefront)	0
Debrino	0 caulker (join sealant)	0
CJM Services	0 carpenter (resilient)	0
T&C	0 carpenters (millwork)	0
Division 10	0 installers (specialties)	0
G&H	0 foreman, 1 apprentice, 1 journeyman, 0 insulator, 0 controls (HVAC)	2
Capital	0 tilers (ceramic)	0
Barber Drywall	0 foreman, 0 apprentice, 0 carpenters, 0 taper (exterior framing)	0
	Total Workforce	7

Miscellaneous Others		
CHA	Joe Sullivan	1
Town of Carver	Bill Harriman	1
Hastie Fence	Connected chain link fencing to outbuilding section to access road.	2
	Total Misc. Workforce	4

Construction Activity:

American Electrical: Installed UPS in the communications room and racks, installed lights in the outbuilding.

Dandis: Priming in fire pump room, painted access to attic in the main building.

Delta: Not on site.

Dig It: Not on site.

G&H: Continue to place diffusers in the training room and the dentition areas.

T&C: Not on site.

Capital: Not on site.

Clerk's remarks: none

Site Visitors/Meetings: see above

Deliveries: none

Equipment Used: Empire: (2) Boom Lift 600s, Barber (2) Scissor Lift, Commercial: Lull 944E, Mini Bobcat

PROJECT:	Carver Police Station	PROJECT #:		Report Number:	222
-----------------	-----------------------	-------------------	--	-----------------------	-----

Contract Time:	Date: 12-28-2020	
Days Elapsed:	Day: Monday	
Extensions:	Weather: Clear	
Days Remaining:	Temperature Cycle at 7 AM:	31 – 52 deg.
Site Condition:	Dry	

Contractor	Workforce	
Tower Construction	0 Superintendent, 0 laborer, 2 carpenters – Kevin Thompson (site supervision)	2
Dig It	1 operator, 1 laborer, 1 foreman, 0 dirtworks (sitework)	3
Dandis	0 painter (painting)	0
Delta	0 sprinkler fitters (fire protection)	0
American Electrical	1 foreman, 1 journeyman, 0 apprentice (electrical)	2
Lapan	0 foreman, 0 journeyman, 0 apprentice, 0 insulator (mechanical)	0
Belcour	0 roofer (roofing)	0
Central Ceilings	0 carpenter (acoustical ceilings)	0
Hareld Glass	2 glazers (storefront)	2
Debrino	0 caulker (join sealant)	0
CJM Services	0 carpenter (resilient)	0
T&C	0 carpenters (millwork)	0
Division 10	0 installers (specialties)	0
G&H	0 foreman, 1 apprentice, 1 journeyman, 0 insulator, 0 controls (HVAC)	2
Capital	2 tilers (ceramic)	2
Barber Drywall	0 foreman, 0 apprentice, 0 carpenters, 0 taper (exterior framing)	0
	Total Workforce	13

Miscellaneous Others		
CHA	Alyssa Chatani	1
Town of Carver	Bill Harriman	1
Hastie Fence	Continue fence installation by the outbuilding.	3
	Total Misc. Workforce	5

Construction Activity:

American Electrical: Continue working on lighting controls.

Dandis: Not on site.

Delta: Not on site.

Dig It: Continue spreading loam.

G&H: Placing ductwork connections in the grills and diffusers.

Hareld: Punch list items and replacing the broken glass in the training room.

Capital: Continue ceramic tile in training room storage room and kitchenette and in men's toilet room.

Tower: Site supervision, installed evidence lockers and installed downspout boots.

Clerk's remarks: none

Site Visitors/Meetings: see above

Deliveries: none

Equipment Used: Empire: (2) Boom Lift 600s, Barber (2) Scissor Lift, Commercial: Lull 944E, Mini Bobcat

PROJECT:	Carver Police Station	PROJECT #:		Report Number:	223
-----------------	-----------------------	-------------------	--	-----------------------	-----

Contract Time:	Date: 12-29-2020	
Days Elapsed:	Day: Tuesday	
Extensions:	Weather: Cloudy	
Days Remaining:	Temperature Cycle at 7 AM:	22 – 31 deg.
Site Condition:	Dry	

Contractor	Workforce	
Tower Construction	1 Superintendent, 0 laborer, 0 carpenters – Kevin Thompson (site supervision)	1
Dig It	1 operator, 1 laborer, 1 foreman, 0 dirtworks (sitework)	3
Dandis	0 painter (painting)	0
Delta	0 sprinkler fitters (fire protection)	0
American Electrical	1 foreman, 1 journeyman, 0 apprentice (electrical)	2
Lapan	0 foreman, 0 journeyman, 0 apprentice, 0 insulator (mechanical)	0
Belcour	0 roofer (roofing)	0
Central Ceilings	0 carpenter (acoustical ceilings)	0
Hareld Glass	0 glazers (storefront)	0
Debrino	0 caulker (join sealant)	0
CJM Services	0 carpenter (resilient)	0
T&C	2 carpenters (millwork)	2
Division 10	0 installers (specialties)	0
G&H	0 foreman, 1 apprentice, 1 journeyman, 0 insulator, 0 controls (HVAC)	2
Capital	1 tiler (ceramic)	1
Barber Drywall	0 foreman, 0 apprentice, 0 carpenters, 0 taper (exterior framing)	0
	Total Workforce	11

Miscellaneous Others		
CHA	Alyssa Chatani	1
Town of Carver	Bill Harriman	1
Hastie Fence	Continue to install fencing around the outbuilding with poles and support bracing.	3
Next Generation	Finished installing overhead door in outbuilding.	1
	Total Misc. Workforce	6

Construction Activity:

American Electrical: Placing devices in the ceiling grid, and finishing light wiring.

Dandis: Not on site.

Delta: Not on site.

Dig It: Installing the remaining curbing next to sally port.

G&H: Placing ductwork connections in the grills and diffusers.

T&C: Installing baseboard and window trim in the training room.

Capital: Grouting men's locker room and bathroom floor. Setting base tile.

Clerk's remarks: none

Site Visitors/Meetings: see above

Deliveries: none

Equipment Used: Empire: (2) Boom Lift 600s, Barber (2) Scissor Lift, Commercial: Lull 944E, Mini Bobcat

PROJECT:	Carver Police Station	PROJECT #:		Report Number:	224
-----------------	-----------------------	-------------------	--	-----------------------	-----

Contract Time:	Date: 12-30-2020	
Days Elapsed:	Day: Wednesday	
Extensions:	Weather: Overcast	
Days Remaining:	Temperature Cycle at 7 AM:	26 – 32 deg.
Site Condition:	Dry	

Contractor	Workforce	
Tower Construction	1 Superintendent, 0 laborer, 0 carpenters – Kevin Thompson (site supervision)	1
Dig It	1 operator, 1 laborer, 1 foreman, 0 dirtworks (sitework)	3
Dandis	0 painter (painting)	0
Delta	0 sprinkler fitters (fire protection)	0
American Electrical	1 foreman, 1 journeyman, 1 apprentice (electrical)	3
Lapan	0 foreman, 1 journeyman, 0 apprentice, 0 insulator (mechanical)	1
Belcour	0 roofer (roofing)	0
Central Ceilings	0 carpenter (acoustical ceilings)	0
Hareld Glass	0 glazers (storefront)	0
Debrino	0 caulker (join sealant)	0
CJM Services	0 carpenter (resilient)	0
T&C	2 carpenters (millwork)	2
New England Floors	1 installers (specialties)	1
G&H	1 foreman, 1 apprentice, 1 journeyman, 0 insulator, 0 controls (HVAC)	3
Capital	1 tiler (ceramic)	1
Barber Drywall	0 foreman, 0 apprentice, 0 carpenters, 0 taper (exterior framing)	0
	Total Workforce	15

Miscellaneous Others		
CHA	Alyssa Chatani	1
Town of Carver	Bill Harriman	1
Carver Police	Chief Duphily, Mike Shaw	2
Hastie Fence	Continue to place chain link face on poles around entrance.	3
	Total Misc. Workforce	7

Construction Activity:

American Electrical: Installing fire alarm devices in the ceiling grid and at the outbuilding.

Lapan: Placing plumbing fixtures in bathrooms.

New England Floors: Grinding down the detention areas for the epoxy.

Dig It: Placing concrete around curbing and cleaning up the site.

G&H: Set last exterior HVAC unit (heat pump) on the exterior pad.

T&C: Installing chair railing in corridor areas.

Capital: Finishing flooring in the training room storage room.

Clerk's remarks: none

Site Visitors/Meetings: see above

Deliveries: plumbing fixtures

Equipment Used: Empire: (2) Boom Lift 600s, Barber (2) Scissor Lift, Commercial: Lull 944E, Mini Bobcat

PROJECT:	Carver Police Station	PROJECT #:		Report Number:	225
-----------------	-----------------------	-------------------	--	-----------------------	-----

Contract Time:	Date: 12-31-2020	
Days Elapsed:	Day: Thursday	
Extensions:	Weather: Rain	
Days Remaining:	Temperature Cycle at 7 AM:	34 – 38 deg.
Site Condition:	Wet	

Contractor	Workforce	
Tower Construction	1 Superintendent, 0 laborer, 0 carpenters – Kevin Thompson (site supervision)	1
Dig It	1 operator, 0 laborer, 1 foreman, 0 dirtworks (sitework)	2
Dandis	0 painter (painting)	0
Delta	0 sprinkler fitters (fire protection)	0
American Electrical	1 foreman, 1 journeyman, 1 apprentice (electrical)	3
Lapan	0 foreman, 0 journeyman, 0 apprentice, 0 insulator (mechanical)	0
Belcour	0 roofer (roofing)	0
Central Ceilings	0 carpenter (acoustical ceilings)	0
Hareld Glass	0 glazers (storefront)	0
Debrino	0 caulker (join sealant)	0
CJM Services	0 carpenter (resilient)	0
T&C	2 carpenters (millwork)	2
New England Floors	1 installers (specialties)	1
G&H	1 foreman, 0 apprentice, 0 journeyman, 0 insulator, 0 controls (HVAC)	1
Capital	1 tiler (ceramic)	1
A/C Painting	2 installers (wallcovering)	2
Barber Drywall	0 foreman, 0 apprentice, 0 carpenters, 0 taper (exterior framing)	0
	Total Workforce	13

Miscellaneous Others		
CHA	Alyssa Chatani	1
Town of Carver	Bill Harriman	1
Hastie Fence	Continue to place chain link fence along the area at the outbuilding.	3
	Total Misc. Workforce	5

Construction Activity:

American Electrical: Working on communication wiring in the communications room and devices in the lobby area.

A/C Painting: Began wall covering in the corridor and conference room.

New England Floors: Grinding out detention flooring for epoxy.

Dig It: Placing concrete around existing curbing along the front of the parking lot.

G&H: Finished outbuilding ductwork and sally port existing louver connections.

T&C: Placing baseboard trim inside training storage room and cutting in sinks.

Capital: Continue grouting bathroom floors off the corridor area.

Clerk's remarks: none

Site Visitors/Meetings: see above

Deliveries: none

Equipment Used: Empire: (2) Boom Lift 600s, Barber (2) Scissor Lift, Commercial: Lull 944E, Mini Bobcat
