

Carver Police Station Carver, MA

MONTHLY PROGRESS REPORT October 2020



Architect:



Jacunski Humes Architects, LLC

General Contractor:



Tower Construction Corp.

Owner's Project Manager:



prepared by:
Daedalus Projects, Inc.

PROJECT
Carver Police Station**PROJECT MANAGER**
Joe Sullivan**CONTRACTOR**
Tower Construction**ON SITE REPRESENTATIVE**
Alyssa Chatani

MONTHLY PROGRESS REPORT - OCTOBER 2020

GENERAL COMMENTARY OF MONTHLY PROGRESS

During the month of October, sitework continued with Dig-It prepping and laying out the site to prepare for binder. They brought in fill to grade and paved the binder course of asphalt. They also helped with the fire suppression line to the outbuilding and the underground conduit for the future gate. After paving, they began the layout of the pre-cast curbing. American Electrical continued the exterior disconnects for HVAC equipment. They continued overhead wiring at the main building and outbuilding for power, fire alarm devices, and lighting. They also installed electrical panels at the electrical room. LaPan installed the outbuilding vent and piping, the water meter, and 1" water line at the outbuilding. They continued copper water connections inside of the mechanical room and installed the water heater and associating piping. G&H continued ductwork in the attic area, installed refrigerant line sets at the main building, and installed condensate connections. They continued mechanical rough-in at the outbuilding including installing the unit heater in the fire pump room. Viking Industries continued ductwork insulation. Commercial Masonry continued CMU walls in the mechanical room and cells to the deck. T&C Woodworking was on site for measuring and layout of the upcoming casework. Barber Drywall continued hanging drywall and taping and sanding walls to prepare for priming. Dandis began priming around door frames and finished walls. They also continued painting exterior trim and the Sally Port walls and piping. Empire continued siding at the cupola edges and PVC at the main entry. They also framed the attic access door and crickets at the roof hatch and security ceilings. Belcour finished the outbuilding roof. Tower continued the outbuilding soffit trim and siding, installed door frames at the outbuilding, and installed wood blocking around the overhead doors at the Sally Port. Debrino caulked the exterior PVC gaps and corners, around windows, and the cell area and door frames. They also began caulking the outbuilding PVC trim. Central Ceilings began installing acoustical grid. Bobe Materials met on site for layout of the upcoming wire mesh partitions. JAILS began their security ceilings in the cell areas. Next Generation Doors installed the overhead doors at the Sally Port. Cape Cod Central Vac continued the remaining piping in the corridors for the central vacuum system. American Flag Pole installed the flag pole foundations. New Era continued installing access control wiring. Briggs was on site for compaction testing, asphalt testing, and a wood construction inspection. SWE's structural engineer was on site to inspect the outbuilding trusses. Heads Up Irrigation visited the site to review scope of work and provide the irrigation layout plan. E911, ComTech, Comcast, and Verizon were all on site for a walk-through to review upcoming work. Eversource installed a new utility pole adjacent to the site. DPH performed a preliminary walk-through of the cell area and will return once JHA requests the final inspection. All activities are outlined below.

SCHEDULE COMMENTARY

Tower Construction provided a master schedule with an occupancy date of March 8, 2021.

SAFETY COMPLIANCE

Ongoing safety walks are performed. No outstanding issues. Extra precautions are being taken due to COVID-19; a handwashing sink has been installed on site and all meetings are virtual. Tower Construction had a discussion with subcontractors on site on following safety protocol. They are each filling out a daily COVID-19 safety sheet. CHA is filling out daily health certifications as well.

HOT ITEMS

Coordination of all subcontractors completed for cell ceilings: electrical, sprinkler, HVAC, and security.
The asphalt course of binder was poured with the top coat to be paved in the springtime.

DIVISION 04 – MASONRY**Section 04 20 00 Unit Masonry**

Week of September 28

- Not on site.

Week of October 5

- Building up CMU walls in the mechanical room and cells.

Week of October 12, 19 and 26

- Not on site.

DIVISION 07 – ROOFING & SIDING**Section 074000 Roofing and Siding**

Week of September 28

- Continue shingles at front side of building.
- Putting PVC bead board at entry.
- Working on trim at north side of cupola.

Week of October 5

- Starting to place siding shingles at exterior edge of cupola.
- Continuing to install PVC shingles at rear of cupola.
- Completed rear shingles at rear of cupola.
- Installing shingles at front side of cupola.
- Building and framing around attic access door.

Week of October 12

- Finishing outbuilding roof.
- Working on cupola exterior and PVC shingles.
- Placing exterior PVC shingles on the front side of cupola.

Week of October 19

- Completed cupola trim and siding touch-ups.
- Constructing crickets on roof/hatch security ceilings.

Week of October 26

- Not on site.

DIVISION 09 – FINISHES**Section 09 12 00 Gypsum Board Assemblies**

Week of September 28

- Continue to hang drywall and taping.
- Sheet rocking and taping.

Week of October 5

- Continued to hang drywall and taping continues.
- Continues to install sheet rock and taping.
- Finish hanging Sheetrock. Second coat on corner bead joints.
- Finish wall board taping.
- Continues to finish wall board with taping.

Week of October 12

- Continue finishing wallboard with joint compound at locker rooms and office areas. Continue sanding walls to prepare for priming.
- Continue taping and sanding walls.
- Continue joint compound and sanding interior walls.
- Continue to finish wall board, sanding out walls.

Week of October 19

- Sheet rocking and topping out walls and continue outbuilding framing.
- Topping out walls in main building.

Week of October 26

- Boarding tops and misc. taping.
- Continue taping wallboard sections inside of training room and fire taping above ceiling areas.
- Taping in the training room and touching up walls.
- Taping and sanding training room and fire taping.
- Installing sheetrock on the ceiling of the outbuilding.

DIVISION 21 – FIRE SUPPRESSION**Section 21 00 00 Fire Protection****Week of September 28**

- Testing dry system.

Week of October 5

- Installing water to system to conduct a self-test in systems.
- Placing fire suppression pump at outbuilding.

Week of October 12

- Installing sprinkler piping in outbuilding.
- Continue placing 6” fire main from outbuilding to hydrant.
- Installing fire hydrant next to existing parking lot piping.
- Running a test on fire suppression system on outbuilding.

Week of October 19

- Testing fire suppression system with FD.
- Testing underground fire sprinkler piping at outbuilding.
- Testing underground sprinkler line to outbuilding and hydrant.

Week of October 26

- Not on site.

DIVISION 22 – PLUMBING**Section 22 00 00 Plumbing**

Week of September 28 and October 5

- Not on site.

Week of October 12

- Install outbuilding vent. Install domestic water main.
- Installing vent piping in outbuilding and the water meter.

Week of October 19

- Connecting 1" water line in outbuilding and water meter.
- Installing water line into fire pump room at outbuilding.
- Installing mechanical room piping, water service meter.
- Installing copper water connections inside of mechanical room.
- Installing piping for water heater.

Week of October 26

- Installing water heater.
- Installing water heater piping in mechanical room.

DIVISION 23 – HVAC**Section 23 00 00 HVAC**

Week of September 28

- Continue ductwork in attic.

Week of October 5

- Installing additional ductwork in the attic.
- Placing ductwork inside of attic area to equipment.
- Placing ductwork in attic and to units.

Week of October 12

- Continuing refrigerant lines in main building and ductwork in attic.
- Continue installing ductwork inside the attic area to overhead units.
- Installing the exterior air intake on outbuilding.

Week of October 19

- Continue ductwork install in the attic.
- Installing refrigerant lines inside attic areas.
- Continue refrigerant line sets at attic area.

Week of October 26

- Continue drains at main building. Continue rough in at outbuilding.
- Continue to install line sets in the attic for HVAC units.
- Continue to install pre-manufactured line sets to HVAC units inside the attic areas.
- Continues to install line set terminations to units in attic and installing unit heater in fire pump room in outbuilding.
- Continuing to place line set connections to the new attic mechanical units, installing condensate connections.

DIVISION 26 – ELECTRICAL**Section 26 00 00 Electrical**

Week of September 28

- Continued exterior disconnects.
- Installing exterior disconnects for HVAC equipment.

Week of October 5

- Pulling electrical wire down to switch.
- Continue to pull wire.
- Electrical wire for lighting and switch legs.
- Continue to pull wiring inside of J-boxes to electrical room.
- Continue pulling wire to outlets.

Week of October 12

- Continue wiring into main electrical room.
- Running power wiring for outlets and rights back to electrical room.

Week of October 19

- Continue overhead wiring at main building for power and lighting.
- Continue fire alarm cable wiring.
- Continue install of wiring for lighting and fire alarm.
- Continues to pull wiring back to electrical room.
- Installing electrical panels in electrical room/outbuilding wiring.

Week of October 26

- Building out the electrical room.
- Wiring the outbuilding.
- Placing electrical cabinets inside electrical room.
- Wiring in electrical room and electrical panel installation.
- Installing electrical cabinets inside of electrical room.
- Continue to install panels inside of the electrical room.

DIVISION 31 – EARTHWORK**Section 31 20 00 Earth Moving**

Week of September 28 and October 5

- Not on site.

Week of October 12

- Prepping and laying out the site to prepare for binder.
- Bringing in common fill.
- Working on fire suppression line next to outbuilding.
- Continue working on layout of roadway and bringing in fill.
- Bringing in T-base for road bed.

Week of October 19


- Continue bringing in fill and compacting for binder on Friday.
- Continue prepping for binder.
- Installed underground conduit for future gate.
- Prepping for asphalt pavement and layout.
- Installing roof drain system in main building. Grading for binder.

Week of October 26

- Continue to set elevation markers and grade out west elevation.
- Asphalt paving the binder course.
- Laying out pre-cast curbing in parking area.



Training Room Progress

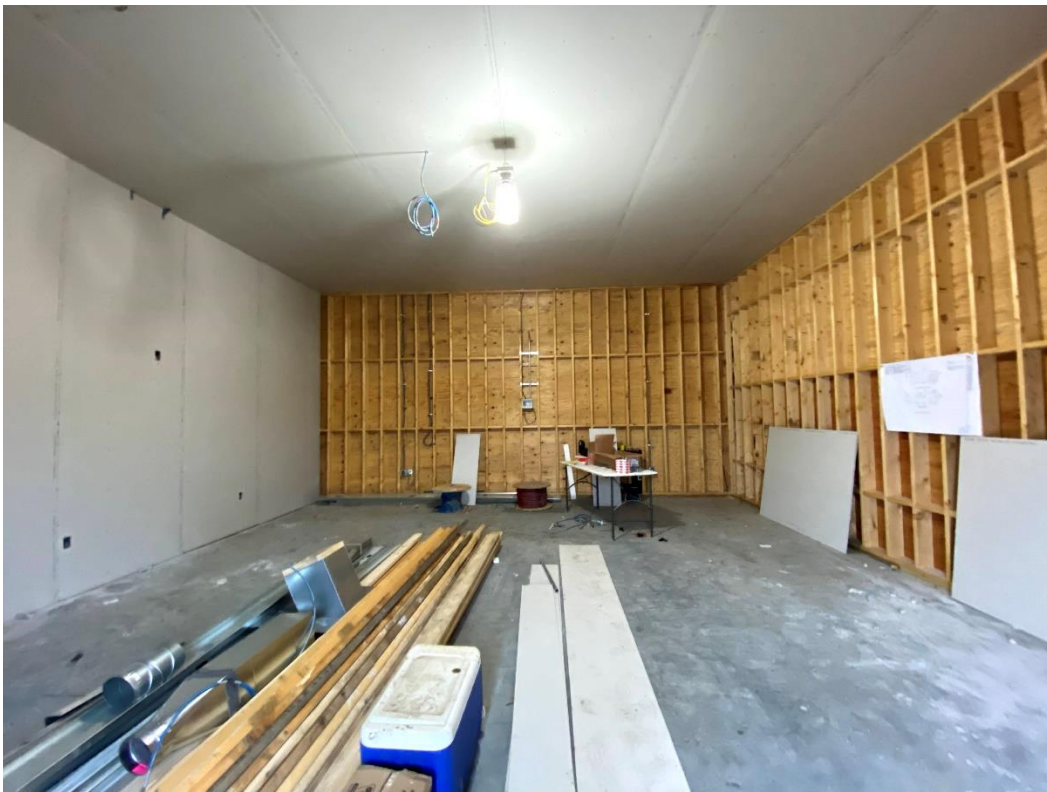

Outbuilding Progress



Acoustical Ceiling Grid Began



Electrical Room Progress



Cupola & Exterior Progress



Mechanical Pad & Exterior Progress



Asphalt Binder Course



Overhead Door Installed at Sally Port



Outbuilding & Main Building Progress




West Exterior Progress




Interior Progress at Dispatch



Interior Progress at Day Room

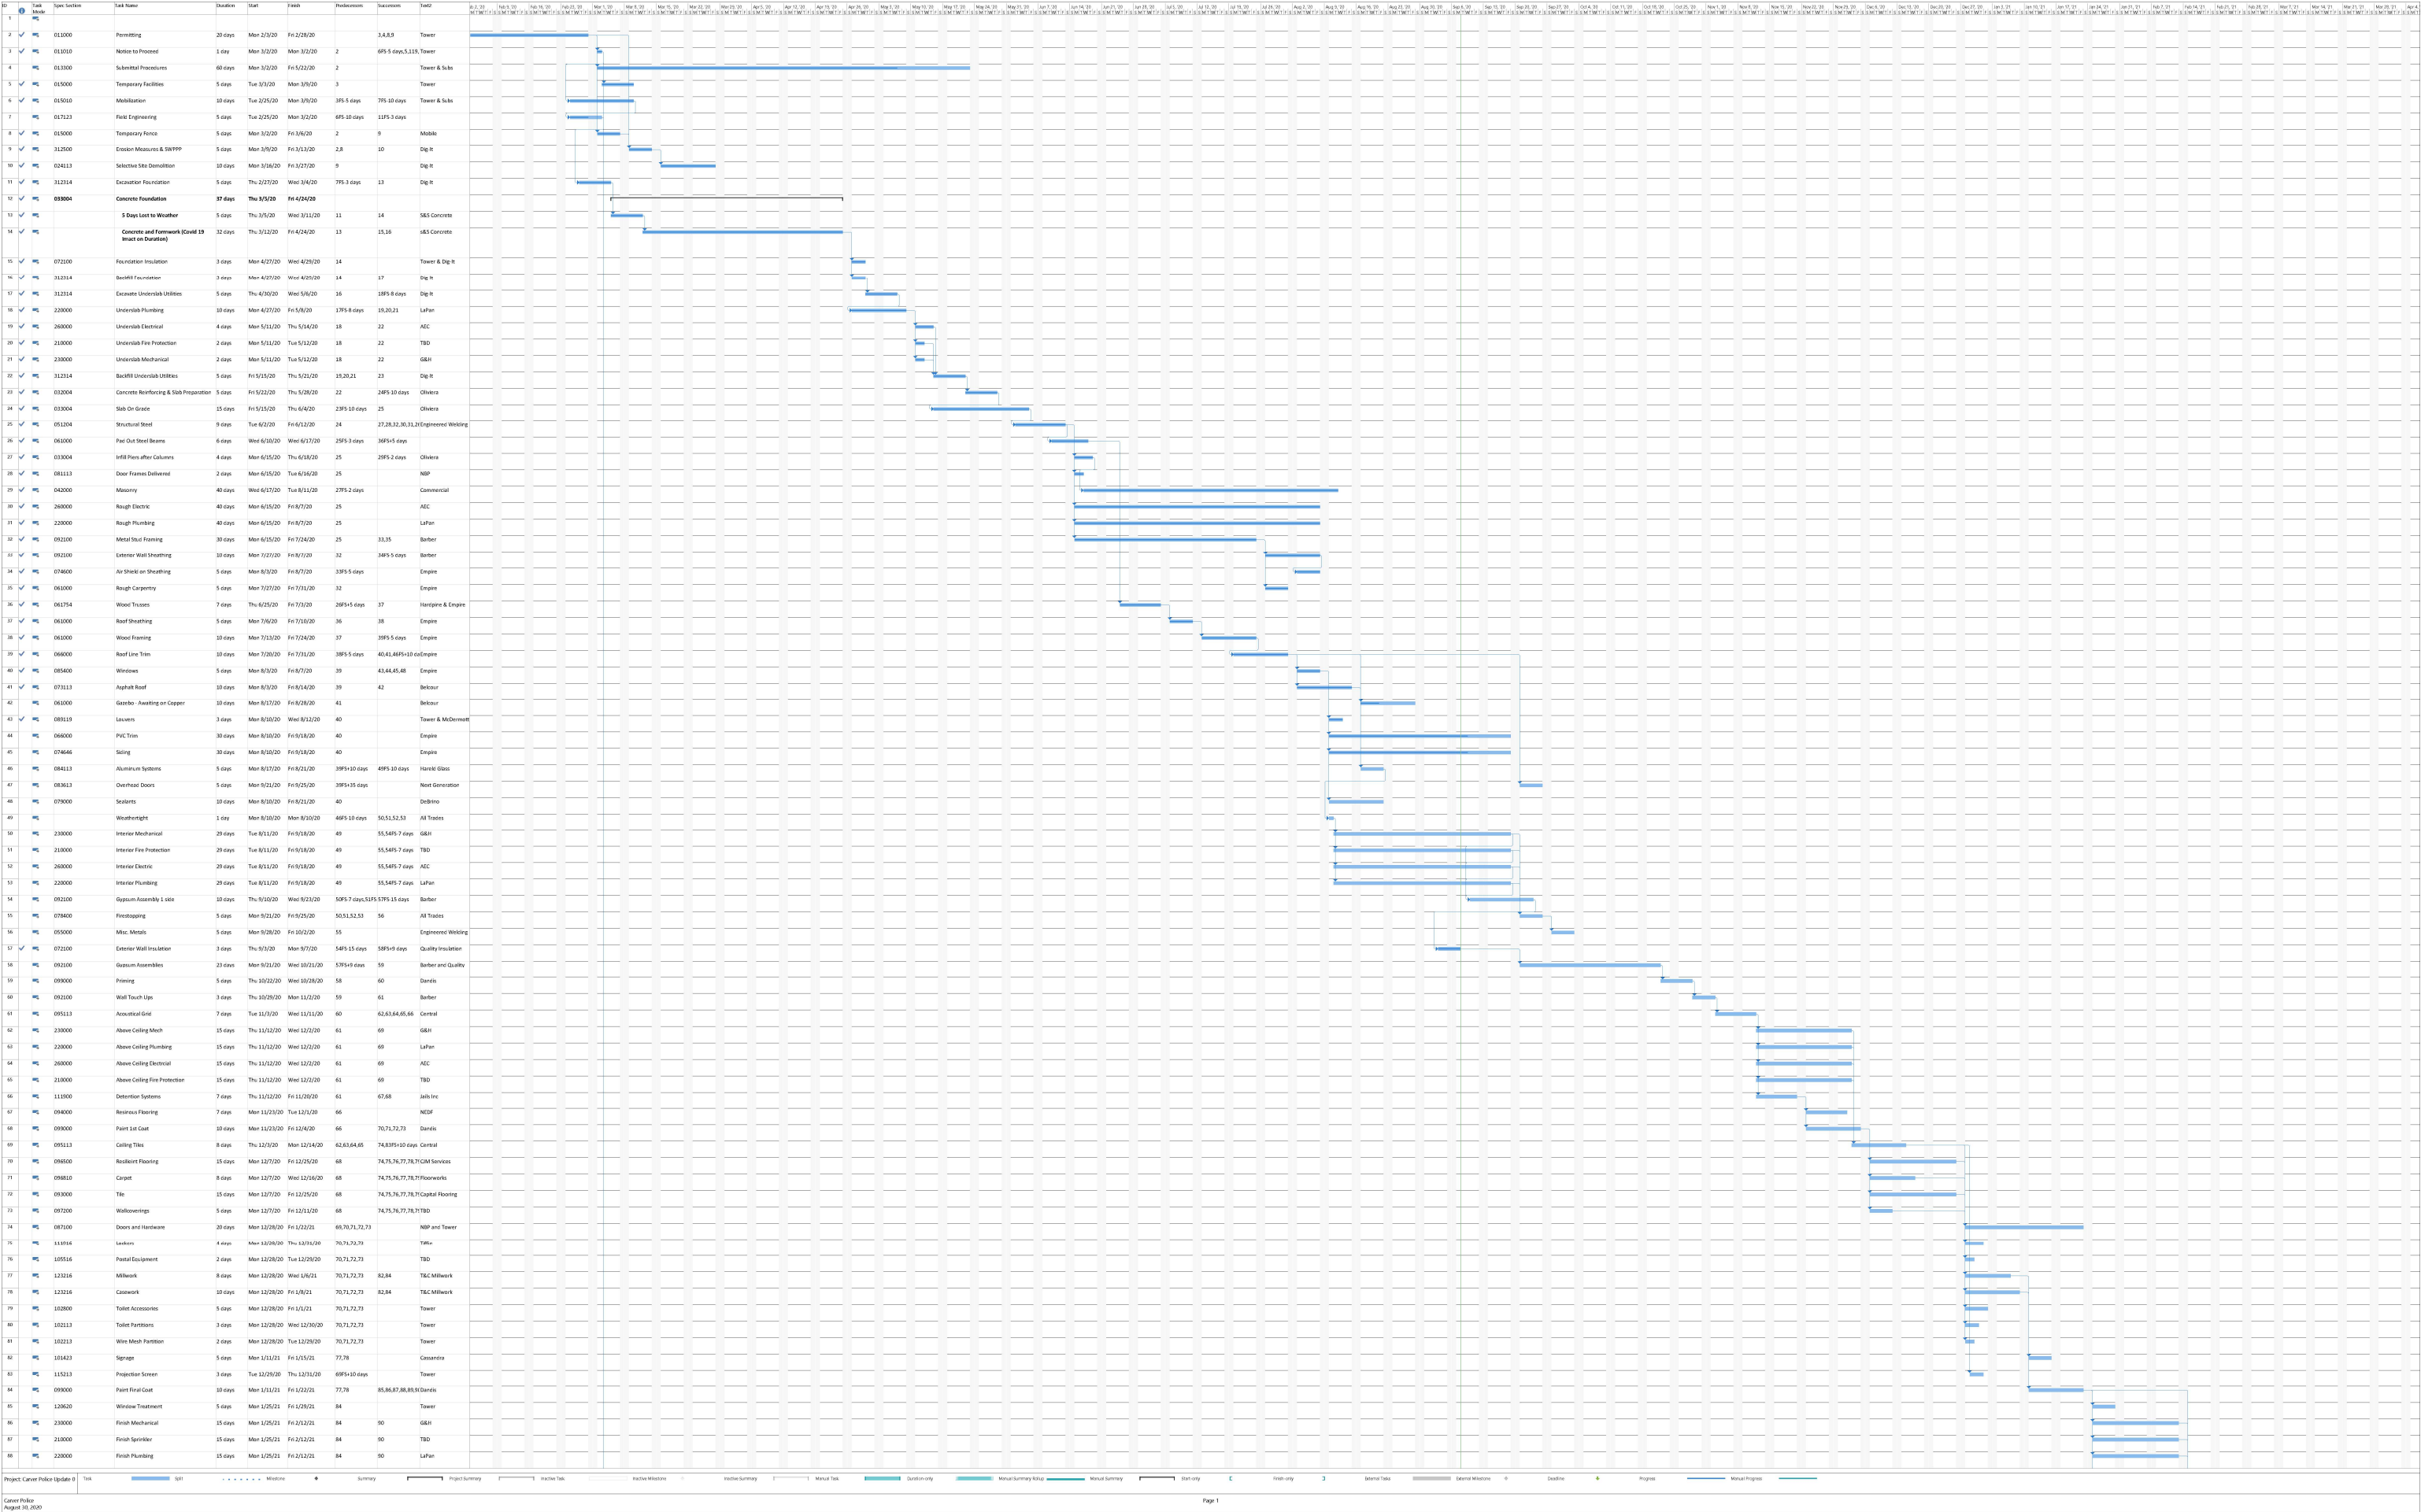

Tower Construction
Change Proposal Log

					Open Change Proposals			10.17.20
					Rejected Change Proposals			
					Approved Change Proposals			
CP#	CO#	Date	Description	CP Amount	Amount Approved	Amount Pending	Amount Not Approved	Subcontractor
1		03.12.20	Fire Protection File Sub Award	\$ 91,092.02			\$ 91,092.02	
1 Rev 1	1	03.16.20	Fire Protection File Sub Award	\$ 49,369.00	\$ 49,369.00			Delta Mechanical
2		04.07.20	ASI No. 001 - Fire Pump Modifications	\$ 284,304.41			\$ 284,304.41	
2 Rev 1	2	04.12.20	ASI No. 001 - Fire Pump Modifications	\$ 273,320.55	\$273,320.55			EWF
								Debito Caulking
								Barber Drywall
								Bode Material
								Delta Mechanical
								American
								LaPan
								Dig It
								Outback Engineering
3	2	03.12.20	ASI No. 002 BDA Review	\$ (31,268.05)	\$ (31,268.05)			Americal Electrical
4		03.12.20	ASI No. 003 - Main Circuit Breaker	\$ 3,067.04			\$ 3,067.04	Americal Electrical
4 Rev 1	2	04.07.20	ASI No. 003 - Main Circuit Breaker	\$ -	\$ -			American Electrical
5		04.07.20	Alternate No. 001 - Out Building Construction	\$ 344,000.00			\$ 344,000.00	All trades
5 Rev 1	3	04.12.20	Alternate No. 001 - Out Building Construction	\$ 344,000.00	\$344,000.00			All Trades
6		03.18.20	Septic System	\$ 44,269.79			\$ 44,269.79	Dig-It Construction
7		04.07.20	Unforeseen Old Foundation Removal	\$ 5,397.34			\$ 5,397.34	Dig-It Construction
7 Rev 1	2	04.12.20	Unforeseen Old Foundation Removal	\$ 5,285.68	\$ 5,285.68			Dig-It Construction
8		04.07.20	ASI No. 006 - Genset AP	\$ 451.61			\$ 451.61	American Electrical
8 Rev 1	2	04.12.20	ASI No. 006 - Genset AP	\$ 431.08	\$ 431.08			American Electrical
9		04.08.20	Unsuitable Materials	\$ 36,581.71			\$ 36,581.71	Dig-It Construction
9 Rev 1		04.12.20	Unsuitable Materials	\$ 36,254.87			\$ 36,254.87	Dig-It Construction
9 Rev 2	2	04.14.20	Unsuitable Materials	\$ 19,995.75	\$ 19,995.75			Dig-It Construction
10	4	04.22.20	ASI No. 008 DS-C Fixture	\$ 1,473.34	\$ 1,473.34			American Electrical
								LaPan
11		04.22.20	ASI No. 009 Security Revisions	\$ 1,510.74			\$ 1,510.74	American Electrical
11 Rev 1	4	05.13.20	ASI No. 009 Security Revisions	\$ -	\$ -			American Electrical
12	4	05.13.20	ASI No. 004 Mechanical Equipment Relocation	\$ -	\$ -			American Electrical
								G&H Mechanical
13	4	05.13.20	ASI No. 007 Locker Electrical	\$ 677.88	\$ 677.88			American
14	4	07.14.20	ASI No. 010 Wall Type Revision	\$ (964.92)	\$ (964.92)			Barber
15		05.13.20	ASI No. 011 Fire Alarm Revisions	\$ -			\$ -	American Electrical
16	4	05.13.20	ASI No. 012 Door Leaf Type DL-A	\$ -	\$ -			Hareld Glass
17		05.13.20	Delete UPS From Project Scope	\$ (30,207.60)			(\$30,207.60)	American Electrical
18		06.16.20	ASI No. 13 Fire Alarm Scope of Work Revisions	\$4,173.60			\$4,173.60	American Electrical
18 Rev 1	5	09.18.20	ASI # 13 R-1 Fire Alarm Revision	\$0.00	\$0.00			American Electrical
19		08.12.20	ASI # 17 Framing Revision	\$4,361.01			\$4,361.01	Barber Drywall
19 Rev 1	5	09.18.20	ASI # 17 Framing Revision Revised	\$2,931.11	\$2,931.11			Barber Drywall
20		07.30.20	ASI # 16 Library Curbing Replacemnet	\$18,312.71			\$ 18,312.71	Dig It
20 Rev 1		08.24.20	ASI # 16 Library Curbing Replacemnet	\$14,652.30			\$14,652.30	Dig It
20 Rev 2	5	09.18.20	ASI # 16 Library Curbing Replacemnet	\$11,161.35	\$11,161.35			Dig It
21	5	07.30.20	ASI # 15 Electrical Additions	\$2,975.19	\$2,975.19			Americal Electrical
21 Rev 1		09.18.20	ASI # 15 R-1 Electrical Revisions					
22	5	08.04.20	ASI # 21 CPT- 01 Attick Stock	\$2,076.15	\$2,076.15			Floor Works
23	5	08.12.20	ASI # 18 Cupola roofing	\$3,264.00	\$3,264.00			Belcour
24			ASI # 26 Rear Gate Electrical Infrastructure	\$ 8,264.32			\$ 8,264.32	Dig-It
								American Electrical
24 Rev 1		10.17.20	ASI # 26 Rear Gate Electrical Infrastructure	\$ 2,101.78		\$ 2,101.78		Dig-It
25	5	09.19.20	ASI # 14 Aluminum Storefront Colors	\$ -	\$ -			Hareld Glass
26	5	09.19.20	ASI # 19 Memorial Revision	\$ -	\$ -			
27		10.17.20	ASI # 20 E911 Power	\$ -		\$ -		American
28	5	09/19.20	ASI # 22 Column Enclosure Dimensional Adjustment	\$ -	\$ -			Barber Drywall
29		10.07.20	ASI # 23 Dispatch Casework	\$ -		\$ -		T&C Woodworking
30			ASI # 24 Fire Pump B02 Revision					American Electrical
								Delta Mechancial
								LaPan
								G&H
31	5	09.19.20	ASI # 25 Dispatch Flooring Colors	\$ -	\$ -			CJM Services
32		10.17.20	ASI # 27 TV Box Mounting Heights	\$ -		\$ -		American Electrical
33		10.07.20	ASI # 28 Owner Requested Data and Power	\$ 1,823.64		\$ 1,823.64		American Electrical
34		10.17.20	ASI # 29 Communication Rm 114 Coordination	\$ -		\$ -		American Electrical
								G&H
								Delta Mechancial
35		10.07.20	ASI # 30 Dispatch Area Revisions	\$ 508.72		\$ 508.72		American Electrical
36		10.17.20	ASI # 31 and ASI # 32 Paint Clarifications	\$ -		\$ -		Dandis
37			ASI # 33 Additional Lockers					Barber Drywall
								Tiffin Lockers
								American Electrical
								G&H
								Central Ceiling
38			ASI # 34 Condenser Relocation					American Electrical
								G&H
								Belcour Roofing
								Barber Drywall
								Dig-It
39		10.17.20	Cupola Lighting	\$ -		\$ -		American
40			Lighting Protection					American
			Totals		\$684,728.11	\$ 4,434.14		
					\$ 6,957,500.00			
	1		CP 1 R1	\$ 49,369.00	\$ 7,006,869.00			
	2		CP 2R1, 3, 4R1, 7R1, 8R1, 9R2	\$ 267,765.01	\$ 7,274,634.01			
	3		CP 5R1	\$ 344,000.00	\$ 7,618,634.01			
	4		CP 10, 11R1, 12, 13, 14, 16	\$ 1,186.30	\$ 7,619,820.31			
	5		CP 18R1, 19R1, 20R2, 21, 22, 23, 25, 26, 28, 31	\$22,407.80	\$ 7,642,228.11			

SHOP DRAWING LOG

PROJECT: New Facility for the Carver Police Department, 3 Center Street, Carver, Massachusetts								STATE PROJECT No.:			
G.C.: Tower Construction Corporation								JHA PROJECT No.: 1830			
TEAM: JH Architects (JHA); Garcia-Galuska-DeSousa (GGD); Linden Landscape Architects (LLA); Szewczak Associates (SA); Paul Hawley Associates (PHA); CAMA (CAMA); Building Engineering Resources (BER)								G.C. PROJECT No.: 2252			
JHA SHOP DRAWING NUMBER	G.C. SHOP DRAWING NUMBER	DESCRIPTION <div> <div></div> = Reviewed & Returned <div></div> = Under JHA Review <div></div> = Under Consultant Review <div></div> = Under Owner Review <div></div> = Awaiting G.C. Response </div>	DATE REC'D - From - G.C.	DATE SENT - To - Owner	DATE REC'D - From - Owner	DATE SENT - To - Consult	DATE REC'D - From - Consult	DATE RTN'D - To - G.C.	REVIEWER	ACTION / REMARK	COMMENTS
DIVISION 0 - OWNER SUBMISSIONS											
DIVISION 1 - GENERAL REQUIREMENTS											
010000-001-1	-	Underslab Coordination Drawings	04/01/20	-	-	04/01/20	04/15/20	04/15/20	BER	AN	
011000-001-1	011000-01s	Carver Site Access Plan	01/29/20	01/29/20	02/20/20	01/29/20	01/29/20	02/20/20	ToC/LLA	AN	
011000-002-1	011000-02	Carver Police Schedule	02/19/20	-	-	-	-	02/27/20	JHA	A	
011000-003-1	011000-03	Above Slab Coordination Drawings	05/06/20	-	-	05/06/20	05/28/20	05/28/20	BER	A	
017700-001-1	017700-01	Septic As-Built's Stamped	09/03/20	-	-	09/03/20	09/15/20	09/15/20	GGD	A	
DIVISION 2 - EXISTING CONDITIONS											
DIVISION 3 - CONCRETE											
032004-001-1	032004-01	Rebar Shop Drawing	01/15/20	-	-	01/15/20	-	-	SA/LLA	-	Incorporated into 032004-001-2
032004-001-2	032004-02	Rebar Shop Drawing	01/22/20	-	-	01/28/20	02/05/20	02/05/20	SA/LLA	AC/RR	
032004-001-2	032004-02	Rebar Shop Drawing	-	-	-	-	-	04/03/20	SA/LLA	AC	Updated marks dated 2020-04-03
032004-001-3	032004-01 Rev2	Rebar Shop Drawing	03/03/20	-	-	04/03/20	04/03/20	04/03/20	SA	R	Re-design voided via negotiations
033004-001-1	033004-02s	Concrete Slab on Grade	02/19/20	-	-	02/19/20	02/24/20	02/24/20	SA	AC	
033004-002-1	033004-4s	Footings + Foundation Walls	02/19/20	-	-	02/19/20	02/24/20	02/24/20	SA	AC	
033004-002-2	033004-4s Rev 1	Footings + Foundation Walls	03/06/20	-	-	03/06/20	-	-	SA	-	Received For Record Only
033004-002-3	033004-4s Rev 2	Footings + Foundation Walls	03/10/20	-	-	03/10/20	03/19/20	03/19/20	SA	AC	
033004-003-1	033004-06s	Expansion Joint	03/05/20	-	-	03/06/20	03/13/20	03/13/20	SA	A	
033004-004-1	033004-07s	Non-Shrink Grout	03/05/20	-	-	03/06/20	03/13/20	03/13/20	SA	A	
033004-005-1	033004-08s	Stego Wrap Vapor Barrier 15 Mil	03/05/20	-	-	03/06/20	03/13/20	03/13/20	SA	A	
033004-006-1	033004-09s	Concrete Slab on Grade Layout	05/06/20	-	-	05/06/20	05/14/20	05/14/20	SA/JHA	AC	

SHOP DRAWING LOG

PROJECT: New Facility for the Carver Police Department, 3 Center Street, Carver, Massachusetts								STATE PROJECT No.:			
G.C.: Tower Construction Corporation								JHA PROJECT No.: 1830			
TEAM: JH Architects (JHA); Garcia-Galuska-DeSousa (GGD); Linden Landscape Architects (LLA); Szewczak Associates (SA); Paul Hawley Associates (PHA); CAMA (CAMA); Building Engineering Resources (BER)								G.C. PROJECT No.: 2252			
JHA SHOP DRAWING NUMBER	G.C. SHOP DRAWING NUMBER	DESCRIPTION <div> <div></div> = Reviewed & Returned <div></div> = Under JHA Review <div></div> = Under Consultant Review <div></div> = Under Owner Review <div></div> = Awaiting G.C. Response </div>	DATE REC'D - From - G.C.	DATE SENT - To - Owner	DATE REC'D - From - Owner	DATE SENT - To - Consult	DATE REC'D - From - Consult	DATE RTN'D - To - G.C.	REVIEWER	ACTION / REMARK	COMMENTS
DIVISION 4 - MASONRY											
042000-001-1	042000-01s	Unit Masonry	01/22/20	-	-	01/22/20	01/29/20	02/05/20	JHA	A	
042000-002-1	042000-02s	Masonry Reinforcement Shop Drawings	01/22/20	-	-	01/22/20	01/29/20	01/30/20	SA/JHA	AC	
042000-003-1	042000-03s	Precast Concrete Products	02/14/20	-	-	-	-	02/14/20	JHA	AC	
042000-004-1	042000-04s	Precast Concrete Profile	02/18/20	-	-	-	-	02/19/20	JHA	AC	
042000-005-1	042000-05s	Precast Concrete Color Samples	03/04/20	-	-	-	-	03/16/20	JHA	AC	Samples Received 3/12/20
DIVISION 5 - METALS											
051204-001-1	051204-01	Anchor Bolts Setting Plan & Details	01/15/20	-	-	01/15/20	01/29/20	01/29/20	SA	AC	
051204-002-1	051204-02s	Structural Steel Drawings	02/13/20	-	-	02/13/20	02/27/20	02/27/20	SA	RR	
051204-002-2	051204-02 Rev 1	Structural Steel Drawings	03/21/20	-	-	03/21/20	04/02/20	04/02/20	SA	A/AC	
055133-001-1	051204-03s	Ships Ladder	05/27/20	-	-	-	-	06/10/20	JHA	AC	
DIVISION 6 - WOOD & PLASTICS											
061000-001-1	061000-01s	Lumber	03/26/20	-	-	03/31/20	04/03/20	04/03/20	SA/JHA	AC/RR	
061000-001-2	061000-01s Rev 1	Lumber	04/08/20	-	-	-	-	04/08/20	JHA	-	Not accepted for review
061000-002-1	061000-01s	LVLs	04/10/20	-	-	04/10/20	04/20/20	04/21/20	SA	AC	
061000-003-1	061000-02s	Air Infiltration Barrier and Tape	04/10/20	-	-	-	-	04/15/20	SA/JHA	A	
061000-004-1	061000-03s	Construction Subfloor Adhesive	04/10/20	-	-	04/10/20	-	04/21/20	JHA	AC	
061000-005-1	061000-04s	Exterior Sheathing	04/10/20	-	-	04/10/20	04/20/20	04/21/20	SA	AC	
061000-006-1	061000-05s	Hunter Panels	04/10/20	-	-	-	-	04/15/20	SA/JHA	A	
061000-007-1	061000-06s	Self-Adhered Flashing	04/10/20	-	-	-	-	04/15/20	SA/JHA	R	
061000-007-2	061000-06s Rev 1	Self-Adhered Flashing	04/21/20	-	-	-	-	04/21/20	JHA	A	
061000-008-1	061000-07s	TJI	04/10/20	-	-	04/10/20	04/20/20	04/21/20	SA	AC/R	
061000-009-1	06100-08s	Framing Lumber Materials	04/10/20	-	-	04/10/20	04/20/20	04/21/20	SA	AC	
061000-010-1	061000-09	Soffit Vent	07/28/20	-	-	-	-	07/28/20	JHA	AC	
061754-001-1	061754-01s	Truss Shop Drawing	01/27/20	-	-	01/28/20	02/11/20	02/11/20	SA	RR	
061754-001-2	061754-01s Rev 1	Trusses	03/10/20	-	-	03/10/20	03/24/20	03/24/20	SA	AC	
061754-001-3	061754-01s Rev 2	Truss Seals	05/18/20	-	-	05/18/20	05/28/20	05/28/20	SA	AC	
061754-002-1	061754-02s	Outbuilding Truss SD	04/29/20	-	-	04/29/20	05/08/20	05/12/20	SA	AC	

SHOP DRAWING LOG

PROJECT: New Facility for the Carver Police Department, 3 Center Street, Carver, Massachusetts								STATE PROJECT No.:			
G.C.: Tower Construction Corporation								JHA PROJECT No.: 1830			
TEAM: JH Architects (JHA); Garcia-Galuska-DeSousa (GGD); Linden Landscape Architects (LLA); Szewczak Associates (SA); Paul Hawley Associates (PHA); CAMA (CAMA); Building Engineering Resources (BER)								G.C. PROJECT No.: 2252			
JHA SHOP DRAWING NUMBER	G.C. SHOP DRAWING NUMBER	DESCRIPTION <div> <div></div> = Reviewed & Returned <div></div> = Under JHA Review <div></div> = Under Consultant Review <div></div> = Under Owner Review <div></div> = Awaiting G.C. Response </div>	DATE REC'D - From - G.C.	DATE SENT - To - Owner	DATE REC'D - From - Owner	DATE SENT - To - Consult	DATE REC'D - From - Consult	DATE RTN'D - To - G.C.	REVIEWER	ACTION / REMARK	COMMENTS
064000-001-1	06400-01s	Fiberglass Column	06/10/20	-	-	-	-	06/12/20	JHA	A	
064400-001-1	064400-01s	Moldings and Decorative Millwork	05/06/20	-	-	-	-	05/15/20	JHA	AC	
066000-001-1	06600-01s	PVC Trim	05/06/20	-	-	-	-	05/13/20	JHA	A	
DIVISION 7 - THERMAL & MOISTURE PROTECTION											
072100-001-1	033004-05s	Dow Insulation	03/05/20	-	-	-	-	03/15/20	JHA	A	
072100-002-1	033004-09s	Tuff II Coating	03/05/20	-	-	-	-	03/15/20	JHA	A	
072100-003-1	072100-01	Building Insulation	07/23/20	-	-	-	-	07/28/20	JHA	A/R	
073113-001-1	073113s	Asphalt Shingles	02/18/20	-	-	-	-	02/20/20	JHA	AC/RR/R	
073113-002-1	073113-25s	Color Samples & Color Chart	03/04/20	-	-	-	-	03/16/20	JHA	AC	Samples Received 3/12/20
073113-003-1	073113-26	Roof Hatch	07/23/20	-	-	-	-	07/24/20	JHA	A	
074600-001-1	074600-01s	NuCedar	04/10/20	-	-	-	-	04/16/20	JHA	AC/RR	
074600-002-1	074600-02	Siding Color Samples	05/07/20	05/20/20	05/20/20	-	-	05/27/20	JHA	AC	Samples Received 5/15/20
074646-001-1	074646-01s	Fiber Cement Siding	04/10/20	-	-	-	-	04/16/20	JHA	AC	
075323-001-1	075323-01s	Membrane Roofing	03/04/20	-	-	-	-	03/15/20	JHA	A/R	Only Flat Insulation Not Approved
075323-002-1	075323-02s	Metal Roofing	06/23/20	-	-	-	-	07/01/20	JHA	AC	
075323-003-1	075323-03s	Metal Roof Color Samples	07/07/20	-	-	-	-	08/07/20	JHA	R	
075323-004-1	075323-04	Substitution Request - Cupola Clips	10/07/20	-	-	-	-	10/07/20	JHA	AC	
079200-001-1	079200-01s	Elastomeric Joint Sealant	01/30/20	-	-	-	-	02/10/20	JHA	R	
079200-002-1	079200-02s	Sealant Color Chart	01/30/20	-	-	-	-	02/10/20	JHA	RR	
079200-003-1	079200-03s	Non-Sag Urethane Sealant	01/30/20	-	-	-	-	02/10/20	JHA	A	
079200-004-1	079200-04s	Acrylic-Emulsion Sealant and Color Chart	01/30/20	-	-	-	-	02/03/20	JHA	AC	
079200-005-1	079200-05s	Security Sealant	01/30/20	-	-	-	-	01/30/20	JHA	R	
079200-005-2	079200-05s Rev1	Security Sealant	02/07/20	-	-	-	-	02/07/20	JHA	A	
079200-006-1	079200-06s	Resilient Silicone Sealant	01/30/20	-	-	-	-	02/03/20	JHA	R	
DIVISION 8 - OPENINGS											
081113-001-1	081113-01	Door and Frame Schedule	04/13/20	-	-	-	-	04/16/20	JHA	AC	
081113-001-2	081113-03s Rev1	Door and Frame Schedule	05/01/20	-	-	-	-	-	JHA	-	Not Reviewed
081113-001-3	081113-03 Rev2	Steel Doors and Frames	08/03/20	-	-	-	-	08/05/20	JHA	R	
081113-002-1	081113-02	Door Frames	04/13/20	-	-	-	-	04/16/20	JHA	RR	

SHOP DRAWING LOG

PROJECT: New Facility for the Carver Police Department, 3 Center Street, Carver, Massachusetts								STATE PROJECT No.:			
G.C.: Tower Construction Corporation								JHA PROJECT No.: 1830			
TEAM: JH Architects (JHA); Garcia-Galuska-DeSousa (GGD); Linden Landscape Architects (LLA); Szewczak Associates (SA); Paul Hawley Associates (PHA); CAMA (CAMA); Building Engineering Resources (BER)								G.C. PROJECT No.: 2252			
JHA SHOP DRAWING NUMBER	G.C. SHOP DRAWING NUMBER	DESCRIPTION <div> <div></div> = Reviewed & Returned <div></div> = Under JHA Review <div></div> = Under Consultant Review <div></div> = Under Owner Review <div></div> = Awaiting G.C. Response </div>	DATE REC'D - From - G.C.	DATE SENT - To - Owner	DATE REC'D - From - Owner	DATE SENT - To - Consult	DATE REC'D - From - Consult	DATE RTN'D - To - G.C.	REVIEWER	ACTION / REMARK	COMMENTS
081113-002-2	081113-03s Rev1	Doors Frames	05/01/20	-	-	-	-	05/13/20	JHA	R	
081113-003-1	081113-03	Steel Doors	04/13/20	-	-	-	-	04/16/20	JHA	AC/RR/R	
081113-003-2	081113-03s Rev1	Steel Doors	05/01/20	-	-	-	-	05/13/20	JHA	A/R	
081400-001-1	081400-01	Wood Doors	04/13/20	-	-	-	-	04/16/20	JHA	AC	
083326-001-1	083616-03s	Shop Drawing and Product Data for Door 125C	04/10/20	-	-	-	-	04/16/20	JHA	AC	
083613-001-1	083613-01s	Shop Drawings for Doors 125B & 118B	03/06/20	-	-	-	-	03/16/20	JHA	AC	
083613-002-1	083616-02s	Product Data Overhead Doors 112B and 118B	04/10/20	-	-	-	-	04/16/20	JHA	AC	
083613-003-1	083616-04s	Motors	04/10/20	-	-	-	-	04/16/20	JHA	RR	
084113-001-1	088000-01s	Door & Frame Product Data	05/18/20	-	-	-	-	05/27/20	JHA	AC	
084113-002-1	084113-01s	Aluminum Entrances & Storefronts	05/28/20	-	-	-	-	06/12/20	JHA	AC/RR	
084113-003-1	084113-02s	Color Samples	06/04/20	-	-	-	-	06/15/20	JHA	AC	Cover sheet & Scan only
085400-001-1	085400-01s	Fiberglass Windows	03/06/20	-	-	-	-	03/15/20	JHA	AC	
085400-002-1	085400-01s	Fiberglass Windows Shop Drawings	04/01/20	-	-	-	-	04/02/20	JHA	AC	
087100-001-1	087100-01	Door Hardware Schedule	04/13/20	-	-	04/13/20	04/14/20	04/16/20	PHA/JHA	AN/RRfR	
087100-001-2	087100-01sRev1	Door Hardware Schedule	04/29/20	-	-	04/29/20	05/04/20	05/04/20	PHA/JHA	A	
087100-002-1	087100-02	Door Hardware	04/13/20	-	-	04/13/20	04/14/20	04/16/20	PHA/JHA	AN/RRfR	
087100-002-2	087100-02s	Door Hardware PD	04/29/20	-	-	04/29/20	05/04/20	05/04/20	PHA/JHA	A	
087100-003-1	088000-02s	Hardware PD	05/18/20	-	-	05/18/20	05/26/20	05/27/20	PHA	R	
087100-004-1	087100-01 Rev2	Aluminum Hardware Schedule	09/23/20	-	-	09/25/20	09/30/20	09/30/20	PHA	RR	
087100-004-2	087100-01 Rev3	Aluminum Hardware Schedule	10/05/20	-	-	10/05/20	10/07/20	10/07/20	PHA	AC	
087113-001-1	087113-01s	Automatic Doors	02/12/20	-	-	-	-	02/14/20	JHA	AC	
088000-001-1	088000-03s	Float Glass PD	05/18/20	-	-	-	-	05/27/20	JHA	AC	
088000-002-1	088000-04	Glass Sample	08/19/20	-	-	-	-	09/16/20	JHA	A	Glass Samples Rec'd 9/15
089119-001-1	089119-01s	Louver SD & Color Chart	02/24/20	-	-	-	-	02/27/20	JHA	AC	
089119-002-1	089119-02s	Louver Color Samples	04/21/20	-	-	-	-	05/27/20	JHA	R	Siding Samples Rec'd 5/15
089119-002-2	089119-02s Rev1	Louver Color Samples	06/03/20	-	-	-	-	06/15/20	JHA	AC	Cover sheet & Scan only
DIVISION 9 - FINISHES											
092100-001-1	092100-01s	Gypsum Board	03/30/20	-	-	-	-	03/31/20	JHA	AC/R	Only Impact Gypsum was Rejected
092100-002-1	092100-02s	National Gypsum	04/04/20	-	-	-	-	04/06/20	JHA	R	
092100-003-1	092100-03s	Cold-Formed Steel Exterior Framing	04/20/20	-	-	04/20/20	04/28/20	04/29/20	SA/JHA	RR	
092100-003-2	092100-03s rev1	Cold-Formed Steel Exterior Framing	06/05/20	-	-	06/05/20	06/09/20	06/10/20	SA/JHA	AC	
093000-001-1	093000-01s	Tile Products	06/22/20	-	-	06/22/20	07/02/20	07/02/20	CAMA	AC	

SHOP DRAWING LOG

PROJECT: New Facility for the Carver Police Department, 3 Center Street, Carver, Massachusetts								STATE PROJECT No.:			
G.C.: Tower Construction Corporation								JHA PROJECT No.: 1830			
TEAM: JH Architects (JHA); Garcia-Galuska-DeSousa (GGD); Linden Landscape Architects (LLA); Szewczak Associates (SA); Paul Hawley Associates (PHA); CAMA (CAMA); Building Engineering Resources (BER)								G.C. PROJECT No.: 2252			
JHA SHOP DRAWING NUMBER	G.C. SHOP DRAWING NUMBER	DESCRIPTION <div> = Reviewed & Returned = Under JHA Review = Under Consultant Review = Under Owner Review = Awaiting G.C. Response </div>	DATE REC'D	DATE SENT	DATE REC'D	DATE SENT	DATE REC'D	DATE RTN'D	REVIEWER	ACTION / REMARK	COMMENTS
			- From - G.C.	- To - Owner	- From - Owner	- To - Consult	- From - Consult	- To - G.C.			
093000-002-1	093000-02s	Grout & Sealant	06/22/20	-	-	06/22/20	07/02/20	07/02/20	CAMA	A	
093000-003-1	093000-03s	Setting Materials	06/22/20	-	-	06/22/20	07/02/20	07/02/20	CAMA	A	
093000-004-1	093000-04s	Stainless Steel Metal Trim	06/22/20	-	-	06/22/20	07/02/20	07/02/20	CAMA	A	
093000-005-1	093000-05s	CWT-04	06/22/20	-	-	06/22/20	07/02/20	07/02/20	CAMA	A	
093000-006-1	093000-06s	Tile Products	07/09/20	-	-	07/09/20	07/23/20	07/23/20	CAMA	AC	
093000-007-1	093000-07	Tile Shop Drawings	08/19/20	-	-	08/19/20	08/31/20	08/31/20	CAMA	A	
094000-001-1	094000-01s	Industrial Floor System	02/07/20	-	-	-	-	02/07/20	JHA	R	AC Only if Samples are Approved
094000-002-1	094000-02s	Industrial Floor Color Samples	03/04/20	-	-	-	-	03/30/20	JHA	A	Samples Received 3/12/20
095113-001-1	095113-01	Acoustical Ceiling Panels	01/02/20	-	-	-	-	01/07/20	JHA	AC	
	095113-02										
	095113-03										
	095113-04										
	095113-05										
095113-002-1	095113-06	Acoustical Ceiling Samples	01/13/20	-	-	-	-	03/15/20	JHA	A/R	Samples Received 3/12/20
096500-001-1	096500-01s	Solid Vinyl Tile (SVT-01)(SVT-02)(SVT-03)	01/30/20	-	-	01/30/20	02/06/20	02/07/20	CAMA	A	
096500-002-1	096500-02s	Luxury Vinyl Tile (LVT-01)	01/30/20	-	-	01/30/20	02/06/20	02/07/20	CAMA	AC	
096500-003-1	096500-03s	Rubber Anti-Static Tile (ESD-01)(ESD-02)(ESD-03)	01/30/20	-	-	01/30/20	02/06/20	02/07/20	CAMA	AC	
096500-004-1	096500-04s	Resilient Base	01/30/20	-	-	01/30/20	02/06/20	02/07/20	CAMA	AC	
096500-005-1	096500-05s	Samples	01/30/20	-	-	01/30/20	02/06/20	02/07/20	CAMA	AC	
096810-001-1	096810-01	Carpet Tile	07/30/20	-	-	07/30/20	07/30/20	07/30/20	CAMA	A	
097200-001-1	097200-01s	RWC-01 Impact Wall Resistant Solution	07/01/20	-	-	07/01/20	07/13/20	07/13/20	CAMA	A	
097200-002-1	097200-02s	VWC-01 Denovo Ledge 04	07/01/20	-	-	07/01/20	07/13/20	07/13/20	CAMA	A	
097200-003-1	097200-03s	VWC-02 Denovo Milestone 05	07/01/20	-	-	07/01/20	07/13/20	07/13/20	CAMA	A	
097200-004-1	097200-04s	Samples	07/01/20	-	-	07/01/20	07/13/20	07/13/20	CAMA	A	
099000-001-1	099000-01	Painting Product Data	01/15/20	-	-	01/15/20	01/29/20	01/29/20	CAMA	RR	
099000-001-2	099000-01 R1	Painting Product Data	01/31/20	-	-	01/31/20	02/06/20	02/07/20	CAMA	AC	
099000-002-1	099000-02	Interior Finish - Fire Rated Plywood	08/25/20	-	-	08/25/20	09/08/20	09/09/20	CAMA	A	
099000-003-1	099000-03	Paint Color Samples	09/14/20	-	-	09/14/20	09/28/20	09/29/20	CAMA	AC	
099000-004-1	099000-04	Epoxy Water Emulsion Primer Sealer	10/07/20	-	-	10/07/20			CAMA		
DIVISION 10 - SPECIALTIES											
101100-001-1	101100-01	Visual Displays	07/08/20	-	-	07/09/20	07/17/20	07/22/20	JHA/CAMA	AC	
102113-001-1	102113-01	Toilet Compartments	07/15/20	-	-	07/15/20	07/17/20	07/21/20	JHA/CAMA	AC	

SHOP DRAWING LOG

PROJECT: New Facility for the Carver Police Department, 3 Center Street, Carver, Massachusetts								STATE PROJECT No.:			
G.C.: Tower Construction Corporation								JHA PROJECT No.: 1830			
TEAM: JH Architects (JHA); Garcia-Galuska-DeSousa (GGD); Linden Landscape Architects (LLA); Szewczak Associates (SA); Paul Hawley Associates (PHA); CAMA (CAMA); Building Engineering Resources (BER)								G.C. PROJECT No.: 2252			
JHA SHOP DRAWING NUMBER	G.C. SHOP DRAWING NUMBER	DESCRIPTION <div> <div></div> = Reviewed & Returned <div></div> = Under JHA Review <div></div> = Under Consultant Review <div></div> = Under Owner Review <div></div> = Awaiting G.C. Response </div>	DATE REC'D - From - G.C.	DATE SENT - To - Owner	DATE REC'D - From - Owner	DATE SENT - To - Consult	DATE REC'D - From - Consult	DATE RTN'D - To - G.C.	REVIEWER	ACTION / REMARK	COMMENTS
102213-001-1	102213-01s	Wire Mesh Partitions	03/13/20	-	-	03/15/20	-	03/15/20	JHA	RR	
102800-001-1	102800-01s	Toilet and Bath Accessories	05/20/20	-	-	-	-	05/27/20	JHA	AC/R	
102800-001-2	102800-01Rev1	Paper Towel Dispenser & Waste Receptacle	09/03/20	-	-	-	-	09/03/20	JHA	A	
104416-001-1	104416-01s	Fire Extinguishers	05/20/20	-	-	-	-	05/27/20	JHA	A	
105113-001-1	105113-01s	Metal Locker SD	03/13/20	03/16/20	03/25/20	03/15/20	03/20/20	03/31/20	JHA	AC	
105500-001-1	105500-01s	High Security Key Box	04/22/20	-	-	-	-	04/23/20	JHA	AC	
105516-001-1	105516-01	Postal Specialties	07/15/20	-	-	-	-	07/15/20	JHA	AC	
107516-001-1	107516-01s	Flag Poles	05/28/20	-	-	-	-	06/10/20	JHA	A	
DIVISION 11 - EQUIPMENT											
115000-001-1	115000-01s	Canopy Hood	04/27/20	-	-	-	-	04/27/20	JHA	AC	
115000-002-1	115000-01s	Canopy Hood	04/28/20	-	-	-	-	04/28/20	JHA	AC	
115213-001-1	115213-01	Projection Screen	07/08/20	-	-	-	-	07/09/20	JHA	A	
111900-001-1	111900-01s	Detention Equipment	04/01/20	-	-	-	-	04/02/20	JHA	AC	
DIVISION 12 - FURNISHINGS											
120620-001-1	120620-01	Window Treatments	08/26/20	-	-	08/26/20	09/08/20	09/09/20	JHA/CAMA	AC	
123216-001-1	123216-01s	Casework Shop Drawings	03/24/20	-	-	-	-	04/02/20	JHA	RR	
123216-001-2	123216-01 Rev1	Casework Shop Drawings	08/18/20	-	-	-	-	08/26/20	JHA	AC/RR	RR on Dispatch #107 Only
129313-001-1	129313-01s	Bike Rack	04/28/20	-	-	04/28/20	04/29/20	04/29/20	LLA	A	
DIVISION 13 - SPECIAL CONSTRUCTION											
134700-001-1	134700-01 134700-02 134700-03	Bullet Resistant Protection	02/24/20	-	-	-	-	02/27/20	JHA	AC	

SHOP DRAWING LOG

PROJECT: New Facility for the Carver Police Department, 3 Center Street, Carver, Massachusetts								STATE PROJECT No.:			
G.C.: Tower Construction Corporation								JHA PROJECT No.: 1830			
TEAM: JH Architects (JHA); Garcia-Galuska-DeSousa (GGD); Linden Landscape Architects (LLA); Szewczak Associates (SA); Paul Hawley Associates (PHA); CAMA (CAMA); Building Engineering Resources (BER)								G.C. PROJECT No.: 2252			
JHA SHOP DRAWING NUMBER	G.C. SHOP DRAWING NUMBER	DESCRIPTION <div> <div></div> = Reviewed & Returned <div></div> = Under JHA Review <div></div> = Under Consultant Review <div></div> = Under Owner Review <div></div> = Awaiting G.C. Response </div>	DATE REC'D - From - G.C.	DATE SENT - To - Owner	DATE REC'D - From - Owner	DATE SENT - To - Consult	DATE REC'D - From - Consult	DATE RTN'D - To - G.C.	REVIEWER	ACTION / REMARK	COMMENTS
DIVISION 14 - CONVEYING EQUIPMENT											
DIVISION 21 - FIRE SUPPRESSION											
210000-001-1	210000-01S	Fire Protection	01/17/20	-	-	01/17/20	-	-	BER	-	VOIDED BY GTC on 4/8/20
210000-002-1	210000-01s	Underground Fire Service	04/29/20	-	-	04/29/20	05/08/20	05/11/20	BER	A	
210000-003-1	210000-02s	Wet Sprinkler Piping	04/29/20	-	-	04/29/20	05/08/20	05/11/20	BER	A	
210000-004-1	210000-03s	Dry Pipe Sprinkler	04/29/20	-	-	04/29/20	05/08/20	05/11/20	BER	A	
210000-005-1	210000-04s	Valves	04/29/20	-	-	04/29/20	-	-	-	-	SUPERSEDED by FPC ON 5/6/20
210000-005-2	210000-04 Rev1s	Valves	05/06/20	-	-	05/07/20	05/13/20	05/13/20	BER	A	
210000-006-1	210000-05s	Hangers and Supports	04/29/20	-	-	04/29/20	05/13/20	05/13/20	BER	A	
210000-007-1	210000-06s	FDC	04/29/20	-	-	04/29/20	05/13/20	05/13/20	BER	A	
210000-008-1	210000-07s	Sprinkler Heads	04/29/20	-	-	04/29/20	05/13/20	05/13/20	BER	A	
210000-009-1	210000-08s	Sprinkler Cabinet	04/29/20	-	-	04/29/20	05/13/20	05/13/20	BER	A	
210000-010-1	210000-09s	Signaling Devices	04/29/20	-	-	04/29/20	-	-	-	-	SUPERSEDED by FPC ON 5/6/20
210000-010-2	210000-09 Rev1s	Signaling Devices	05/06/20	-	-	05/07/20	05/27/20	05/27/20	BER	A	
210000-011-1	210000-10s	Water Pressure Gauges	04/29/20	-	-	04/29/20	-	-	-	-	SUPERSEDED by FPC ON 5/6/20
210000-011-2	210000-10 Rev1s	Water Pressure Gauges	05/06/20	-	-	05/07/20	05/27/20	05/27/20	BER	A	
210000-012-1	210000-11s	Sleeves and Penetrations	04/29/20	-	-	04/29/20	05/13/20	05/13/20	BER	A	
210000-013-1	210000-12s	Fire Hydrants	04/29/20	05/13/20	05/14/20	04/29/20	05/13/20	05/14/20	BER	AC	
210000-014-1	210000-13s	Hydraulic Calcs & Drawings	05/06/20	-	-	05/07/20	05/27/20	05/27/20	BER	RR	
210000-014-2	210000-13 Rev1	Hydraulic Calcs & Drawings	07/20/20	-	-	07/21/20	08/03/20	08/03/20	BER	A	
210000-015-1	210000-14s	FP Drawings	05/06/20	-	-	05/07/20	-	-	BER	RR	Engineer Comments in 210000-014-1
210000-016-1	210000-15s	Fire Pump	05/06/20	-	-	05/07/20	05/27/20	05/27/20	BER	AC	
210000-017-1	210000-16s	Underground Water Storage Tank	05/13/20	-	-	05/13/20	05/27/20	05/27/20	BER	AC	
210000-018-1	210000-17s	Sprinkler Coordination Drawings	06/08/20	-	-	06/08/20	06/22/20	06/22/20	BER	A	

SHOP DRAWING LOG

PROJECT: New Facility for the Carver Police Department, 3 Center Street, Carver, Massachusetts								STATE PROJECT No.:			
G.C.: Tower Construction Corporation								JHA PROJECT No.: 1830			
TEAM: JH Architects (JHA); Garcia-Galuska-DeSousa (GGD); Linden Landscape Architects (LLA); Szewczak Associates (SA); Paul Hawley Associates (PHA); CAMA (CAMA); Building Engineering Resources (BER)								G.C. PROJECT No.: 2252			
JHA SHOP DRAWING NUMBER	G.C. SHOP DRAWING NUMBER	DESCRIPTION <div> <div></div> = Reviewed & Returned <div></div> = Under JHA Review <div></div> = Under Consultant Review <div></div> = Under Owner Review <div></div> = Awaiting G.C. Response </div>	DATE REC'D - From - G.C.	DATE SENT - To - Owner	DATE REC'D - From - Owner	DATE SENT - To - Consult	DATE REC'D - From - Consult	DATE RTN'D - To - G.C.	REVIEWER	ACTION / REMARK	COMMENTS
DIVISION 22 - PLUMBING											
220000-001-1	220000-01s	Tight Tank	02/17/20	-	-	02/17/20	03/02/20	03/02/20	BER	AC	
220000-002-1	220000-02s	Water Heaters	02/17/20	-	-	02/17/20	03/02/20	03/02/20	BER	A	
220000-003-1	220000-03s	Pumps	02/17/20	-	-	02/17/20	03/02/20	03/02/20	BER	A	
220000-004-1	220000-04s	Pipe I.D.	02/17/20	-	-	02/17/20	03/02/20	03/02/20	BER	A	
220000-005-1	220000-05s	Water Meter	02/17/20	-	-	02/17/20	03/02/20	03/02/20	BER	A	
220000-006-1	220000-06s	Cross Connection Points	02/17/20	-	-	02/17/20	03/02/20	03/02/20	BER	A	
220000-007-1	220000-07s	Pipe Supports	02/21/20	-	-	02/24/20	03/02/20	03/02/20	BER	A	
220000-008-1	220000-08s	Sleeves, Iners, Fire Stopping & Escutcheons	02/21/20	-	-	02/24/20	03/02/20	03/02/20	BER	A	
220000-009-1	220000-09s	Pipe Materials	02/21/20	-	-	02/24/20	03/02/20	03/02/20	BER	A	
220000-010-1	220000-10s	Copper Pipe	02/21/20	-	-	02/24/20	03/02/20	03/02/20	BER	A	
220000-011-1	220000-11s	Sanitary Waste & Vent	02/21/20	-	-	02/24/20	03/02/20	03/02/20	BER	A	
220000-012-1	220000-12s	Press & Temp Control Devices	02/21/20	-	-	02/24/20	03/02/20	03/02/20	BER	A	
220000-013-1	220000-13s	Insulation	02/21/20	-	-	02/24/20	03/02/20	03/02/20	BER	A	
220000-014-1	220000-14s	Traps & Strainers	02/21/20	-	-	02/24/20	03/02/20	03/02/20	BER	AC	
220000-015-1	220000-15s	Thermometers & Pressure Gauges	02/21/20	-	-	02/24/20	03/02/20	03/02/20	BER	A	
220000-016-1	220000-16s	Wall Hydrants & Hose Bibbs	02/21/20	-	-	02/24/20	03/02/20	03/02/20	BER	A	
220000-017-1	220000-17s	Water Hammer Arrestors	02/21/20	-	-	02/24/20	03/02/20	03/02/20	BER	A	
220000-018-1	220000-18s	Drains	03/10/20	-	-	03/10/20	03/24/20	03/24/20	BER	A	
220000-019-1	220000-19s	Plumbing Fixtures - Water Closets	03/10/20	-	-	03/10/20	03/24/20	03/24/20	BER/JHA	AC	
220000-020-1	220000-20s	Plumbing Fixtures - Urinals	03/10/20	-	-	03/10/20	03/24/20	03/24/20	BER/JHA	AC	
220000-021-1	220000-21s	Plumbing Fixtures - Sinks & Faucets	03/10/20	-	-	03/10/20	03/24/20	03/24/20	BER/JHA	AC	
220000-022-1	220000-22s	Plumbing Fixtures - Shower	03/10/20	-	-	03/10/20	03/24/20	03/24/20	BER/JHA	AC	
220000-023-1	220000-23s	Plumbing Fixtures - Lavatories	03/10/20	-	-	03/10/20	03/24/20	03/24/20	BER/JHA	A	
220000-024-1	220000-24s	Plumbing Fixtures - Ice Maker Box	03/10/20	-	-	03/10/20	03/24/20	03/24/20	BER/JHA	A	
220000-025-1	220000-25s	Plumbing Fixtures - Laundry Washing Machine Box	03/10/20	-	-	03/10/20	03/24/20	03/24/20	BER/JHA	A	
220000-026-1	220000-26s	Exterior Wall Hydrant	03/10/20	-	-	03/10/20	03/24/20	03/24/20	BER/JHA	AC	
220000-027-1	220000-27s	Plumbing Fixtures - Emergency Eye Wash & Shower	03/10/20	-	-	03/10/20	03/24/20	03/24/20	BER/JHA	A	
220000-028-1	220000-28s	Plumbing Fixtures - Detention Grade Shower System	03/10/20	-	-	03/10/20	03/24/20	03/24/20	BER/JHA	AC	
220000-029-1	220000-29s	Plumbing Fixtures - Drinking Fountain	03/10/20	-	-	03/10/20	03/24/20	03/24/20	BER/JHA	A	

SHOP DRAWING LOG

PROJECT: New Facility for the Carver Police Department, 3 Center Street, Carver, Massachusetts								STATE PROJECT No.:			
G.C.: Tower Construction Corporation								JHA PROJECT No.: 1830			
TEAM: JH Architects (JHA); Garcia-Galuska-DeSousa (GGD); Linden Landscape Architects (LLA); Szewczak Associates (SA); Paul Hawley Associates (PHA); CAMA (CAMA); Building Engineering Resources (BER)								G.C. PROJECT No.: 2252			
JHA SHOP DRAWING NUMBER	G.C. SHOP DRAWING NUMBER	<div>DESCRIPTION</div> <div> <div></div> = Reviewed & Returned <div></div> = Under JHA Review <div></div> = Under Consultant Review <div></div> = Under Owner Review <div></div> = Awaiting G.C. Response </div>	DATE REC'D	DATE SENT	DATE REC'D	DATE SENT	DATE REC'D	DATE RTN'D	REVIEWER	ACTION / REMARK	COMMENTS
			- From - G.C.	- To - Owner	- From - Owner	- To - Consult	- From - Consult	- To - G.C.			
220000-030-1	220000-30s	Plumbing Fixtures - Combination Lav-Toilets	03/10/20	-	-	03/10/20	03/24/20	03/24/20	BER/JHA	RR	
220000-030-2	220000-30s Rev1	Plumbing Fixtures - Combination Lav-Toilets	07/02/20	-	-	07/02/20	07/17/20	07/21/20	BER/JHA	AC	
220000-030-3	220000-34	DS-C Fixture	07/27/20	-	-	07/27/20	08/03/20	08/03/20	BER	A	
220000-031-1	220000-31s	Thermostatic Mixing Valves	03/10/20	-	-	03/10/20	03/24/20	03/24/20	BER	A	
220000-032-1	220000-32s	Plumbing Fixtures - Detention Grade Shower Valve	03/10/20	-	-	03/10/20	03/24/20	03/24/20	BER/JHA	R	
220000-033-1	220000-33s	Plumbing Fixtures - Boot Wash Hose Bib	03/10/20	-	-	03/10/20	03/24/20	03/24/20	BER/JHA	AC	
DIVISION 23 - HVAC											
230000-001-1	230000-01s	Ductwork & Air Distribution Equipment	03/12/20	-	-	03/12/20	03/25/20	03/25/20	BER	A	
230000-002-1	230000-02s	Centrifugal Fans	03/12/20	-	-	03/12/20	03/25/20	03/25/20	BER	A	
230000-003-1	230000-03s	RGDs	03/12/20	-	-	03/12/20	03/25/20	03/25/20	BER/JHA	A/AC	
230000-004-1	230000-04s	ERV & VRF	03/12/20	-	-	03/12/20	03/25/20	03/25/20	BER	AC	
230000-005-1	230000-05s	Duct & Pipe Insulation	03/17/20	-	-	03/18/20	03/25/20	03/25/20	BER	A	
230000-006-1	230000-06s	Electrical Heaters	03/18/20	-	-	03/18/20	03/25/20	03/25/20	BER	AC	
230000-007-1	230000-07s	Motorized Dampers	03/18/20	-	-	03/18/20	03/25/20	03/25/20	BER	A	
230000-008-1	230000-08s	Outbuilding HVAC Equipment	04/29/20	-	-	04/29/20	05/13/20	05/13/20	BER	A	
DIVISION 26 - ELECTRICAL											
260000-001-1	260000-01s	Fire Alarm System	02/12/20	-	-	02/12/20	02/14/20	02/14/20	BER	A/AC/RR	
260000-001-2	260000-01s Rev 1	Fire Alarm System	03/17/20	-	-	03/18/20	03/19/20	03/19/20	BER	A/AC/RR	
260000-001-3	260000-01s Rev 2	Fire Alarm System	05/15/20	-	-	05/15/20	05/18/20	-	BER	-	VOIDED by 260000-001-4
260000-001-4	260000-01s Rev 3	Fire Alarm System	05/20/20	-	-	05/26/20	05/27/20	05/27/20	BER	A/AC	
260000-002-1	260000-02s	Engine Generator System	02/12/20	-	-	02/12/20	02/14/20	02/14/20	BER	AC/RR	
260000-002-2	260000-02s Rev 1	Engine Generator System	03/12/20	-	-	03/12/20	03/16/20	03/16/20	BER	AC/RR	
260000-002-3	260000-02s Rev 2	Engine Generator System	03/19/20	-	-	03/19/20	03/19/20	03/19/20	BER	AC	
260000-003-1	260000-03s	Lightning Protection	02/12/20	-	-	02/12/20	02/14/20	02/14/20	BER	A/AC/RR	
260000-003-2	260000-03s Rev1	Lightning Protection	02/20/20	-	-	02/20/20	02/20/20	02/24/20	BER/JHA	A/AC	
260000-004-1	260000-04s	Storm Switch (ATS)	02/20/20	-	-	02/20/20	02/21/20	02/24/20	BER	AC	

SHOP DRAWING LOG

PROJECT: New Facility for the Carver Police Department, 3 Center Street, Carver, Massachusetts								STATE PROJECT No.:			
G.C.: Tower Construction Corporation								JHA PROJECT No.: 1830			
TEAM: JH Architects (JHA); Garcia-Galuska-DeSousa (GGD); Linden Landscape Architects (LLA); Szewczak Associates (SA); Paul Hawley Associates (PHA); CAMA (CAMA); Building Engineering Resources (BER)								G.C. PROJECT No.: 2252			
JHA SHOP DRAWING NUMBER	G.C. SHOP DRAWING NUMBER	DESCRIPTION <div> <div></div> = Reviewed & Returned <div></div> = Under JHA Review <div></div> = Under Consultant Review <div></div> = Under Owner Review <div></div> = Awaiting G.C. Response </div>	DATE REC'D	DATE SENT	DATE REC'D	DATE SENT	DATE REC'D	DATE RTN'D	REVIEWER	ACTION / REMARK	COMMENTS
			- From - G.C.	- To - Owner	- From - Owner	- To - Consult	- From - Consult	- To - G.C.			
260000-005-1	260000-05s	Encl for Indiv Mntd Overcurrent & Switching Dev	03/17/20	-	-	03/18/20	03/19/20	03/19/20	BER	A/AC	
260000-006-1	260000-06s	Panelboards	03/17/20	-	-	03/18/20	03/19/20	03/19/20	BER	A/AC	
260000-007-1	260000-07s	Cartridge Fuses	03/17/20	-	-	03/18/20	03/19/20	03/19/20	BER	AC	
260000-008-1	260000-08s	Branch Panel SPD Protection	03/17/20	-	-	03/18/20	03/19/20	03/19/20	BER	A	
260000-009-1	260000-09s	Lighting Fixture	03/18/20	-	-	03/18/20	03/20/20	03/20/20	BER/JHA	A/AC	
260000-009-02	260000-09s Rev 1	Lighting Fixture	04/13/20	-	-	04/13/20	04/14/20	04/14/20	BER/JHA	A/AC	
260000-010-1	260000-10s	Lighting Control	03/18/20	-	-	03/18/20	03/20/20	03/20/20	BER/JHA	A/AC/R	
260000-011-1	260000-11s	Raceways & Fittings	03/18/20	-	-	03/18/20	03/19/20	03/19/20	BER	A	
260000-012-1	260000-12s	Cable Tray	03/18/20	-	-	03/18/20	03/19/20	03/19/20	BER	A/R	
260000-013-1	260000-13s	Uninterruptible Power System	03/24/20	-	-	03/24/20	03/25/20	03/25/20	BER	R	
260000-013-2	260000-13 Rev 1	Uninterruptible Power System	03/30/20	-	-	03/30/20	03/31/20	03/31/20	BER	AC	
260000-014-1	260000-14s	Grounding System	03/26/20	-	-	03/29/20	03/30/20	03/30/20	BER	A	
260000-015-1	260000-15s	Phasing & Color Coding	03/26/20	-	-	03/29/20	03/30/20	03/30/20	BER	A	
260000-016-1	260000-16s	Wiring Materials	03/26/20	-	-	03/29/20	03/30/20	03/30/20	BER	A/AC	
260000-017-1	260000-17s	Wiring Devices	03/26/20	-	-	03/29/20	03/30/20	03/30/20	BER	A/AC	
260000-018-1	260000-18s	Access Panels	03/26/20	-	-	03/29/20	03/30/20	03/30/20	BER	AC	
260000-019-1	260000-19s	Outlet, Junction, Pull Boxes	03/26/20	-	-	03/29/20	03/30/20	03/30/20	BER	A/AC	
260000-020-1	260000-20s	Trough	03/26/20	-	-	03/29/20	03/30/20	03/30/20	BER	A	
260000-021-1	260000-21s	Floor Boxes	03/26/20	-	-	03/29/20	03/30/20	03/30/20	BER	AC	
260000-022-1	260000-22s	Motor Control	03/30/20	-	-	03/30/20	03/31/20	03/31/20	BER	AC	
260000-023-1	260000-23s	Integrated Technology Infrastructure Support	03/30/20	-	-	03/30/20	03/31/20	03/31/20	BER	AC	
260000-024-1	260000-24s	Equipment Racks	04/01/20	-	-	04/01/20	04/02/20	04/02/20	BER	AC	
260000-025-1	260000-25s	Surge Protected Power Strip	04/01/20	-	-	04/01/20	04/02/20	04/02/20	BER	A	
260000-026-1	260000-26s	Cable Supports	04/01/20	-	-	04/01/20	04/02/20	04/02/20	BER	A	
260000-027-1	260000-27s	Bonding & Grounding Jumper Cable	04/01/20	-	-	04/01/20	04/02/20	04/02/20	BER	A	
260000-028-1	260000-28s	Unshielded Twisted Pair Cable	04/01/20	-	-	04/01/20	04/02/20	04/02/20	BER	AC	
260000-029-1	260000-29s	Broadband RF Cabling System	04/01/20	-	-	04/01/20	04/02/20	04/02/20	BER	AC	
260000-030-1	260000-30s	Underground Enclosures	04/01/20	-	-	04/01/20	04/02/20	04/02/20	BER	AC	
260000-031-1	260000-31s	Lighting Factory Drawings	04/30/20	-	-	04/30/20	05/01/20	05/01/20	BER	AC	
260000-032-1	260000-32s	Lighting - Factory Drawings Vode	05/13/20	-	-	05/13/20	05/14/20	05/14/20	BER	AC	
260000-033-1	260000-33	Power System Studies	08/03/20	-	-	08/03/20	08/06/20	08/07/20	BER	AC	

SHOP DRAWING LOG

PROJECT: New Facility for the Carver Police Department, 3 Center Street, Carver, Massachusetts								STATE PROJECT No.:			
G.C.: Tower Construction Corporation								JHA PROJECT No.: 1830			
TEAM: JH Architects (JHA); Garcia-Galuska-DeSousa (GGD); Linden Landscape Architects (LLA); Szewczak Associates (SA); Paul Hawley Associates (PHA); CAMA (CAMA); Building Engineering Resources (BER)								G.C. PROJECT No.: 2252			
JHA SHOP DRAWING NUMBER	G.C. SHOP DRAWING NUMBER	DESCRIPTION <div> <div></div> = Reviewed & Returned <div></div> = Under JHA Review <div></div> = Under Consultant Review <div></div> = Under Owner Review <div></div> = Awaiting G.C. Response </div>	DATE REC'D - From - G.C.	DATE SENT - To - Owner	DATE REC'D - From - Owner	DATE SENT - To - Consult	DATE REC'D - From - Consult	DATE RTN'D - To - G.C.	REVIEWER	ACTION / REMARK	COMMENTS
DIVISION 27 - COMMUNICATIONS											
DIVISION 31 - EARTHWORK											
312000-001-1	312000-01s	K-RAP Base	03/06/20	-	-	03/06/20	03/09/20	03/09/20	GGD	AC	
312500-001-1	312500-01s	Erosion Control	01/17/20	-	-	01/17/20	01/27/20	01/28/20	LLA	A	
312500-002-1	312500-02s	SWPPP	02/17/20	-	-	02/17/20	02/25/20	02/25/20	GGD	RR	
312500-002-2	312500-02s Rev 1	SWPPP	03/02/20	-	-	03/02/20	03/09/20	03/09/20	GGD	AC	
DIVISION 32 - EXTERIOR IMPROVEMENTS											
321313-001-1	033004-03s	Exterior Flatwork	02/19/20	-	-	02/19/20	02/24/20	02/24/20	LLA	A	
321313-002-1	321313-02s	Site Tactile Warning Tiles	04/29/20	04/30/20	04/30/20	04/29/20	04/30/20	04/30/20	LLA	AC	
321613-001-1	321613-01s	Precast Concrete Curb	04/21/20	-	-	04/21/20	04/22/20	04/22/20	LLA	A	
323113-001-1	323113-01s	Shop Drawings	07/01/20	-	-	07/01/20	07/03/20	07/06/20	LLA	A	
323913-001-1	323913-01s	Steel Bollards and Bollard Covers	04/29/20	-	-	04/29/20	04/30/20	04/30/20	LLA	AC	
DIVISION 33 - UTILITIES											
330000-001-1	330000-01	Manhole and Precast Concrete Structure	01/08/20	-	-	01/08/20	01/16/20	01/17/20	GGD	RR	
330000-001-2	330000-01s	Manhole and Precast Concrete Structure	02/17/20	-	-	02/17/20	02/25/20	02/25/20	GGD	AC	
330000-002-1	330000-01s	Site Utilities	01/17/20	-	-	01/17/20	01/28/20	01/28/20	GGD	AC	
330000-003-1	330000-02s	Sewers and Pipes	01/17/20	-	-	01/17/20	01/24/20	01/24/20	GGD	RR	
330000-004-1	033004-01s	Concrete Ductbank	02/19/20	-	-	02/19/20	02/24/20	02/24/20	GGD	RR	
330000-004-2	033004-01s Rev 1	Concrete Ductbank	03/05/20	-	-	03/06/20	03/17/20	03/17/20	GGD	A	
330000-005-1	330000-03s	K-RAP Base	02/27/20	-	-	02/27/20	-	-	-	-	VOIDED by GC - See 312000-001-1



ON-SITE REPRESENTATIVE DAILY REPORT

PROJECT:	Carver Police Station	PROJECT #:		Report Number:	163
-----------------	-----------------------	-------------------	--	-----------------------	-----

Contract Time:	Date: 10-01-2020	
Days Elapsed:	Day: Thursday	
Extensions:	Weather: Clear	
Days Remaining:	Temperature Cycle at 7 AM:	55 – 73 deg.
Site Condition:	Dry	

Contractor	Workforce	
Tower Construction	1 Superintendent, 0 laborer, 3 carpenter – Kevin Thompson (site supervision)	4
Dig It	0 operator, 0 laborer, 0 foreman (sitework)	0
Dandis	0 painter (painting)	0
Delta	2 sprinkler fitters (fire protection)	2
American Electrical	1 foreman, 0 journeyman, 0 apprentice (electrical)	1
Lapan	0 foreman, 0 journeyman, 0 apprentice, 0 insulator (mechanical)	0
Belcour	3 roofers (roofing)	3
Empire	0 foreman, 5 carpenter, 1 apprentice, (framing)	6
Hareld Glass	0 glazers (storefront)	0
Debrino	1 caulker (join sealant)	1
Commercial Masonry	0 foreman, 0 bricklayers, 0 laborers (masonry)	0
G&H	0 foreman, 0 apprentice, 0 journeyman, 0 insulator (HVAC)	0
Barber Drywall	0 foreman, 1 apprentice, 1 carpenters, 3 tapers (exterior framing)	5
	Total Workforce	23

Miscellaneous Others		
CHA	Alyssa Chatani	1
Town of Carver	Bill H., Dave S.	2
SWE	Bill Fluhr, Structural Engineer	1
New Era	Access control wiring at Comm. room	2
	Total Misc. Workforce	6

Construction Activity:

American Electrical: Continued exterior disconnects.

G&H: Not on site.

Barber: Continue to hang drywall and taping.

Delta: Testing dry system.

Commercial Masonry: Not on site.

Empire: Putting PVC bead board at entry.

Dandis: Not on site.

Belcour: Continue shingles at front side of building.

Debrino: Caulking exterior siding of PVC.

Clerk's remarks: Tower continued outbuilding soffit trim and siding.

Site Visitors/Meetings: See above

Deliveries: none

Equipment Used: Empire: (2) Boom Lift 600s, Barber (2) Scissor Lift, Commercial: Lull 944E, Mini Bobcat



ON-SITE REPRESENTATIVE DAILY REPORT

PROJECT:	Carver Police Station	PROJECT #:		Report Number:	164
-----------------	-----------------------	-------------------	--	-----------------------	-----

Contract Time:	Date: 10-02-2020	
Days Elapsed:	Day: Friday	
Extensions:	Weather: Clear	
Days Remaining:	Temperature Cycle at 7 AM:	46 – 70 deg.
Site Condition:	Dry	

Contractor	Workforce	
Tower Construction	1 Superintendent, 0 laborer, 3 carpenter – Kevin Thompson (site supervision)	4
Dig It	0 operator, 0 laborer, 0 foreman (sitework)	0
Dandis	0 painter (painting)	0
Delta	0 sprinkler fitters (fire protection)	0
American Electrical	1 foreman, 0 journeyman, 0 apprentice (electrical)	1
Lapan	0 foreman, 0 journeyman, 0 apprentice, 0 insulator (mechanical)	0
Belcour	0 roofers (roofing)	0
Empire	0 foreman, 3 carpenter, 1 apprentice, (framing)	4
Hareld Glass	0 glazers (storefront)	0
Debrino	1 caulker (join sealant)	1
Commercial Masonry	0 foreman, 0 bricklayers, 0 laborers (masonry)	0
G&H	1 foreman, 1 apprentice, 0 journeyman, 0 insulator (HVAC)	2
Barber Drywall	0 foreman, 1 apprentice, 1 carpenters, 2 tapers (exterior framing)	4
Total Workforce		16

Miscellaneous Others		
CHA	Alyssa Chatani	1
Town of Carver	Bill H., Mike Shaw, Sgt. Joe Ritz	3
Heads Up Irrigation	Robert Turner	1
Briggs	Michael	1
Total Misc. Workforce		6

Construction Activity:

American Electrical: Installing exterior disconnects for HVAC equipment.

G&H: Ductwork in attic.

Barber: Sheet rocking and taping.

Delta: Not on site.

Commercial Masonry: Not on site.

Empire: Working on trim at north side of cupola.

Dandis: Not on site.

Belcour: Not on site.

Debrino: Continue exterior caulking.

Clerk's remarks: Tower continued outbuilding siding.

Site Visitors/Meetings: See above

Deliveries: Durock

Equipment Used: Empire: (2) Boom Lift 600s, Barber (2) Scissor Lift, Commercial: Lull 944E, Mini Bobcat



ON-SITE REPRESENTATIVE DAILY REPORT

PROJECT:	Carver Police Station	PROJECT #:		Report Number:	165
-----------------	-----------------------	-------------------	--	-----------------------	-----

Contract Time:	Date: 10-05-2020	
Days Elapsed:	Day: Monday	
Extensions:	Weather: Rain	
Days Remaining:	Temperature Cycle at 7 AM:	47 – 63 deg.
Site Condition:	Dry	

Contractor	Workforce	
Tower Construction	1 Superintendent, 0 laborer, 2 carpenter – Kevin Thompson (site supervision)	3
Dig It	0 operator, 0 laborer, 0 foreman (sitework)	0
Dandis	0 painter (painting)	0
Delta	0 sprinkler fitters (fire protection)	0
American Electrical	1 foreman, 1 journeyman, 1 apprentice (electrical)	3
Lapan	0 foreman, 0 journeyman, 0 apprentice, 0 insulator (mechanical)	0
Belcour	0 roofers (roofing)	0
Empire	0 foreman, 0 carpenter, 0 apprentice, (framing)	0
Hareld Glass	2 glazers (storefront)	2
Debrino	0 caulker (join sealant)	0
Commercial Masonry	0 foreman, 3 bricklayers, 1 laborers (masonry)	4
G&H	1 foreman, 1 apprentice, 2 journeyman, 0 insulator (HVAC)	4
Barber Drywall	0 foreman, 1 apprentice, 1 carpenters, 2 tapers (exterior framing)	4
	Total Workforce	20

Miscellaneous Others		
CHA	Alyssa Chatani	1
Town of Carver	Bill H., Chief Duphily	2
	Total Misc. Workforce	3

Construction Activity:

American Electrical: Pulling electrical wire down to switch.

G&H: Additional ductwork and installing in the attic.

Barber: Continued to hang drywall and taping continues.

Delta: Not on site.

Commercial Masonry: Building up CMU walls in the mechanical room and cells.

Empire: Not on site.

Dandis: Not on site.

Hareld: Placing end dames in storefront frames.

Debrino: Not on site.

Clerk's remarks: Tower installing door frames at entry doors of outbuilding.

Site Visitors/Meetings: See above

Deliveries: none

Equipment Used: Empire: (2) Boom Lift 600s, Barber (2) Scissor Lift, Commercial: Lull 944E, Mini Bobcat



ON-SITE REPRESENTATIVE DAILY REPORT

PROJECT:	Carver Police Station	PROJECT #:		Report Number:	166
-----------------	-----------------------	-------------------	--	-----------------------	-----

Contract Time:	Date: 10-06-2020	
Days Elapsed:	Day: Tuesday	
Extensions:	Weather: Fair	
Days Remaining:	Temperature Cycle at 7 AM:	43 – 67 deg.
Site Condition:	Dry	

Contractor	Workforce	
Tower Construction	1 Superintendent, 0 laborer, 2 carpenter – Kevin Thompson (site supervision)	3
Dig It	0 operator, 0 laborer, 0 foreman (sitework)	0
Dandis	0 painter (painting)	0
Delta	1 sprinkler fitters (fire protection)	1
American Electrical	1 foreman, 0 journeyman, 0 apprentice (electrical)	1
Lapan	0 foreman, 0 journeyman, 0 apprentice, 0 insulator (mechanical)	0
Belcour	0 roofers (roofing)	0
Empire	0 foreman, 2 carpenter, 1 apprentice, (framing)	3
Hareld Glass	0 glazers (storefront)	0
Debrino	0 caulker (join sealant)	0
Commercial Masonry	0 foreman, 0 bricklayers, 0 laborers (masonry)	0
G&H	1 foreman, 1 apprentice, 1 journeyman, 0 insulator (HVAC)	3
Barber Drywall	0 foreman, 1 apprentice, 6 carpenters, 2 tapers (exterior framing)	9
	Total Workforce	20

Miscellaneous Others		
CHA	Alyssa Chatani	1
Town of Carver	Bill Harriman	1
JHA	Brian Humes	1
Debrino Caulking	Brendan & Louis	2
Eversource	1 rep	1
	Total Misc. Workforce	6

Construction Activity:

American Electrical: Continue to pull wire.

G&H: Placing ductwork inside of attic area to equipment.

Barber: Continues to install sheet rock and taping.

Delta: Installing water to system to conduct a self test in systems.

Commercial Masonry: Not on site.

Empire: Starting to place siding shingles at exterior edge of cupola.

Dandis: Not on site.

Hareld: Not on site.

Debrino: Not on site.

Clerk's remarks: Tower installing cement board siding at out building.

Site Visitors/Meetings: See above

Deliveries: 84 lumber picking up extra trim from the main building

Equipment Used: Empire: (2) Boom Lift 600s, Barber (2) Scissor Lift, Commercial: Lull 944E, Mini Bobcat



ON-SITE REPRESENTATIVE DAILY REPORT

PROJECT:	Carver Police Station	PROJECT #:		Report Number:	167
-----------------	-----------------------	-------------------	--	-----------------------	-----

Contract Time:	Date: 10-07-2020	
Days Elapsed:	Day: Wednesday	
Extensions:	Weather: Fair	
Days Remaining:	Temperature Cycle at 7 AM:	52 – 74 deg.
Site Condition:	Dry	

Contractor	Workforce	
Tower Construction	1 Superintendent, 0 laborer, 2 carpenter – Kevin Thompson (site supervision)	3
Dig It	0 operator, 0 laborer, 0 foreman (sitework)	0
Dandis	0 painter (painting)	0
Delta	0 sprinkler fitters (fire protection)	0
American Electrical	1 foreman, 1 journeyman, 1 apprentice (electrical)	3
Lapan	0 foreman, 0 journeyman, 0 apprentice, 0 insulator (mechanical)	0
Belcour	0 roofers (roofing)	0
Empire	0 foreman, 2 carpenter, 1 apprentice, (framing)	3
Hareld Glass	3 glazers (storefront)	3
Debrino	1 caulker (join sealant)	1
Commercial Masonry	0 foreman, 0 bricklayers, 0 laborers (masonry)	0
G&H	0 foreman, 0 apprentice, 0 journeyman, 0 insulator (HVAC)	0
Barber Drywall	0 foreman, 1 apprentice, 1 carpenters, 1 taper (exterior framing)	3
Total Workforce		16

Miscellaneous Others		
CHA	Alyssa Chatani	1
Town of Carver	Bill Harriman, Dave S., Chief Duphily	3
Tower Construction	Patrick Fitzgerald	1
Total Misc. Workforce		5

Construction Activity:

American Electrical: Electrical wire for lighting and switch legs.

G&H: Not on site.

Barber: Finish hanging Sheetrock. Second coat on corner bead joints.

Delta: Not on site.

Commercial Masonry: Not on site.

Empire: Continuing to install pvc shingles at rear of cupola.

Dandis: Not on site.

Hareld: Placing glass in storefront frames.

Debrino: Sealing and caulking at sealants of PVC corners.

Clerk's remarks: Tower installing trim and siding at outbuilding.

Site Visitors/Meetings: See above, weekly meeting

Deliveries: 84 lumber picking up extra trim from the main building

Equipment Used: Empire: (2) Boom Lift 600s, Barber (2) Scissor Lift, Commercial: Lull 944E, Mini Bobcat



ON-SITE REPRESENTATIVE DAILY REPORT

PROJECT:	Carver Police Station	PROJECT #:		Report Number:	168
-----------------	-----------------------	-------------------	--	-----------------------	-----

Contract Time:	Date: 10-08-2020	
Days Elapsed:	Day: Thursday	
Extensions:	Weather: Fair	
Days Remaining:	Temperature Cycle at 7 AM:	46 – 62 deg.
Site Condition:	Dry	

Contractor	Workforce	
Tower Construction	1 Superintendent, 0 laborer, 2 carpenter – Kevin Thompson (site supervision)	3
Dig It	0 operator, 0 laborer, 0 foreman (sitework)	0
Dandis	0 painter (painting)	0
Delta	2 sprinkler fitters (fire protection)	2
American Electrical	1 foreman, 1 journeyman, 1 apprentice (electrical)	3
Lapan	0 foreman, 0 journeyman, 0 apprentice, 0 insulator (mechanical)	0
Belcour	0 roofers (roofing)	0
Empire	0 foreman, 1 carpenter, 1 apprentice, (framing)	2
Hareld Glass	2 glazers (storefront)	2
Debrino	1 caulker (join sealant)	1
Commercial Masonry	0 foreman, 0 bricklayers, 0 laborers (masonry)	0
G&H	0 foreman, 0 apprentice, 0 journeyman, 0 insulator (HVAC)	0
Barber Drywall	0 foreman, 1 apprentice, 1 carpenters, 1 taper (exterior framing)	3
Total Workforce		16

Miscellaneous Others		
CHA	Alyssa Chatani	1
Town of Carver	Bill Harriman, Chief Duphily	2
Total Misc. Workforce		3

Construction Activity:

American Electrical: Continue to pull wiring inside of J-boxes to electrical room.

G&H: Not on site.

Barber: Finish wall board taping.

Delta: Placing fire suppression pump at outbuilding.

Commercial Masonry: Not on site.

Empire: Completed rear shingles at rear of cupola.

Dandis: Not on site.

Hareld: Installing glass at storefront frames and caulking.

Debrino: Not on site.

Clerk's remarks: Tower installing cement board siding at outbuilding.

Site Visitors/Meetings: See above

Deliveries: none

Equipment Used: Empire: (2) Boom Lift 600s, Barber (2) Scissor Lift, Commercial: Lull 944E, Mini Bobcat



ON-SITE REPRESENTATIVE DAILY REPORT

PROJECT:	Carver Police Station	PROJECT #:		Report Number:	169
-----------------	-----------------------	-------------------	--	-----------------------	-----

Contract Time:	Date: 10-09-2020	
Days Elapsed:	Day: Friday	
Extensions:	Weather: Fair	
Days Remaining:	Temperature Cycle at 7 AM:	35 – 59 deg.
Site Condition:	Dry	

Contractor	Workforce	
Tower Construction	1 Superintendent, 0 laborer, 2 carpenter – Kevin Thompson (site supervision)	3
Dig It	0 operator, 0 laborer, 0 foreman (sitework)	0
Dandis	0 painter (painting)	0
Delta	0 sprinkler fitters (fire protection)	0
American Electrical	1 foreman, 1 journeyman, 1 apprentice (electrical)	3
Lapan	0 foreman, 0 journeyman, 0 apprentice, 0 insulator (mechanical)	0
Belcour	0 roofers (roofing)	0
Empire	1 foreman, 2 carpenter, 1 apprentice, (framing)	4
Hareld Glass	0 glazers (storefront)	0
Debrino	1 caulker (join sealant)	1
Commercial Masonry	0 foreman, 0 bricklayers, 0 laborers (masonry)	0
G&H	1 foreman, 1 apprentice, 1 journeyman, 0 insulator (HVAC)	3
Barber Drywall	0 foreman, 0 apprentice, 0 carpenters, 3 taper (exterior framing)	3
	Total Workforce	17

Miscellaneous Others		
CHA	Alyssa Chatani	1
Town of Carver	Bill Harriman, Mike Shaw, Det. Bill Kelly	3
Cape Cod Vac	Continue to rough in central vac	2
	Total Misc. Workforce	6

Construction Activity:

American Electrical: Continue pulling wire to outlets.

G&H: Placing ductwork in attic and to units.

Barber: Continues to finish wall board with taping.

Delta: Not on site.

Commercial Masonry: Not on site.

Empire: Installing shingles at front side of cupola. Building and framing around attic access door.

Dandis: Not on site.

Hareld: Not on site.

Debrino: Caulking around windows and blocks.

Clerk's remarks: Tower installing cement board siding at outbuilding.

Site Visitors/Meetings: See above

Deliveries: none

Equipment Used: Empire: (2) Boom Lift 600s, Barber (2) Scissor Lift, Commercial: Lull 944E, Mini Bobcat



ON-SITE REPRESENTATIVE DAILY REPORT

PROJECT:	Carver Police Station	PROJECT #:		Report Number:	170
-----------------	-----------------------	-------------------	--	-----------------------	-----

Contract Time:	Date: 10-12-2020	
Days Elapsed:	Day: Monday	
Extensions:	Weather: Fair	
Days Remaining:	Temperature Cycle at 7 AM:	50 – 56 deg.
Site Condition:	Dry	

Contractor	Workforce	
Tower Construction	1 Superintendent, 0 laborer, 0 carpenter – Kevin Thompson (site supervision)	1
Dig It	1 operator, 2 laborer, 1 foreman (sitework)	4
Dandis	0 painter (painting)	0
Delta	0 sprinkler fitters (fire protection)	0
American Electrical	0 foreman, 0 journeyman, 0 apprentice (electrical)	0
Lapan	0 foreman, 0 journeyman, 0 apprentice, 0 insulator (mechanical)	0
Belcour	0 roofers (roofing)	0
Empire	0 foreman, 0 carpenter, 0 apprentice, (framing)	0
Hareld Glass	0 glazers (storefront)	0
Debrino	0 caulker (join sealant)	0
Commercial Masonry	0 foreman, 0 bricklayers, 0 laborers (masonry)	0
G&H	0 foreman, 0 apprentice, 0 journeyman, 0 insulator (HVAC)	0
Barber Drywall	0 foreman, 0 apprentice, 0 carpenters, 2 taper (exterior framing)	2
	Total Workforce	7

Miscellaneous Others		
CHA	Alyssa Chatani	0
Town of Carver	Bill Harriman, Dave S.	2
	Total Misc. Workforce	2

Construction Activity:

American Electrical: Not on site.

G&H: Not on site.

Barber: Continue finishing wallboard with joint compound at locker rooms and office areas. Continue sanding walls to prepare for priming.

Delta: Not on site.

Dig It: Prepping and laying out the site to prepare for binder.

Empire: Not on site.

Dandis: Not on site.

Hareld: Not on site.

Debrino: Not on site.

Clerk's remarks: Union holiday/reduced manpower

Site Visitors/Meetings: See above

Deliveries: none

Equipment Used: Empire: (2) Boom Lift 600s, Barber (2) Scissor Lift, Commercial: Lull 944E, Mini Bobcat



ON-SITE REPRESENTATIVE DAILY REPORT

PROJECT:	Carver Police Station	PROJECT #:		Report Number:	171
-----------------	-----------------------	-------------------	--	-----------------------	-----

Contract Time:	Date: 10-13-2020	
Days Elapsed:	Day: Tuesday	
Extensions:	Weather: Cloudy	
Days Remaining:	Temperature Cycle at 7 AM:	54 – 66 deg.
Site Condition:	Dry	

Contractor	Workforce	
Tower Construction	1 Superintendent, 0 laborer, 2 carpenters – Kevin Thompson (site supervision)	3
Dig It	1 operator, 1 laborer, 1 foreman (sitework)	3
Dandis	0 painter (painting)	0
Delta	3 sprinkler fitters (fire protection)	3
American Electrical	0 foreman, 0 journeyman, 0 apprentice (electrical)	0
Lapan	1 foreman, 0 journeyman, 0 apprentice, 0 insulator (mechanical)	1
Belcour	0 roofers (roofing)	0
Empire	0 foreman, 0 carpenter, 0 apprentice, (framing)	0
Hareld Glass	0 glazers (storefront)	0
Debrino	2 caulkers (join sealant)	2
Commercial Masonry	0 foreman, 0 bricklayers, 0 laborers (masonry)	0
G&H	1 foreman, 1 apprentice, 1 journeyman, 0 insulator (HVAC)	3
Barber Drywall	0 foreman, 0 apprentice, 0 carpenters, 2 taper (exterior framing)	2
Total Workforce		

Miscellaneous Others		
CHA	Alyssa Chatani	1
Town of Carver	Bill Harriman	1
Comm Tech & E911	Scott Gray & Comm Tech rep	2
Total Misc. Workforce		4

Construction Activity:

American Electrical: Not on site.

G&H: Continuing refrigerant lines in main building and ductwork in attic.

Barber: Continue taping and sanding walls.

Delta: Installing sprinkler piping in outbuilding.

Dig It: Bringing in common fill. Working on fire suppression line next to outbuilding.

Lapan: Install outbuilding vent. Install domestic water main.

Dandis: Not on site.

Hareld: Not on site.

Debrino: Caulking the cell area and door frames.

Clerk's remarks: Tower is continuing wood blocking around overhead doors at Sally Port.

Site Visitors/Meetings: See above

Deliveries: common fill

Equipment Used: Empire: (2) Boom Lift 600s, Barber (2) Scissor Lift, Commercial: Lull 944E, Mini Bobcat

PROJECT:	Carver Police Station	PROJECT #:		Report Number:	172
-----------------	-----------------------	-------------------	--	-----------------------	-----

Contract Time:	Date: 10-14-2020	
Days Elapsed:	Day: Wednesday	
Extensions:	Weather: Cloudy	
Days Remaining:	Temperature Cycle at 7 AM:	47 – 68 deg.
Site Condition:	Dry	

Contractor	Workforce	
Tower Construction	1 Superintendent, 0 laborer, 2 carpenters – Kevin Thompson (site supervision)	3
Dig It	1 operator, 1 laborer, 1 foreman (sitework)	3
Dandis	0 painter (painting)	0
Delta	2 sprinkler fitters (fire protection)	2
American Electrical	0 foreman, 0 journeyman, 0 apprentice (electrical)	0
Lapan	1 foreman, 0 journeyman, 0 apprentice, 0 insulator (mechanical)	1
Belcour	0 roofers (roofing)	0
Empire	0 foreman, 0 carpenter, 0 apprentice, (framing)	0
Hareld Glass	0 glazers (storefront)	0
Debrino	2 caulkers (join sealant)	2
Commercial Masonry	0 foreman, 0 bricklayers, 0 laborers (masonry)	0
G&H	1 foreman, 1 apprentice, 1 journeyman, 0 insulator (HVAC)	3
Barber Drywall	0 foreman, 0 apprentice, 0 carpenters, 3 taper (exterior framing)	3
Total Workforce		17

Miscellaneous Others		
CHA	Alyssa Chatani, Joe Sullivan	2
Town of Carver	Bill Harriman, Chief Duphily, Dave R., Dave S.,	4
Tower Construction	Patrick Fitzgerald	1
S&D Road Service	Lift maintenance	1
Cape Cod Vac	Continue remaining piping in corridor.	2
Total Misc. Workforce		10

Construction Activity:

American Electrical: Not on site.

G&H: Continue installing ductwork inside the attic area to overhead units.

Barber: Continue joint compound and sanding interior walls.

Delta: Continue placing 6" fire main from outbuilding to hydrant.

Dig It: Continue working on layout of roadway and bringing in fill.

Lapan: Installing vent piping in outbuilding and the water meter.

Dandis: Not on site.

Hareld: Not on site.

Debrino: Continue working on exterior, caulking on the east side of building.

Clerk's remarks: Weekly meeting, site cookout

Site Visitors/Meetings: See above

Deliveries: none

Equipment Used: Empire: (2) Boom Lift 600s, Barber (2) Scissor Lift, Commercial: Lull 944E, Mini Bobcat



ON-SITE REPRESENTATIVE DAILY REPORT

PROJECT:	Carver Police Station	PROJECT #:		Report Number:	173
-----------------	-----------------------	-------------------	--	-----------------------	-----

Contract Time:	Date: 10-15-2020	
Days Elapsed:	Day: Thursday	
Extensions:	Weather: Cloudy	
Days Remaining:	Temperature Cycle at 7 AM:	45 – 70 deg.
Site Condition:	Dry	

Contractor	Workforce	
Tower Construction	1 Superintendent, 0 laborer, 2 carpenters – Kevin Thompson (site supervision)	3
Dig It	1 operator, 1 laborer, 1 foreman (sitework)	3
Dandis	1 painter (painting)	1
Delta	3 sprinkler fitters (fire protection)	3
American Electrical	1 foreman, 1 journeyman, 1 apprentice (electrical)	3
Lapan	0 foreman, 0 journeyman, 0 apprentice, 0 insulator (mechanical)	0
Belcour	0 roofers (roofing)	0
Empire	0 foreman, 1 carpenter, 0 apprentice, (framing)	1
Hareld Glass	0 glazers (storefront)	0
Debrino	2 caulkers (join sealant)	2
Commercial Masonry	0 foreman, 0 bricklayers, 0 laborers (masonry)	0
G&H	0 foreman, 0 apprentice, 0 journeyman, 0 insulator (HVAC)	0
Barber Drywall	0 foreman, 1 apprentice, 2 carpenters, 2 taper (exterior framing)	5
Total Workforce		21

Miscellaneous Others		
CHA	Alyssa Chatani	1
Town of Carver	Bill Harriman, Dave S.	2
Sun Dog	Doug	1
Dig It	Kerry	1
Total Misc. Workforce		5

Construction Activity:

American Electrical: Continue wiring into main electrical room.

G&H: Not on site.

Barber: Continue to finish wall board, sanding out walls.

Delta: Installing fire hydrant next to existing parking lot piping.

Dig It: Bringing in T-base for road bed.

Empire: Working on cupola exterior and PVC shingles.

Dandis: Placing primer around interior door frames.

Hareld: Not on site.

Debrino: Caulking exterior north side of main building and seams of PVC.

Clerk's remarks: Tower finished up exterior siding on outbuilding.

Site Visitors/Meetings: See above

Deliveries: t-base

Equipment Used: Empire: (2) Boom Lift 600s, Barber (2) Scissor Lift, Commercial: Lull 944E, Mini Bobcat



ON-SITE REPRESENTATIVE DAILY REPORT

PROJECT:	Carver Police Station	PROJECT #:		Report Number:	174
-----------------	-----------------------	-------------------	--	-----------------------	-----

Contract Time:	Date: 10-16-2020	
Days Elapsed:	Day: Friday	
Extensions:	Weather: Clear	
Days Remaining:	Temperature Cycle at 7 AM:	54 – 70 deg.
Site Condition:	Dry	

Contractor	Workforce	
Tower Construction	1 Superintendent, 0 laborer, 2 carpenters – Kevin Thompson (site supervision)	3
Dig It	1 operator, 1 laborer, 1 foreman (sitework)	3
Dandis	2 painter (painting)	2
Delta	2 sprinkler fitters (fire protection)	2
American Electrical	1 foreman, 1 journeyman, 0 apprentice (electrical)	2
Lapan	0 foreman, 0 journeyman, 0 apprentice, 0 insulator (mechanical)	0
Belcour	2 roofers (roofing)	2
Empire	0 foreman, 1 carpenter, 0 apprentice, (framing)	1
Hareld Glass	0 glazers (storefront)	0
Debrino	2 caulkers (join sealant)	2
Commercial Masonry	0 foreman, 0 bricklayers, 0 laborers (masonry)	0
G&H	0 foreman, 0 apprentice, 1 journeyman, 0 insulator (HVAC)	1
Barber Drywall	0 foreman, 0 apprentice, 0 carpenters, 0 taper (exterior framing)	0
Total Workforce		18

Miscellaneous Others		
CHA	Alyssa Chatani	1
Town of Carver	Bill Harriman, Mike Shaw	2
New Era	Mike	1
Superior Propane	1 rep	1
Verizon	Telecomm crew	2
Total Misc. Workforce		7

Construction Activity:

American Electrical: Running power wiring for outlets and rights back to electrical room.

G&H: Installing the exterior air intake on outbuilding.

Barber: Not on site.

Delta: Running a test on fire suppression system on outbuilding.

Dig It: Bringing in a T-base for roadway binder.

Empire: Placing exterior PVC shingles on the front side of cupola.

Dandis: Started interior wall priming of north side.

Belcour: Finishing outbuilding roof

Debrino: Sealing up interior door frame edges with caulking.

Clerk's remarks: none

Site Visitors/Meetings: See above

Deliveries: t-base

Equipment Used: Empire: (2) Boom Lift 600s, Barber (2) Scissor Lift, Commercial: Lull 944E, Mini Bobcat



ON-SITE REPRESENTATIVE DAILY REPORT

PROJECT:	Carver Police Station	PROJECT #:		Report Number:	175
-----------------	-----------------------	-------------------	--	-----------------------	-----

Contract Time:	Date: 10-19-2020	
Days Elapsed:	Day: Monday	
Extensions:	Weather: Clear	
Days Remaining:	Temperature Cycle at 7 AM:	43 – 64 deg.
Site Condition:	Dry	

Contractor	Workforce	
Tower Construction	1 Superintendent, 0 laborer, 0 carpenters – Kevin Thompson (site supervision)	1
Dig It	2 operator, 2 laborer, 1 foreman (sitework)	5
Dandis	1 painter (painting)	1
Delta	1 sprinkler fitters (fire protection)	1
American Electrical	1 foreman, 1 journeyman, 0 apprentice (electrical)	2
Lapan	1 foreman, 0 journeyman, 0 apprentice, 0 insulator (mechanical)	1
Belcour	0 roofers (roofing)	0
Empire	0 foreman, 1 carpenter, 1 apprentice, (framing)	2
Hareld Glass	0 glazers (storefront)	0
Debrino	2 caulkers (join sealant)	2
Commercial Masonry	0 foreman, 0 bricklayers, 0 laborers (masonry)	0
G&H	1 foreman, 1 apprentice, 1 journeyman, 0 insulator (HVAC)	3
Barber Drywall	0 foreman, 0 apprentice, 0 carpenters, 0 taper (exterior framing)	0
Total Workforce		18

Miscellaneous Others		
CHA	Alyssa Chatani, Joe Sullivan	2
Town of Carver	Chief Duphily, Dave S., Jesse Boyle	3
B&B Lightning Protection	Outbuilding lightning protection	2
Total Misc. Workforce		7

Construction Activity:

American Electrical: Continue overhead wiring at main building for power and lighting.

G&H: Continue ductwork install in the attic.

Barber: Not on site.

Delta: Testing fire suppression system with FD.

Dig It: Continue bringing in fill and compacting for binder on Friday.

Empire: Completed cupola trim and siding.

Dandis: Continue painting at exterior and priming interior walls.

Lapan: Connecting 1" water line in outbuilding and water meter.

Debrino: Continue caulking at exterior trim.

Clerk's remarks: none

Site Visitors/Meetings: See above

Deliveries: water heater, t-base

Equipment Used: Empire: (2) Boom Lift 600s, Barber (2) Scissor Lift, Commercial: Lull 944E, Mini Bobcat



ON-SITE REPRESENTATIVE DAILY REPORT

PROJECT:	Carver Police Station	PROJECT #:		Report Number:	176
-----------------	-----------------------	-------------------	--	-----------------------	-----

Contract Time:	Date: 10-20-2020	
Days Elapsed:	Day: Tuesday	
Extensions:	Weather: Clear	
Days Remaining:	Temperature Cycle at 7 AM:	43 – 64 deg.
Site Condition:	Dry	

Contractor	Workforce	
Tower Construction	1 Superintendent, 0 laborer, 0 carpenters – Kevin Thompson (site supervision)	1
Dig It	1 operator, 1 laborer, 1 foreman (sitework)	3
Dandis	1 painter (painting)	1
Delta	1 sprinkler fitters (fire protection)	1
American Electrical	1 foreman, 1 journeyman, 1 apprentice (electrical)	3
Lapan	1 foreman, 0 journeyman, 0 apprentice, 0 insulator (mechanical)	1
Belcour	0 roofers (roofing)	0
Empire	0 foreman, 1 carpenter, 1 apprentice, (framing)	2
Hareld Glass	0 glazers (storefront)	0
Debrino	2 caulkers (join sealant)	2
Commercial Masonry	0 foreman, 0 bricklayers, 0 laborers (masonry)	0
G&H	1 foreman, 1 apprentice, 1 journeyman, 0 insulator (HVAC)	3
Barber Drywall	0 foreman, 0 apprentice, 0 carpenters, 0 taper (exterior framing)	0
	Total Workforce	17

Miscellaneous Others		
CHA	Alyssa Chatani, Joe Sullivan	2
Town of Carver	Bill Harriman, Dave S., Jesse Boyle	3
Next Generation	Installing overhead door at sally port.	2
	Total Misc. Workforce	7

Construction Activity:

American Electrical: Continue fire alarm cable wiring.

G&H: Continue ductwork at attic area.

Barber: Not on site.

Delta: Testing underground fire sprinkler piping at outbuilding.

Dig It: Continue prepping for binder. Installed underground conduit for future gate.

Empire: Completed cupola trim and siding touch-ups.

Dandis: Painting sally port ceiling walls and piping.

Lapan: Installing water line into fire pump room at outbuilding.

Debrino: Continue interior caulking door frames and exterior seams.

Clerk's remarks: none

Site Visitors/Meetings: See above

Deliveries: none

Equipment Used: Empire: (2) Boom Lift 600s, Barber (2) Scissor Lift, Commercial: Lull 944E, Mini Bobcat



ON-SITE REPRESENTATIVE DAILY REPORT

PROJECT:	Carver Police Station	PROJECT #:		Report Number:	177
-----------------	-----------------------	-------------------	--	-----------------------	-----

Contract Time:	Date: 10-21-2020	
Days Elapsed:	Day: Wednesday	
Extensions:	Weather: Fog	
Days Remaining:	Temperature Cycle at 7 AM:	58 – 70 deg.
Site Condition:	Dry	

Contractor	Workforce	
Tower Construction	1 Superintendent, 0 laborer, 0 carpenters – Kevin Thompson (site supervision)	1
Dig It	1 operator, 1 laborer, 1 foreman (sitework)	3
Dandis	1 painter (painting)	1
Delta	1 sprinkler fitters (fire protection)	1
American Electrical	1 foreman, 1 journeyman, 1 apprentice (electrical)	3
Lapan	1 foreman, 0 journeyman, 0 apprentice, 0 insulator (mechanical)	1
Belcour	0 roofers (roofing)	0
Empire	0 foreman, 0 carpenter, 0 apprentice, (framing)	0
Hareld Glass	0 glazers (storefront)	0
Debrino	2 caulkers (join sealant)	2
Commercial Masonry	0 foreman, 0 bricklayers, 0 laborers (masonry)	0
G&H	0 foreman, 0 apprentice, 0 journeyman, 0 insulator (HVAC)	0
Barber Drywall	0 foreman, 0 apprentice, 0 carpenters, 0 taper (exterior framing)	0
	Total Workforce	12

Miscellaneous Others		
CHA	Alyssa Chatani, Joe Sullivan	2
Town of Carver	Bill Harriman, Dave S., Chief Duphily	3
Next Generation	Installing overhead door at sally port.	2
American Flag Pole	Installing flag pole foundation	1
DPH	Preliminary review of cell area	1
Briggs	Compaction testing	1
Eversource	Crew installing new pole	1
	Total Misc. Workforce	11

Construction Activity:

American Electrical: Continue install of wiring for lighting and fire alarm.

G&H: Not on site.

Delta: Testing underground sprinkler line to outbuilding and hydrant.

Dig It: Prepping for asphalt pavement and layout.

Dandis: Priming walls at sally port area.

Lapan: Installing mechanical room piping, water service meter.

Debrino: Continue caulking interior door frames.

Clerk's remarks: Began installing pockets for shades at window shade locations.

Site Visitors/Meetings: See above, weekly meeting

Deliveries: sheet rock, toilet accessories

Equipment Used: Empire: (2) Boom Lift 600s, Barber (2) Scissor Lift, Commercial: Lull 944E, Mini Bobcat



ON-SITE REPRESENTATIVE DAILY REPORT

PROJECT:	Carver Police Station	PROJECT #:		Report Number:	178
-----------------	-----------------------	-------------------	--	-----------------------	-----

Contract Time:	Date: 10-22-2020	
Days Elapsed:	Day: Thursday	
Extensions:	Weather: Cloudy	
Days Remaining:	Temperature Cycle at 7 AM:	55 – 72 deg.
Site Condition:	Dry	

Contractor	Workforce	
Tower Construction	1 Superintendent, 0 laborer, 0 carpenters – Kevin Thompson (site supervision)	1
Dig It	1 operator, 1 laborer, 1 foreman (sitework)	3
Dandis	1 painter (painting)	1
Delta	0 sprinkler fitters (fire protection)	0
American Electrical	1 foreman, 1 journeyman, 1 apprentice (electrical)	3
Lapan	1 foreman, 0 journeyman, 0 apprentice, 0 insulator (mechanical)	1
Belcour	0 roofers (roofing)	0
Empire	0 foreman, 0 carpenter, 0 apprentice, (framing)	0
Hareld Glass	0 glazers (storefront)	0
Debrino	2 caulkers (join sealant)	2
Commercial Masonry	0 foreman, 0 bricklayers, 0 laborers (masonry)	0
G&H	0 foreman, 1 apprentice, 1 journeyman, 0 insulator (HVAC)	2
Barber Drywall	0 foreman, 1 apprentice, 4 carpenters, 0 taper (exterior framing)	5
	Total Workforce	18

Miscellaneous Others		
CHA	Alyssa Chatani	1
Town of Carver	Bill Harriman, Dave S., Chief Duphily, Mike Shaw	4
	Total Misc. Workforce	5

Construction Activity:

American Electrical: Continues to pull wiring back to electrical room.

G&H: Installing refrigerant lines inside attic areas.

Delta: Not on site.

Dig It: Continue to prep for binder.

Dandis: Priming and painting exterior PVC.

Lapan: Installing copper water connections inside of mechanical room.

Debrino: Continue interior caulking.

Barber: Sheet rocking and topping out walls and continue outbuilding framing.

Clerk's remarks: none

Site Visitors/Meetings: See above

Deliveries: none

Equipment Used: Empire: (2) Boom Lift 600s, Barber (2) Scissor Lift, Commercial: Lull 944E, Mini Bobcat



ON-SITE REPRESENTATIVE DAILY REPORT

PROJECT:	Carver Police Station	PROJECT #:		Report Number:	179
-----------------	-----------------------	-------------------	--	-----------------------	-----

Contract Time:	Date: 10-23-2020	
Days Elapsed:	Day: Friday	
Extensions:	Weather: Cloudy	
Days Remaining:	Temperature Cycle at 7 AM:	52 – 69 deg.
Site Condition:	Dry	

Contractor	Workforce	
Tower Construction	1 Superintendent, 0 laborer, 0 carpenters – Kevin Thompson (site supervision)	1
Dig It	1 operator, 1 laborer, 1 foreman, 2 dirtworks (sitework)	5
Dandis	3 painter (painting)	3
Delta	0 sprinkler fitters (fire protection)	0
American Electrical	1 foreman, 1 journeyman, 1 apprentice (electrical)	3
Lapan	1 foreman, 0 journeyman, 0 apprentice, 0 insulator (mechanical)	1
Belcour	0 roofers (roofing)	0
Empire	0 foreman, 1 carpenter, 1 apprentice, (framing)	2
Hareld Glass	0 glazers (storefront)	0
Debrino	2 caulkers (join sealant)	2
Commercial Masonry	0 foreman, 0 bricklayers, 0 laborers (masonry)	0
G&H	0 foreman, 1 apprentice, 2 journeyman, 0 insulator (HVAC)	3
Barber Drywall	0 foreman, 1 apprentice, 3 carpenters, 0 taper (exterior framing)	4
Total Workforce		24

Miscellaneous Others		
CHA	Alyssa Chatani	1
Town of Carver	Bill Harriman	1
Central Ceilings	1 rep	1
Eversource	Crew continuing new pole work	5
Total Misc. Workforce		8

Construction Activity:

American Electrical: Installing electrical panels in electrical room/outbuilding wiring.

G&H: Continue refrigerant like sets at attic area.

Empire: Constructing crickets on roof/hatch security ceilings.

Dig It: Installing roof drain system in main building. Grading for binder.

Dandis: Exterior PVC painting at cupola and gable ends.

Lapan: Installing piping for water heater.

Debrino: Caulking/sealing outbuilding PVC trim.

Barber: Topping out walls in main building.

Clerk's remarks: none

Site Visitors/Meetings: See above

Deliveries: sheet rock

Equipment Used: Empire: (2) Boom Lift 600s, Barber (2) Scissor Lift, Commercial: Lull 944E, Mini Bobcat

PROJECT:	Carver Police Station	PROJECT #:		Report Number:	180
-----------------	-----------------------	-------------------	--	-----------------------	-----

Contract Time:	Date: 10-26-2020	
Days Elapsed:	Day: Monday	
Extensions:	Weather: Cloudy	
Days Remaining:	Temperature Cycle at 7 AM:	47 – 57 deg.
Site Condition:	Dry	

Contractor	Workforce	
Tower Construction	1 Superintendent, 0 laborer, 0 carpenters – Kevin Thompson (site supervision)	1
Dig It	0 operator, 1 laborer, 1 foreman, 8 dirtworks (sitework)	10
Dandis	2 painter (painting)	2
Delta	0 sprinkler fitters (fire protection)	0
American Electrical	1 foreman, 0 journeyman, 1 apprentice (electrical)	2
Lapan	1 foreman, 0 journeyman, 0 apprentice, 0 insulator (mechanical)	1
Belcour	0 roofers (roofing)	0
Central Ceilings	1 carpenter (acoustical ceilings)	1
Hareld Glass	0 glazers (storefront)	0
Debrino	0 caulkers (join sealant)	0
Commercial Masonry	0 foreman, 0 bricklayers, 0 laborers (masonry)	0
G&H	0 foreman, 2 apprentice, 2 journeyman, 0 insulator (HVAC)	4
Barber Drywall	0 foreman, 1 apprentice, 1 carpenters, 1 taper (exterior framing)	3
Total Workforce		

Miscellaneous Others		
CHA	Alyssa Chatani	1
Town of Carver	Bill Harriman	1
Briggs	Asphalt testing	1
T&C Woodworking	Measuring and laying out casework.	1
Viking Industries	Continue ductwork insulation	1
Total Misc. Workforce		5

Construction Activity:

American Electrical: Building out the electrical room. Wiring the outbuilding.

G&H: Continue drains at main building. Continue rough in at outbuilding.

Central Ceilings: Begin installing acoustical grid.

Dig It: Continue to set elevation markers and grade out west elevation. Asphalt paving the binder course.

Dandis: Continue exterior trim painting and above ceiling areas.

Lapan: Installing water heater.

Debrino: Not on site.

Barber: Boarding tops and misc. taping.

Clerk's remarks: none

Site Visitors/Meetings: See above

Deliveries: insulation, asphalt, cat 6 cable

Equipment Used: Empire: (2) Boom Lift 600s, Barber (2) Scissor Lift, Commercial: Lull 944E, Mini Bobcat



ON-SITE REPRESENTATIVE DAILY REPORT

PROJECT:	Carver Police Station	PROJECT #:		Report Number:	181
-----------------	-----------------------	-------------------	--	-----------------------	-----

Contract Time:	Date: 10-27-2020	
Days Elapsed:	Day: Tuesday	
Extensions:	Weather: Cloudy	
Days Remaining:	Temperature Cycle at 7 AM:	47 – 57 deg.
Site Condition:	Dry	

Contractor	Workforce	
Tower Construction	1 Superintendent, 0 laborer, 0 carpenters – Kevin Thompson (site supervision)	1
Dig It	1 operator, 1 laborer, 1 foreman, 0 dirtworks (sitework)	3
Dandis	2 painter (painting)	2
Delta	0 sprinkler fitters (fire protection)	0
American Electrical	1 foreman, 0 journeyman, 0 apprentice (electrical)	1
Lapan	1 foreman, 0 journeyman, 0 apprentice, 0 insulator (mechanical)	1
Belcour	0 roofers (roofing)	0
Central Ceilings	1 carpenter (acoustical ceilings)	1
Hareld Glass	0 glazers (storefront)	0
Debrino	0 caulkers (join sealant)	0
Commercial Masonry	0 foreman, 0 bricklayers, 0 laborers (masonry)	0
G&H	0 foreman, 1 apprentice, 1 journeyman, 0 insulator (HVAC)	2
Barber Drywall	0 foreman, 0 apprentice, 0 carpenters, 1 taper (exterior framing)	1
	Total Workforce	12

Miscellaneous Others		
CHA	Alyssa Chatani	1
Town of Carver	Bill Harriman	1
	Total Misc. Workforce	2

Construction Activity:

American Electrical: Placing electrical cabinets inside electrical room.

G&H: Continue to install line sets in the attic for HVAC units.

Central Ceilings: Installing ceiling grid and ties inside office sections.

Dig It: Laying out pre-cast curbing in parking area.

Dandis: Exterior painting PVC along the front area of the building.

Lapan: Installing water heater on piping in mechanical room.

Debrino: Not on site.

Barber: Continue taping wallboard sections inside of training room and fire taping above ceiling areas.

Clerk's remarks: none

Site Visitors/Meetings: See above

Deliveries: misc electrical items

Equipment Used: Empire: (2) Boom Lift 600s, Barber (2) Scissor Lift, Commercial: Lull 944E, Mini Bobcat



ON-SITE REPRESENTATIVE DAILY REPORT

PROJECT:	Carver Police Station	PROJECT #:		Report Number:	182
-----------------	-----------------------	-------------------	--	-----------------------	-----

Contract Time:	Date: 10-28-2020	
Days Elapsed:	Day: Wednesday	
Extensions:	Weather: Cloudy	
Days Remaining:	Temperature Cycle at 7 AM:	47 – 57 deg.
Site Condition:	Dry	

Contractor	Workforce	
Tower Construction	1 Superintendent, 0 laborer, 0 carpenters – Kevin Thompson (site supervision)	1
Dig It	0 operator, 0 laborer, 0 foreman, 0 dirtworks (sitework)	0
Dandis	1 painter (painting)	1
Delta	0 sprinkler fitters (fire protection)	0
American Electrical	1 foreman, 0 journeyman, 0 apprentice (electrical)	1
Lapan	0 foreman, 0 journeyman, 0 apprentice, 0 insulator (mechanical)	0
Belcour	0 roofers (roofing)	0
Central Ceilings	1 carpenter (acoustical ceilings)	1
Hareld Glass	0 glazers (storefront)	0
Debrino	0 caulkers (join sealant)	0
Commercial Masonry	0 foreman, 0 bricklayers, 0 laborers (masonry)	0
G&H	0 foreman, 1 apprentice, 1 journeyman, 0 insulator (HVAC)	2
Barber Drywall	0 foreman, 0 apprentice, 0 carpenters, 0 taper (exterior framing)	0
Total Workforce		6

Miscellaneous Others		
CHA	Alyssa Chatani	1
Town of Carver	Bill Harriman, Dave S.	1
Bobe Materials	Jeff (wire mesh partitions)	1
S&S	Steve Child	1
Verizon	Site Visit	2
Total Misc. Workforce		6

Construction Activity:

American Electrical: Wiring in electrical room and electrical panel installation.

G&H: Continue to install pre-manufactured line sets to HVAC units inside the attic areas.

Central Ceilings: Placing grid in office areas at the west area of the building.

Dig It: Not on site.

Dandis: Placing primer on CMU on the exterior walls of the Sally Port.

Lapan: Not on site.

Debrino: Not on site.

Barber: Taping in the training room and touching up walls.

Clerk's remarks: none

Site Visitors/Meetings: See above, weekly meeting

Deliveries: none

Equipment Used: Empire: (2) Boom Lift 600s, Barber (2) Scissor Lift, Commercial: Lull 944E, Mini Bobcat



ON-SITE REPRESENTATIVE DAILY REPORT

PROJECT:	Carver Police Station	PROJECT #:		Report Number:	183
-----------------	-----------------------	-------------------	--	-----------------------	-----

Contract Time:	Date: 10-29-2020	
Days Elapsed:	Day: Thursday	
Extensions:	Weather: Fair	
Days Remaining:	Temperature Cycle at 7 AM:	44 – 49 deg.
Site Condition:	Dry	

Contractor	Workforce	
Tower Construction	1 Superintendent, 0 laborer, 0 carpenters – Kevin Thompson (site supervision)	1
Dig It	0 operator, 0 laborer, 0 foreman, 0 dirtworks (sitework)	0
Dandis	0 painter (painting)	0
Delta	0 sprinkler fitters (fire protection)	0
American Electrical	1 foreman, 0 journeyman, 1 apprentice (electrical)	2
Lapan	0 foreman, 0 journeyman, 0 apprentice, 0 insulator (mechanical)	0
Belcour	0 roofers (roofing)	0
Central Ceilings	1 carpenter (acoustical ceilings)	1
Hareld Glass	0 glazers (storefront)	0
Debrino	0 caulkers (join sealant)	0
Commercial Masonry	0 foreman, 0 bricklayers, 0 laborers (masonry)	0
G&H	0 foreman, 1 apprentice, 1 journeyman, 0 insulator (HVAC)	2
Barber Drywall	0 foreman, 1 apprentice, 2 carpenters, 2 taper (exterior framing)	5
Total Workforce		11

Miscellaneous Others		
CHA	Alyssa Chatani	1
Town of Carver	Chief Duphily	1
Central Ceiling	1 rep reviewing layout	1
Jails	Starting to install steel ceilings in cell areas.	1
Total Misc. Workforce		4

Construction Activity:

American Electrical: Installing electrical cabinets inside of electrical room.

G&H: Continues to install line set terminations to units in attic and installing unit heater in fire pump room in outbuilding.

Central Ceilings: Attaching ceiling grid in Chief's offices and day room.

Dig It: Not on site.

Dandis: Not on site.

Lapan: Not on site.

Debrino: Not on site.

Barber: Taping and sanding training room and fire taping.

Clerk's remarks: none

Site Visitors/Meetings: See above

Deliveries: steel ceiling delivery, misc. electrical

Equipment Used: Empire: (2) Boom Lift 600s, Barber (2) Scissor Lift, Commercial: Lull 944E, Mini Bobcat



ON-SITE REPRESENTATIVE DAILY REPORT

PROJECT:	Carver Police Station	PROJECT #:		Report Number:	184
-----------------	-----------------------	-------------------	--	-----------------------	-----

Contract Time:	Date: 10-30-2020	
Days Elapsed:	Day: Friday	
Extensions:	Weather: Rain/Snow	
Days Remaining:	Temperature Cycle at 7 AM:	30 – 47 deg.
Site Condition:	Wet	

Contractor	Workforce	
Tower Construction	1 Superintendent, 0 laborer, 0 carpenters – Kevin Thompson (site supervision)	1
Dig It	0 operator, 0 laborer, 0 foreman, 0 dirtworks (sitework)	0
Dandis	0 painter (painting)	0
Delta	0 sprinkler fitters (fire protection)	0
American Electrical	1 foreman, 0 journeyman, 1 apprentice (electrical)	2
Lapan	0 foreman, 0 journeyman, 0 apprentice, 0 insulator (mechanical)	0
Belcour	0 roofers (roofing)	0
Central Ceilings	1 carpenter (acoustical ceilings)	1
Hareld Glass	0 glazers (storefront)	0
Debrino	0 caulkers (join sealant)	0
Commercial Masonry	0 foreman, 0 bricklayers, 0 laborers (masonry)	0
G&H	0 foreman, 1 apprentice, 1 journeyman, 0 insulator (HVAC)	2
Barber Drywall	0 foreman, 1 apprentice, 2 carpenters, 0 taper (exterior framing)	3
	Total Workforce	9

Miscellaneous Others		
CHA	Alyssa Chatani	1
Town of Carver	Bill Harriman	1
New Era	Mike	1
Jails	Bolting the steel pan ceilings inside of the cell areas	1
Xfinity/Comcast	Site visit for fiber	2
	Total Misc. Workforce	6

Construction Activity:

American Electrical: Continue to install panels inside of the electrical room.

G&H: Continuing to place line set connections to the new attic mechanical units, installing condensate connections.

Central Ceilings: Placing ceiling grid in Chief's office and 2nd in command.

Dig It: Not on site.

Dandis: Not on site.

Lapan: Not on site.

Debrino: Not on site.

Barber: Installing Sheetrock on the ceiling of the outbuilding.

Clerk's remarks: Coordination of all subcontractors for cell ceilings: electrical, sprinkler, HVAC, security.

Site Visitors/Meetings: See above

Deliveries: none

Equipment Used: Empire: (2) Boom Lift 600s, Barber (2) Scissor Lift, Commercial: Lull 944E, Mini Bobcat
